

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1031 3190

सासाराम/दिनांक:- 30.06.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।


प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- SASCOM-1

1st Quarter from 13/04/2021 to 12/07/2021

1	Name of the Road	from Bhavanpura Canal to Govi		
2	Batch No.	RM/RO/SAS/19/0003		
3	Project ID	10301009010		
4	Total Length of Road (In Km)	1.4		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	0.8		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	13.2427		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.662135		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	
II	SHOULDERS AND EMBANKMENTS		10%	
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	
IV	SIGNAGE AND ROAD SAFETY		10%	
V	VEGETATION		5%	
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.662135

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

Date

(Signature)

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Road :- From Bhavanpura Canal to Govina

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGOR Y	Latitude	Longitude	Event
22/6/22	13:11:39	48	0.1	230	10.1	2300	2715	ROAD	25.1206	84.96868	Speed Breaker
22/6/22	13:12:14	48	0.1	250	30.3	2500	2915	G	25.11987	84.97878	Normal
22/6/22	13:12:14	48	0.1	300	30.3	3000	3415	G	25.1199	84.98838	Curve
22/6/22	13:12:14	48	0.1	250	30.3	2500	2915	G	25.12763	84.9882	Normal
22/6/22	13:12:49	48	0.1	270	20.2	2700	3115	G	25.13763	84.98652	Normal
22/6/22	13:13:0	48	0.1	290	30.3	2900	3315	G	25.147	84.9847	Normal
22/6/22	13:13:0	48	0.1	270	40.4	2700	3115	G	25.15608	84.9843	Normal
22/6/22	13:15:9	48	0.1	260	20.2	2600	3015	G	25.15923	84.98703	Normal
Average IRI							3065				

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 900$$

$$Y = 1315$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Executive Engineer
Rural Work's Department
Works Division-Sasaram-1

22/06/22

22/6/22

22/6/22

Name of Customer :	Narendra Kumar
Name of Work/ Road :	From Bhavanpura Canal to Gov
Lab Job number :	48
Date :	6/22/2022
Section No :	48


Test Date :	6/22/2022
Machine No :	391
Start S No :	375
Start E No :	382
Weather :	Normal
Start Location :	25.1206,84.966
End Location :	25.15923,84.96
Road Name :	From Bhavanpura Canal to Gov
Road Type :	(R) RURAL ROAD
Side :	Sasaram
Interval :	
UV Range :	1715 To 4000 mm/km
Dist Range :	0 To 1028 m
Equation :	$Y = 0 * X^2 + 1.000 * X + 415.2$

Print Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\BRRDA34\Desktop\pump machine\22.06.22\2061443.Xls. Section No.: 48. Eqn: $Y = 0 * X^2 + 1.000 * X + 415.2$
Name of Customer: Narendra Kumar, Name of Work/ Road: From Bhavanpura Canal to Govina, Lab Job number

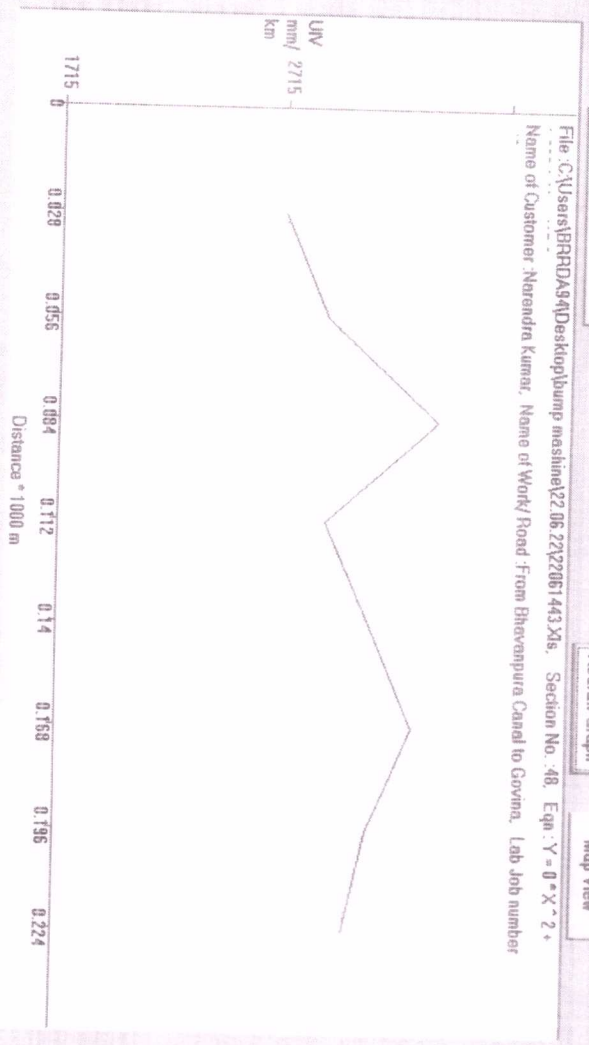

For 22/6/22

22/06/22

22/6/22
