

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक-1495 अरु / नरकटियागंज, दिनांक-04/8/22

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह— सचिव नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:-

MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maint. Policy-2018) योजना
अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर इस पत्र में
संलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु०:- 1. उपयोगिता प्रमाण-पत्र From GFR 19A

2. अधियाचना पत्र।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रा०का०वि०, का०प्र०, नरकटियागंज।

04/08/2022

FORM GFR 19-A
(See Government of India's decision (I) below rule- 150)
Form of Utilization certificate up to the month of Aug-2022
PIU:- E.E RWD(W)DIV-NARKATIAGANJ

SL.NO.	Name of Schemes	Sanction No.& Date with Amount (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5
1	Maintenance Fund of MR(3054) New Maintenance Policy- 2018		NIL	Certified that out of Rs. 0.00 Lacs of grants-in-aid sanctioned during the years 2022-23 in favour of Executive Engineer R. W. D. Works Division, Narkatiaganj a sum of Rs. 0.00 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL Lac remaining unutilized at the end of the period under report.
		TOTAL	NIL	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


SR..DIV ACCOUNTS OFFICER
R.W.D. Works Division, Narkatiaganj

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D. Works Division, Narkatiaganj

Requisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl No	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (in Laes)				Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	RM/WE/NAR/19/0005	KATHWALLA-MAHANKAUL	31808802087	3350 01-08-2019	4.640	171.532	117.524	41.55545	42/2020-21 03.03.2020	02-03-2021	02-03-2021	2.07777	2.07777	2.07777	0.00000	
2	RM/WE/NAR/19/0005	Mahaveer Chaur to Maluma via Pipra Nauranga	318891031900	3350 01-08-2019	1.950	86.250	62.344	17.50936	42/2020-21 03.03.2020	02-03-2021	25-03-2021	0.87547	0.87547	0.00000	0.00000	
3	RM/WE/NAR/19/0005	Kamunya Dhoti tola to Kamunya Daiti Basti	318891031901	3350 01-08-2019	2.300	105.217	76.364	20.70695	42/2020-21 03.03.2020	02-03-2021	23-06-2021	1.03535	0.00000	0.00000	0.00000	

Executive Engineer
Rural Works Department
Works Division Narkatiaganj

04/08/2021



Requisition Formet for Scheme Head-MR-(3054) Under Bihar Kurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division, Narkataganj

3rd Quarter

Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- KATHWALLA - MAHANKAUL

Length of Road :- 4.640 KM
Inspector :- A.E. RWD WORKS SUB DIVISION, CHANPATIA

To:-
Executive Engineer
RWD, Works Division Narkataganj
Position :- A.E.

Date:-

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment	m ²	NIL	NIL	NIL								No pothole found
OM101	Pothole Patching	m ³	NIL	NIL	NIL								No Surface Depression and Rut patching found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL	NIL								No crack Not required
OM103	Crack Sealing	Lm	NIL	NIL	NIL								No Loss of Aggregate (Surface ravelling) found
OM104	Surface Treatment	m ²	NIL	NIL	NIL								No bleeding / furnishing found
	(a) Loss of Aggregate (Surface Ravelling)	m ²	NIL	NIL	NIL								No bleeding / furnishing found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL								No Crocodile cracking found
	(c) Crocodile Cracking	m ²	NIL	NIL	NIL								Notified & repaired
OM105	Edge Repair	m ²	N.A.	N.A.	N.A.								
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.								
OM200	Other activities												No Edge Drop off found
	Shoulder												No Roughness, Scouring or Potholes found
	Unsealed Shoulder	Lm	NIL	NIL	NIL								No Holding Water Found
	(a) Edge Drop-off	Lm	NIL	NIL	NIL								Notified & repaired
OM201	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL								
	(c) Holding water	m ³	NIL	NIL	NIL								
	Embankment Repair	m ³	N.A.	N.A.	N.A.								NA
OM202	Other activities (Rain Cuts)												DONE
OM300	Drainage including culverts major	Lm	N.A.	N.A.	N.A.								DONE
OM301	Surface Drains & Verge	No	NIL	NIL	NIL								DONE
OM302	Culvert Cleaning	m ³	NIL	NIL	NIL								Not required
OM303	Culvert and pit Repair	m ³	NIL	NIL	NIL								
	Other activities (Whitewashing)	m ²	NIL	NIL	NIL								

19/07/25 9m/min

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												Done
OM401	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL								Done
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	NIL	NIL	NIL								Done
OM402	Tree and Shrub Management	No	NIL	NIL	NIL								Done
	Cutting Of Branches Of Trees	No	NIL	NIL	NIL								Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL								Done
	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL								Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	NIL	NIL	NIL								N.A.
OM502	Guard Stones	Lm	NA	NA	NA								N.A.
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Marking	M ²	NIL	NIL	NIL								
	Other activities												

Contractor

J.E

A.E

Executive Engineer
Rural works Department
Works Division, Narkataganj

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Narkatiaganj

3rd Quarter

1	Name of the Road	KATHWALIA - MAHANKAUL		
2	Batch No.	RM/WE/NAR/19/0005		
3	Project ID	31808802087		
4	Total Lenth of Road (in KM)	4.640		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	4.640		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	41.55545		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.0777725		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				2.0777725

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

[Signature]

Date

[Signature]

Signature of person inspecting road

[Signature]
Name and Designation of person inspecting road

(Signature)

Certify by E/I [Signature] Date:-

Executive Engineer
Rural Works Department
Works Division, Narkatiaganj

Name of Road - KATHWALIA - MAHANKAUL [Sec-76]

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
21/4/22	10:56:21	76	0.1	290	20.2	2900	2915	G	26.901472	84.526497	Normal
21/4/22	10:57:0	76	0.1	300	10.1	3000	3023	G	26.901303	84.527473	Normal
21/4/22	10:57:0	76	0.1	300	10.1	3000	3025	G	26.901128	84.52847	Normal
21/4/22	10:57:33	76	0.1	310	20.2	3100	3154	G	26.900982	84.529427	Normal
21/4/22	10:57:33	76	0.1	260	20.2	2600	2658	G	26.900825	84.530387	Normal
21/4/22	10:58:8	76	0.1	320	20.2	3200	3203	G	26.900577	84.531328	Normal
21/4/22	10:58:8	76	0.1	270	20.2	2700	2740	G	26.90037	84.532305	Normal
21/4/22	10:58:8	76	0.1	310	20.2	3100	3100	G	26.90015	84.533265	Normal
21/4/22	10:58:43	76	0.1	320	20.2	3200	3200	G	26.899905	84.534242	Normal
21/4/22	10:59:0	76	0.1	320	20.2	3200	3217	G	26.899793	84.535235	Normal
21/4/22	10:59:0	76	0.1	340	20.2	3400	3460	G	26.899663	84.536228	Normal
21/4/22	10:59:19	76	0.1	300	20.2	3000	3052	G	26.899523	84.537238	Normal
21/4/22	10:59:19	76	0.1	330	20.2	3300	3358	G	26.899397	84.538163	Normal
21/4/22	10:59:19	76	0.1	370	20.2	3700	3745	G	26.899223	84.539208	Normal
21/4/22	11:0:0	76	0.1	380	20.2	3800	3848	G	26.89903	84.54012	Normal
21/4/22	11:0:0	76	0.1	320	20.2	3200	3235	G	26.898762	84.54111	Normal
21/4/22	11:0:0	76	0.1	310	20.2	3100	3154	G	26.898485	84.54202	Normal
21/4/22	11:0:29	76	0.1	390	20.2	3900	3950	G	26.89821	84.542928	Normal
21/4/22	11:0:29	76	0.1	380	20.2	3800	3869	G	26.89791	84.543888	Normal
21/4/22	11:0:29	76	0.1	350	20.2	3500	3541	G	26.897622	84.544797	Normal
21/4/22	11:1:5	76	0.1	330	10.1	3300	3358	G	26.897318	84.545823	Normal
21/4/22	11:1:5	76	0.1	290	10.1	2900	2992	G	26.89705	84.54672	Normal
21/4/22	11:1:5	76	0.1	310	10.1	3100	3152	G	26.89678	84.547677	Normal
21/4/22	11:1:5	76	0.1	350	20.2	3500	3541	G	26.896482	84.548635	Normal
21/4/22	11:1:40	76	0.1	290	20.2	2900	2929	G	26.896232	84.549562	Normal
21/4/22	11:1:40	76	0.1	320	20.2	3200	3235	G	26.895958	84.550505	Normal

MSK 4.8.22
JE

Office
Call

MP

Name of Road - KATHIWALLA - MAHANKAUL [Sec-76]

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
21/4/22	11:2:0	76	0.1	300	20.2	3000	3031	G	26.895653	84.55148	Normal
21/4/22	11:2:0	76	0.1	310	20.2	3100	3133	G	26.895307	84.552407	Normal
21/4/22	11:2:15	76	0.1	330	20.2	3300	3337	G	26.89491	84.553	Normal
21/4/22	11:2:15	76	0.1	360	20.2	3600	3643	G	26.894538	84.554157	Normal
21/4/22	11:2:15	76	0.1	380	20.2	3800	3848	G	26.894123	84.5551	Normal
21/4/22	11:2:50	76	0.1	260	10.1	2600	2622	G	26.89374	84.555925	Normal
21/4/22	11:3:0	76	0.1	370	26.2	3750	3796	G	26.893338	84.5568	Normal
21/4/22	11:3:0	76	0.1	370	20.2	3700	3745	G	26.892932	84.55771	Normal
21/4/22	11:3:0	76	0.1	300	10.1	3000	3052	G	26.892525	84.558618	Culvert
21/4/22	11:3:26	76	0.1	350	20.2	3500	3541	G	26.892105	84.559545	Normal
21/4/22	11:3:26	76	0.1	340	30.3	3400	3439	G	26.891735	84.560353	Normal
21/4/22	11:4:1	76	0.1	310	30.3	3100	3133	G	26.891345	84.561278	Normal
21/4/22	11:4:1	76	0.1	320	20.2	3200	3256	G	26.89098	84.562153	Normal
21/4/22	11:4:1	76	0.1	340	10.1	3400	3445	G	26.890545	84.56313	Normal
21/4/22	11:4:1	76	0.1	340	10.1	3400	3481	G	26.890145	84.563988	Normal
21/4/22	11:4:36	76	0.1	320	10.1	3200	3262	G	26.88976	84.564915	Normal
21/4/22	11:4:36	76	0.1	360	10.1	3600	3643	G	26.889345	84.565773	Normal
21/4/22	11:5:0	76	0.1	300	10.1	3000	3031	G	26.888937	84.566598	Normal
21/4/22	11:5:12	76	0.1	370	10.1	3700	3766	G	26.888522	84.567508	Normal
21/4/22	11:5:12	76	0.1	380	20.2	3800	3869	G	26.88809	84.56838	Normal
21/4/22	11:5:12	76	0.04	340	20.2	3400	3460	G	26.887695	84.569208	Normal

Average IRI Value=3323

MS/4.8.22
S.E

04/08/22
A.E

Executive Engineer
Rural Works Department
Works Division, Narhatyagarh
04/08/22

Name of Customer: VIKASH KUMAR PANDEY
 Name of Work/Road: KATHWALLA - MAHANKAUL
 Lab Job number: 21-Apr-22
 Date: 21-Apr-22
 Section No. 76

Test Date: 21-Apr-22 Road Name: KATHWALLA - MAHANKAUL
 Machine No: (R) RURAL ROAD
 Start S No: 1622 Side: Interval
 Start E No: 5000
 Weather: 1000 mm/hm
 Start Location: 0 To 48 01 = 1000 m
 End Location: Equation: $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$


Print Generate Report and Graph

Redraw Graph

Map View

File F:\121841406 Xa. Section No. 76. Egn: $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer: VIKASH KUMAR PANDEY Name of Work/Road: KATHWALLA - MAHANKAUL Lab Job number

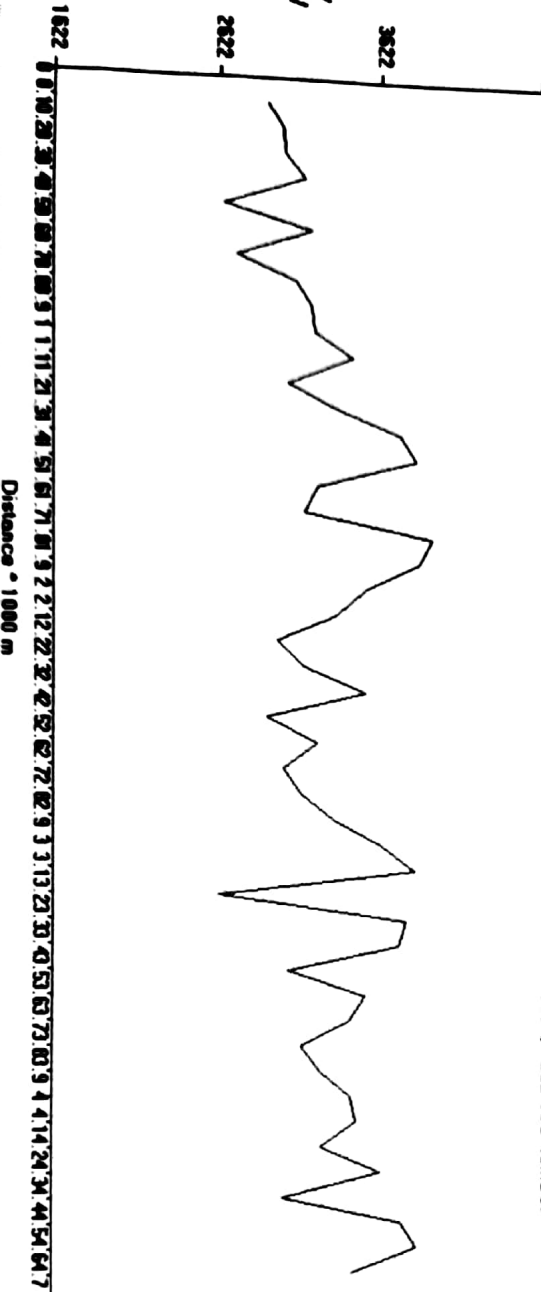

MSB 4-8-22

Dr. P. K. Singh

Executive Engineer
 Rural Works Department
 Works Division, Narkatiyaganj
