

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सिमरी बख्तियारपुर।

पत्रांक— 2537 अ/प्र

दिनांक— 24/11/2022

प्रेषक:—

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सिमरी बख्तियारपुर।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:—


नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं 2021-22 में व्यय हेतु
अनुरक्षण मद में आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं
2021-22 में व्यय हेतु अनुरक्षण मद में संलग्न विवरणी के अनुसार रुपये 12,74,871.00 (बारह लाख
चौहत्तर हजार आठ सौ एकहत्तर रुपये) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि किये
गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:— यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, सिमरी बख्तियारपुर।

24/11/22

Maintenance Requisition for Scheme Head MR(3054) Under Bihar Rural Road Maintenance Policy- 2018
Name of Work Division:- Siarti Bakhityarpur

Road Details										A. A. Details		Agreement Details					Actual Maintenance Expenditure					Length as Per Bump Report 1st Year	IRI As per Bump Report	Current Demand for Maintenance Amount (in Lac)						Remarks
Sl. No.	Road Name	Batch No	Project ID	Actual Date of Completion	Main wok Amount	Maintenance Amount	Main Work Amount	Maintenance of Agreement Amount 1st Year	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maint. Amount	Legenth	1st Year Maint. Exp.	2nd Year Maint. Exp.	3rd Year Maint. Exp.	4th Year Maint. Exp.	5th Year Maint. Exp.	Total Maint. Exp.	1st Quarter			2nd Quarter	3rd Quarter	4th Quarter	5th Quarter	6th Quarter	Total	
1	Anoja - Durgapur	RM/SA/SIM /19/0011	20904302013	30/05/2021	116.73000	60.25000	116.65300	11.83341	11.83341	11.83341	11.83341	11.83341	59.16705	6.125	0	0	0	0	0	0	0	2.95835	2.95835					5.91670		
2	Barsani - Laxmipur masahari	RM/SA/SIM /19/0011	20904302020	12/04/2021	52.55000	27.93000	52.53800	5.56372	5.56372	5.56372	5.56372	5.56372	27.81860	2.827	0	0	0	0	0	0	0	1.39093	1.39093					2.78186		
3	Gareeri Tola Road Nowati	RM/SA/SIM /19/0011	20904302036	10/12/2020	54.03000	28.35000	54.94700	5.40021	5.40021	5.40021	5.40021	5.40021	27.00105	2.766	0	0	0	0	0	0	0	1.35005	1.35005	1.35005				4.05015		
12.7.4871																														


 Executive Engineer
 RWD Work Division
 Siarti Bakhityarpur

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD, Simri Bakhtiyarpur 2nd Quarter (11-03-2021 to 10-06-2021)

1	Name of the Road	Gareebi tola Road Nonati
2	Batch No / Package no	Rm/SA/sim/19/0011
3	Project ID	20904302036
4	Total Length of Road (in Km)	2.766
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	2.766
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	27.00105 Lakh
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.35005 Lakh

Compliance criteria	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANKMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.35005

Bhagat K. Singh
Date of inspection by E / I his agent prepared by
Contractor's self Control unit

RAM KUMAR,
Name and Designation of person inspecting
road

[Signature]
08/11/22
Signature of person inspecting road

[Signature]
23/11/22
Certify by E / I [signature] Date:-

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD Simri Bakhtiyarpur 1st Quarter (11-12-2020 to 10-03-2021)

1	Name of the Road	Chareem' tola Road Nonati		
2	Batch No / Package no	RM/SA/Sim/15/0011		
3	Project ID	20904302036		
4	Total Length of Road (in Km)	2.766		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	2.766		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Sechedule [Agreement Amount for Maintenance] (in Lakh)	27.00105 Lakh		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as par Schedule (in Lakh) [2]	1.35005 Lakh		
Compliance ceriteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non - Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGATATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.35005

Prigay K. Singh
Date of inspection by E / I his agent prepared by Contractor's self Control unit

RAM KUMAR
Name and Designation of person inspecting road

[Signature]
08/11/2022
Signature of person innspecting road

[Signature]
23/11/2022
Certify by E / I [signature] Date:-

STANDARD FORMAT FOR QUARTERLY STATEMENT

PIU NAME- RWD Simri Bakhtiyar Pur 3rd Quarter (11-06-2021 to 10-09-2021)

1	Name of the Road	Ghareeri to a Road Nonati		
2	Batch No / Package no	Rm/SA/sim/19/0011		
3	Project ID	20904302036		
4	Total Length of Road (in Km)	2.766		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	2.766		
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20		
7	Ordinary Maintenance Cost as per Sehedule [Agreement Amount for Maintenance] (in Lakh)	27.00105 Lakh		
8	Quaqrterly Payment :1/20 of Ordinary Mainternance Cost as par Schedule (in Lakh) [2]	1.35005 Lakh		
Compliance ceriteria	Standard job Deserption	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non - Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.35005

RAM KUMAR.

Name and Designation of person inspecting road

Bigay K. Singh
Date of inpection by E / I his agent prepared by Contractor's self Control unit

[Signature]
08/11/22
Signature of person inspecting road

[Signature]
25/11/22
Certify by E / I [signature] Date:-

Government of Bihar
OM01
Rural Works Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Date:

Road From: Chamezi to Road Monahi
Length of Road: 2.766 km
Period: 1st Quarter (11-12-2020 to 10-03-2021)
Inspector: J.E., RWD, Sub Division Sonbhadra

To: **EXECUTIVE ENGINEER,**
RWD, Works Division, Simri Bakhtiyarpur
Position: J.E.

No.	Name	Work	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement	Units											
OM101	Pothole Patching	m2	Nil	Nil	Nil								No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil								No Surface Depression and Rut Patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil								No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate	m2	Nil	Nil	Nil								No Loss of Aggregate (Surface
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil								No Bleeding/Flushing required.
	(c) Crocodile Cracking	m2	Nil	Nil	Nil								No Crocodile cracking found.
OM105	Edge Repair	m2	Nil	Nil	Nil								No Edge Repair required.
OM106	Digouts	m2	N.A	N.A	N.A								
OM107	Concrete Pavement	m3	N.A	N.A	N.A								
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
	(a) Edge Drop-Off	Lm	Nil	Nil	Nil								No Edge Drop-Off required.
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil								No Roughness, Scouring or Potholes required
	(c) Holding water	Lm	Nil	Nil	Nil								No Holding Water Found.
OM202	Embankment Repair	m3	Nil	Nil	Nil								No Embankment Repair required.
	Other activities												
OM300	Drainage including culverts major and minor br												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A								
OM302	Culvert Cleaning	No.	Nil	Nil	Nil								Not required.
OM303	Culvert and Pit Repair	m3	Nil	Nil	Nil								Not required.
	Other activities	m2	Nil	Nil	Nil								Not required.

Bidder

08/11/2022

08/11/22

08/11/22

Standard work item		Work	Units of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
	Grass Control												Not required
OM401	a) Roadside - General Tidy	Ha	Nil	Nil	Nil								Not required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil								
	Tree and Shrub Management												
	Cutting Tree	No	Nil	Nil	Nil								
OM402	Cutting Shrubs	No	Nil	Nil	Nil								Not required
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not required
OM502	Guard stones	Lm	N.A	N.A	N.A								Not required
OM503	Distance stones	No	N.A	N.A	N.A								Not required
OM504	Road markings	m2	Nil	Nil	Nil								Not required
	Other activities												
Signature of Contractor/ Authorized representative													
Date													
Time													
Place													

Signature of Contractor Authorized representative

Date

Time

Place

Signature
08/11/22

Signature
08/11/22
A.E.

Government of Bihar
OM01
Rural Works Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Road From: Chamreoni tola Road Novathi
Length of Road : 2.766
Period: 2nd Quarter (11-03-2021 to 10-06-2021)
Inspector : J.E., RWD, Sub Division Samburda

To :
EXECUTIVE ENGINEER,
RWD, Works Division, Simri Bakhtiyarpur

Date:

No.	Standard work item Name	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												No Pothole found.
OM101	Pothole Patching	m2	Nil	Nil	Nil								No Surface Depression and Rut Patching found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil								No Crack Sealing found
OM 103	Crack Sealing	Lm	Nil	Nil	Nil								
OM104	Surface Treatment												No Loss of Aggregate (Surface
	(a) Loss of Aggregate	m2	Nil	Nil	Nil								No Bleeding/Flushing required.
	(b) Bleeding/ Flushing	m2	Nil	Nil	Nil								No Crocodile cracking found.
	(c) Crocodile Cracking	m2	Nil	Nil	Nil								No Edge Repair required.
OM105	Edge Repair	m2	Nil	Nil	Nil								
OM106	Digouts	m2	N/A	N/A	N/A								
OM107	Concrete Pavement	m3	N/A	N/A	N/A								
	Other activities												
OM200 Shoulder													
	Unsealed Shoulder												
OM201	(a) Edge Drop-Off	Lm	Nil	Nil	Nil								No Edge Drop-Off required.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil								No Roughness, Scouring or Potholes required
	(c) Holding water	Lm	Nil	Nil	Nil								No Holding Water Found.
OM202	Embankment Repair	m3	Nil	Nil	Nil								No Embankment Repair required.
	Other activities												
OM 300 Drainage including culverts major and minor br													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A								Not required.
OM302	Culvert Cleaning	No.	Nil	Nil	Nil								Not required.
OM303	Culvert and Pit Repair	m3	Nil	Nil	Nil								Not required.
	Other activities	m2	Nil	Nil	Nil								

Bidder Bidder Kar Singh 28/11/2021 08/11/21
Executive Engineer, Work Division

Standard work item		Work Units	Units of work required in each kilometre										Comments
No.	Name		1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
	Grass Control												Not required
OM401	a) Roadside - General Tidy	Ha	Nil	Nil	Nil								Not required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil								Not required
	Tree and Shrub Management												Not required
OM402	Cutting Tree	No	Nil	Nil	Nil								Not required
	Cutting Shrubs	No	Nil	Nil	Nil								Not required
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not required
OM502	Guard stones	Lm	N/A	N/A	N/A								Not required
OM503	Distance stones	No	N/A	N/A	N/A								Not required
OM504	Road markings	m2	Nil	Nil	Nil								Not required
	Other activities												

Signature of Contractor/ Authorized representative

Date

Time

Place

Signature
08/11/2022

Signature
08/11/22
A.E.

Government of Bihar
OM01
Rural Works Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Road From: *Garraeai tola Road Mowati*
Length of Road: *2.766 km*
Period: *3rd Quarter (1-06-2021 to 10-09-2021)*
Inspector: *J.E. RWD, Sub Division Sonbarhi*

To: **EXECUTIVE ENGINEER,**
RWD, Works Division, Simri Bakhtiyarpur
Position: *J.E.*

Date:

No.	Name	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil								No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil								No Surface Depression and Rut Patching found.
OM 103	Crack Sealing	Lm	Nil	Nil	Nil								No Crack Sealing found
OM104	Surface Treatment												No Loss of Aggregate (Surface)
	(a) Loss of Aggregate	m2	Nil	Nil	Nil								No Bleeding/Flushing required.
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil								No Crocodile cracking found.
OM105	(c) Crocodile Cracking	m2	Nil	Nil	Nil								No Edge Repair required.
OM106	Edge Repair	m2											
OM107	Digouts	m2	N.A	N.A	N.A								
OM107	Concrete Pavement	m3	N.A	N.A	N.A								
Other activities													
OM200 Shoulder													
Unsealed Shoulder													
OM201	(a) Edge Drop-Off	Lm	Nil	Nil	Nil								No Edge Drop-Off required.
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil								No Roughness, Scouring or Potholes required
	(c) Holding water	Lm	Nil	Nil	Nil								No Holding Water Found.
OM202	Embankment Repair	m3	Nil	Nil	Nil								No Embankment Repair required.
Other activities													
OM 300 Drainage including culverts major and minor br													
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A								Not required.
OM302	Culvert Cleaning	No.	Nil	Nil	Nil								Not required.
OM303	Culvert and Pit Repair	m3	Nil	Nil	Nil								Not required.
Other activities													
		m2	Nil	Nil	Nil								

Executive Engineer, Work Division

Bllder

Standard work item		Work	Units of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation													
OM401	Grass Control												Not required
	a) Roadside - General Tidy	Ha	Nil	Nil	Nil								Not required
	b) Clear near safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil								
	Tree and Shrub Management												Not required
	Cutting Tree	No	Nil	Nil	Nil								Not required
OM402	Cutting Shrubs	No	Nil	Nil	Nil								Not required
	Other activities												
OM500 Safety Signage and Road													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not required
OM502	Guard stones	Lm	N.A	N.A	N.A								Not required
OM503	Distance stones	No	N.A	N.A	N.A								Not required
OM504	Road markings	m2	Nil	Nil	Nil								Not required
	Other activities												

Signature of Contractor/ Authorized representative

2024/10/01

2024/10/01

Date

Time

Place

Signature of Contractor/ Authorized representative

Date

Time

Place

Signature
08/11/2022

Signature
08/11/22
A.E.

Name of work : Gareen Tola Road - Nonali
Name of customer : Ms Bijay Kumar Singh

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMPI/cm	Speed(Km/Hr)	U/(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
14/08/22	15:00:07	33	100	100	14.0 cm	4.7 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7328749	N	86.7528315	E	Normal
14/08/22	15:00:24	33	100	200	17.0 cm	22.5 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7328749	N	86.7528315	E	Normal
14/08/22	15:00:38	33	100	300	13.0 cm	23.4 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.7328749	N	86.7528315	E	Normal
14/08/22	15:00:50	33	100	400	14.0 cm	30.0 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7328599	N	86.8010111	E	Breaker
14/08/22	15:01:03	33	100	500	12.0 cm	29.0 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:01:23	33	100	600	17.0 cm	18.0 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:01:40	33	100	700	10.0 cm	20.4 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:01:52	33	100	800	12.0 cm	30.0 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7328599	N	86.8010111	E	Correl
14/08/22	15:02:04	33	100	900	18.0 cm	30.0 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:02:15	33	100	1000	15.0 cm	31.5 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7328599	N	86.8010111	E	Breaker
14/08/22	15:02:28	33	100	1100	11.0 cm	28.2 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:02:41	33	100	1200	15.0 cm	31.5 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:02:53	33	100	1300	17.0 cm	28.5 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7328599	N	86.8010111	E	Core
14/08/22	15:03:04	33	100	1400	22.0 cm	29.8 Km/Hr	2200.0 mm/Km	2143	2.98	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:03:17	33	100	1500	11.0 cm	30.6 Km/Hr	1100.0 mm/Km	1116	1.67	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:03:29	33	100	1600	10.0 cm	28.2 Km/Hr	1000.0 mm/Km	1022	1.54	Good	25.7328599	N	86.8010111	E	Breaker
14/08/22	15:03:41	33	100	1700	15.0 cm	32.0 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:03:54	33	100	1800	14.0 cm	28.8 Km/Hr	1400.0 mm/Km	1396	2.03	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:04:13	33	100	1900	13.0 cm	27.6 Km/Hr	1300.0 mm/Km	1303	1.91	Good	25.7328599	N	86.8010111	E	Correl
14/08/22	15:04:28	33	100	2000	15.0 cm	19.6 Km/Hr	1500.0 mm/Km	1489	2.16	Good	25.7328599	N	86.8010111	E	Normal
14/08/22	15:04:43	33	100	2100	12.0 cm	23.1 Km/Hr	1200.0 mm/Km	1209	1.79	Good	25.7328599	N	86.8010111	E	Normal

08/11/2022
A.E.

08/11/23
A.E.


08/11/23
A.E.

Name of work		: Gareeri Tola Road - Nonali													
Name of customer		: Ms Bijay Kumar Singh													
(R)Rural Road															
Good		Average		Poor											
< 4000		4001 - 5000		> 5000											
14/08/22	15/04/55	33	100	2200	16.0 cm	14.4 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7232599	N	86.8010111	E	Brekar
14/08/22	15/05/25	33	100	2300	20.0 cm	12.0 Km/Hr	2000.0 mm/Km	1956	2.75	Good	25.7232599	N	86.8010111	E	Normal
14/08/22	15/05/49	33	100	2400	17.0 cm	14.8 Km/Hr	1700.0 mm/Km	1676	2.4	Good	25.7141008	N	86.7899408	E	Normal
14/08/22	15/06/28	33	100	2500	18.0 cm	9.1 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7140188	N	86.7905283	E	Normal
14/08/22	15/06/52	33	100	2600	16.0 cm	14.4 Km/Hr	1600.0 mm/Km	1583	2.28	Good	25.7140188	N	86.7905283	E	Normal
14/08/22	15/07/10	33	100	2700	18.0 cm	20.0 Km/Hr	1800.0 mm/Km	1770	2.51	Good	25.7140188	N	86.7905283	E	Normal


 08/11/2022
 P.E.


 08/11/22
 P.E.

NTGraph ActiveX Control
ner: Bijay kumar Singh , Machine no: 19215 , Road: Gareeri tola to Nanoati , Date: 07/09/22 , Section No: 33 , Equation: $Y=0.93^x$

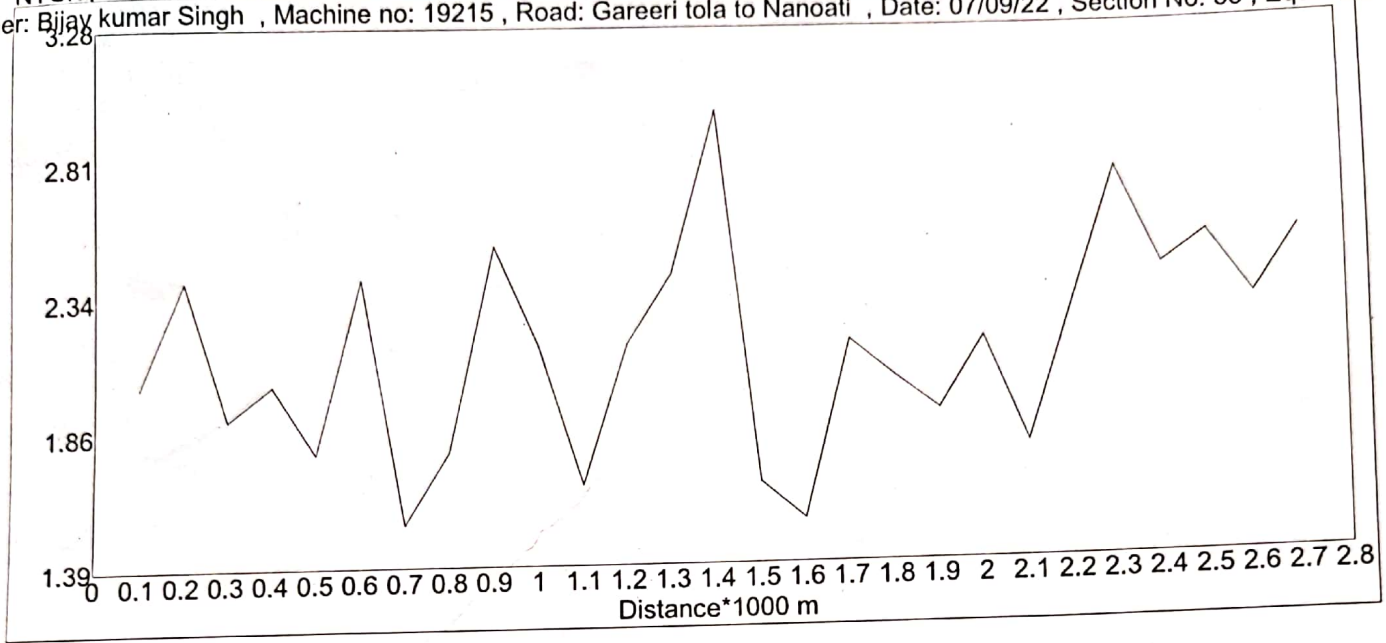

[Signature]
08/11/2022
JE

[Signature]
08/11/22
A.E.

[Signature]
23/11/22
BE
