

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना ।

पत्रांक 118 अड्डे

दिनांक 23/01/22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बी.आर.आर.डी.ए.,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-MR(3054) under Bihar Rural Road Maintenance
Policy-2018 योजना अन्तर्गत पथों का आवंटन का अध्याचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि शीर्ष-MR(3054) under Bihar
Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का आवंटन का
अध्याचना का मांग विहित-प्रपत्र में तैयार कर अध्याचना हेतु भेजी जा रही है। उक्त पथ
का कराये गये कार्य को कनीय अभियंता द्वारा विशिष्टियों के अनुरूप किया जा चुका है।

अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा
की जाये ताकि संवेदक का भुगतान किया जा सके।

अनु० :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Patna

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	3	NH-30 - CHAMPAPUR	10100102176	3024 dated 16.07.2019	1.75000	59.59370	35.94100	13.03039	38/MBD/2020-2021	14.11.2021	--	3135722	25 mm	5%	0.00000	0.00000	35.85100	Surface Work Complete
2	3	NH-30 BAHPUR - MAJHAULI	10100102183	3024 dated 16.07.2019	2.45000	85.81400	48.05900	21.81913	38/MBD/2020-2021	14.11.2021	--	353164	25 mm	5%	0.00000	0.00000	47.95900	Surface Work Complete
Total																	83.81000	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-Date Physical Progress has been uploaded in MIS.


 Executive Engineer
 RWD Works Division, Patna
 23/01/22
 23/01/22

Name of The Road : NH 30 Champapur

Length : 1.750

Package No. : MR-N/2019-2020/PATNA/03

Division : Patna

Block : Bakhtiyarpur

Contractor Name : M/S Vinod Kumar Mishra

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				$Y = 0 * X^2 + 0.936 * X + 278.4$		
23/1/22	12 28 0	101	0.1	370	0	3700	3741	G	25.45612	85.50098	Normal			
23/1/22	12 28 7	101	0.1	230	20.2	2300	2431	G	25.457037	85.501091	Speed Breaker	X= 3400		
23/1/22	12 28 42	101	0.1	170	10.1	1700	1869	G	25.457927	85.501319	Curve	Y= 3460		
23/1/22	12 29 17	101	0.1	340	30.3	3400	3460	G	25.458835	85.501514	Normal			
23/1/22	12 29 17	101	0.1	380	30.3	3800	3835	G	25.459764	85.50186	Normal	(R)RURAL ROAD		
23/1/22	12 29 48	101	0.1	340	30.3	3400	3460	G	25.460602	85.502138	Normal	Good	Average	Poor
23/1/22	12 30 0	101	0.1	380	30.3	3800	3835	G	25.461517	85.502486	Normal	<4000	4001-5000	>5001
23/1/22	12 30 28	101	0.1	380	10.1	3800	3835	G	25.462377	85.502726	Curve			
23/1/22	12 31 3	101	0.1	330	30.3	3300	3367	G	25.463298	85.502752	Normal			
23/1/22	12 31 3	101	0.1	380	30.3	3800	3835	G	25.464111	85.502828	Normal			
23/1/22	12 31 14	101	0.1	290	20.2	2900	2992	G	25.464821	85.503038	Speed Breaker			
23/1/22	12 31 38	101	0.1	280	10.1	3256	3326	G	25.465725	85.503388	Curve			
23/1/22	12 32 0	101	0.1	330	10.1	3300	3367	G	25.466592	85.503394	Normal			
23/1/22	12 32 13	101	0.1	230	30.3	2300	2431	G	25.467376	85.503487	Normal			
23/1/22	12 37 31	101	0.1	190	20.2	1900	2056	G	25.467998	85.503477	Speed Breaker			
23/1/22	12 38 6	101	0.1	160	30.3	1600	1776	G	25.468956	85.503319	Normal			
23/1/22	12 38 6	101	0.1	330	30.2	3300	3367	G	25.469828	85.502933	Normal			
23/1/22	12 39 10	101	0.05	340	10.1	3400	3460	G	25.470649	85.503153	Speed Breaker			
	Total		1.75	5450	383.7	54956	56443		458.343533	1539.04588				
	Average					3053.111	3135.722							

Sun
23.01.22
IT Manager

Joseph
23.01.22
J.E.

Ang
23.01.22
AE

Ang
23.1.22

Name of Customer : M/S Vinod Kumar Mishra
 Name of Work/ Road : NH 30 Champapur
 Lab Job number :
 Date : 23/01/2022
 Section No : 101

Test Date :	23/01/2022	Road Name :	NH 30 Champapur
Machine No :	374	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UV Range :	776 To 5000 1000 mm/km
Start Location :		Dist Range :	0 To 1.9 0.1 * 1000 m
End Location :		Equation :	$Y = 0 * X^2 + 0.936 * X + 278.4$

Print


Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BRRDA23\OneDrive\Desktop\14011322.Xls, Section No. : 101, Eqn : $Y = 0 * X^2 + 0.936 * X + 278.4$

Name of Customer : M/S Vinod Kumar Mishra, Name of Work/ Road : NH 30 Champapur, Lab Job number :

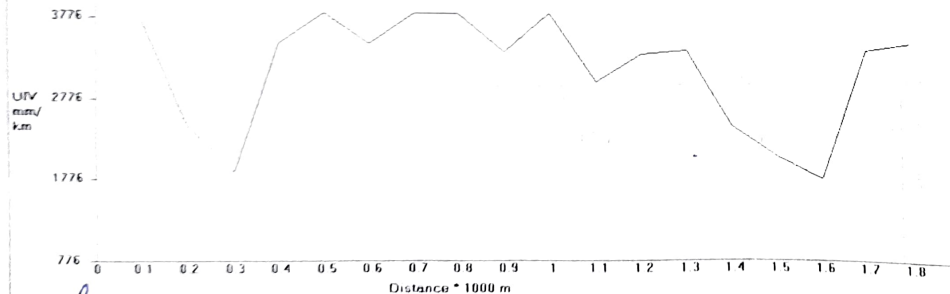

23.01.22
 PT Manager.

23.01.22
 J.E.

23.01.22
 J.E.
