

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1032 अगु०

सासाराम/दिनांक:- 30.6.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुस्करण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुस्क्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- Sasaram-1


2nd Quarter from-13/07/2022 to 12/10/2022

1	Name of the Road	G.T. Road to ghatmapur		
2	Batch No.	RM/RO/SAS/19/0003		
3	Project ID	10104531		
4	Total Length of Road (In Km)	0.8		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	0.8		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	7.49431		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.3747155		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)		60%	
II	SHOULDERS AND EMBANKMENTS		10%	
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%	
IV	SIGNAGE AND ROAD SAFETY		10%	
V	VEGETATION		5%	
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)			[6]	0.3747155

Date of inspection by E/I of his agent


Prepared by Contractor's self Control unit

Name and Designation of person inspection road


22/06/22


(Signature)

Date


22/06/22

Signature of person inspection road

Certify by E/I [signature] Date:-


22/06/22

Name of Road :- G.T road to ghatmapur

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGOR	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
22/6/22	14:6:43	50	0.1	250	30.3	2500	2915	G	24.953722	84.49982	Normal
22/6/22	14:7:0	50	0.1	240	20.2	2400	2815	G	24.952812	84.49797	Normal
22/6/22	14:7:18	50	0.1	280	20.2	2800	3215	G	24.951882	84.49595	Normal
22/6/22	14:7:18	50	0.1	300	20.2	3000	3415	G	24.95106	84.49377	Normal
22/6/22	14:7:53	50	0.1	290	20.2	2900	3315	G	24.95013	84.49292	Normal
22/6/22	14:8:0	50	0.1	280	10.1	2800	3215	G	24.949298	84.49192	Normal
22/6/22	14:8:28	50	0.1	300	10.1	3000	3415	G	24.948432	84.49377	Normal
22/6/22	14:9:4	50	0.1	310	20.2	3100	3515	G	24.947748	84.49628	Normal
Average IRI							3228				

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 900$$

$$Y = 1315$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

Executive Engineer

Rural Work's Department

Works Division-Sasaram-1

22/6/22

22/6/22

22/6/22

Name of Customer:	Neerda Kumar
Name of Work/ Road:	G.T road to ghatampur
Lab Job number:	50
Date:	6/22/2022
Section No.	50

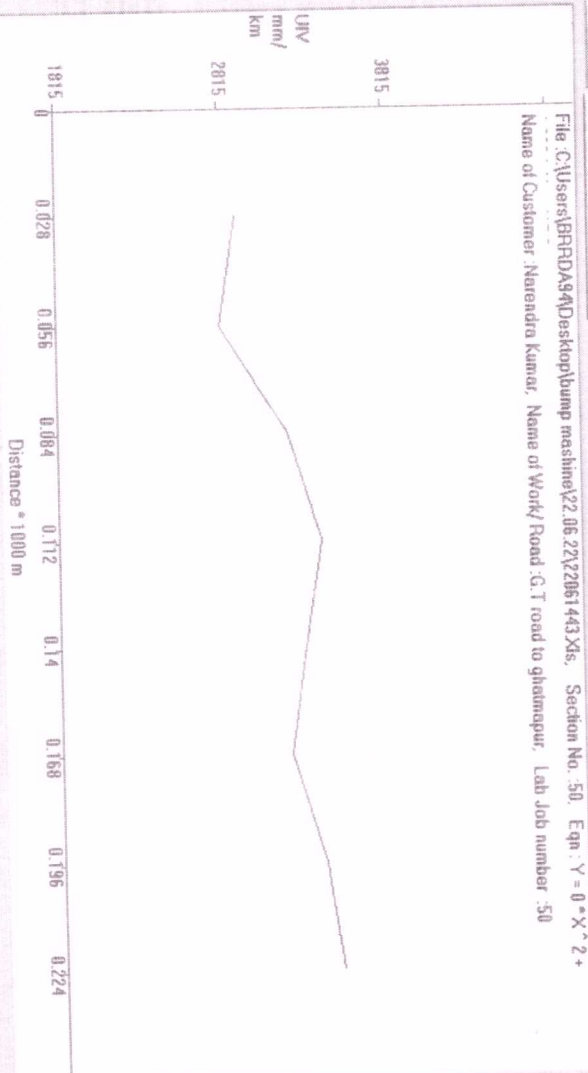
Test Date:	6/22/2022	Road Name:	G.T road to ghatampur
Machine No:	391	Road Type:	(R) RURAL ROAD
Start S. No.:	448	Site:	Sasaram
Start E. No.:	465	Interval:	
Weather:	Normal	UV Range:	1815 To 5000
Start Location:	24.953722 84.4	Dist Range:	0 To 10252
End Location:	24.94746 84.4	Equation:	$Y = 0 * X^2 + 1.000 * X + 0.152$

Print Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\BPRDAS\Desktop\pump machine\22.06.22\2061443.Xls. Section No. 50. Eqn: $Y = 0 * X^2 +$
 Name of Customer: Neerda Kumar, Name of Work/ Road: G.T road to ghatampur, Lab Job number: 50



6/22/2022

WQ
