

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, जमुई।

पत्रांक ७८७/२३

जमुई, दिनांक ३०.६.२०२२

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, जमुई।

सेवा में,

नोडल पदाधिकारी,
३०५४(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय—

शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत ५(पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में।


महाराज,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष MR New Maintenance Policy 2018
योजना अन्तर्गत ५(पाँच) वर्षीय अनुरक्षण के पथों का पथवार मांगी जाने वाली आवंटन की सूची पत्र के
साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु०— यथोक्त

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जमुई।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- R.W.D(WD), Jamui

Block Name:- Khaira

1	Name of the Road	L029 - Jamui-Kauwakol PWD road to Laldaiya-Bishanpur road (VR29)		
2	Batch No.	RM/JA/JAM/19/0015		
3	Project ID	20804102096		
4	Total Lenth of Road (in KM)	3.223		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	3.223		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	30.51355		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.52568		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGETATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.52568

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

(Signature)

Signature of person inspecting road

Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Jamui

Requisition Format for Scheme Head MR (354) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and Surface Renewal)

1 Year (1st Quarter)

RWD, Works Division Jamui

Government Of Bihar

OMD1

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From: (023) Jamui Kaurwadi PWD Road to Lakhaya Bishampur road (V829)
(Package No.-RM/JAM/19/0015)
Length of Road :- 3.22Km
Inspector :- J.E RWD Sub Division : Khaira

To:-

Executive Engineer
R.W.D, Works Division Jamui

Date:- 30.6.2022

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	○ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Dipouts	m ²	N/A	N/A	N/A	N/A							
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												
OM301	Surface Drains & Verges	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whitewashing)	M ²	Nil	Nil	Nil	Nil							Not Required

Wm
30/6/22

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Comments
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near, Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

Executive Engineer, R.W.D. Works Division-Jamui

Division, Jamui

und 3/1/12

Name of Work-1079 - Jamui-Kauwakiol PWD road to Laldiya-Bishanpur road (VR29)

Name of Contractor-Amrendra Kumar Atri Infrastructure Private Limited

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
16/6/22	10:30:0	22	0.1	340	0	3400	3156	G	24.8088	86.23092	Normal
16/6/22	10:30:6	22	0.1	360	10.1	3600	3322	G	24.807942	86.231413	Normal
16/6/22	10:31:44	22	0.1	340	10.1	3400	3156	G	24.807507	86.231632	Normal
16/6/22	10:35:2	22	0.1	380	10.1	3800	3487	G	24.801363	86.227912	Normal
16/6/22	10:35:37	22	0.1	330	20.2	3300	3073	G	24.801363	86.227912	Normal
16/6/22	10:36:4	22	0.1	370	10.1	3700	3405	G	24.800647	86.229225	Normal
16/6/22	10:36:40	22	0.1	350	10.1	3500	3239	G	24.80037	86.229998	Normal
16/6/22	10:37:0	22	0.1	320	10.1	3200	2991	G	24.79987	86.231397	Normal
16/6/22	10:37:25	22	0.1	380	30.3	3800	3487	G	24.79987	86.231397	Normal
16/6/22	10:37:25	22	0.1	310	30.3	3100	2908	G	24.79987	86.231397	Curve
16/6/22	10:37:25	22	0.1	340	30.3	3400	3156	G	24.79987	86.231397	Normal
16/6/22	10:37:25	22	0.1	320	40.4	3200	2991	G	24.79987	86.231397	Normal
16/6/22	10:38:0	22	0.1	220	30.3	2200	2163	G	24.79987	86.231397	Normal
16/6/22	10:38:0	22	0.1	390	40.4	3900	3570	G	24.79987	86.231397	Normal
16/6/22	10:38:0	22	0.1	220	40.4	2200	2163	G	24.79987	86.231397	Normal
16/6/22	10:38:36	22	0.1	330	30.3	3300	3073	G	24.79987	86.231397	Normal
16/6/22	10:38:36	22	0.1	370	40.4	3700	3405	G	24.79987	86.231397	Normal
16/6/22	10:38:36	22	0.1	370	40.4	3700	3405	G	24.79987	86.231397	Normal
16/6/22	10:38:36	22	0.1	360	30.3	3600	3322	G	24.79987	86.231397	Normal
16/6/22	10:38:36	22	0.1	360	30.3	3600	3322	G	24.79987	86.231397	Normal
16/6/22	10:39:11	22	0.1	310	20.2	3100	2908	G	24.79987	86.231397	Normal
16/6/22	10:39:11	22	0.1	350	10.1	3500	3239	G	24.79987	86.231397	Normal
16/6/22	10:39:46	22	0.1	300	30.3	3000	2825	G	24.79987	86.231397	Normal
16/6/22	10:39:46	22	0.1	310	20.2	3100	2908	G	24.79987	86.231397	Normal
16/6/22	10:39:46	22	0.1	310	20.2	3100	2908	G	24.79987	86.231397	Normal
16/6/22	10:40:21	22	0.1	360	20.2	3600	3322	G	24.786307	86.240605	Speed Breaker
16/6/22	10:40:21	22	0.1	300	10.1	3000	2825	G	24.78788	86.238518	Normal
16/6/22	10:41:1	22	0.1	340	20.2	3400	3156	G	24.787118	86.239545	Normal
16/6/22	10:41:1	22	0.1	300	10.1	3000	2825	G	24.78685	86.24	Normal
16/6/22	10:41:36	22	0.1	350	20.2	3500	3239	G	24.786307	86.240605	Normal
16/6/22	10:41:36	22	0.1	240	40.4	2400	2328	G	24.786307	86.240605	Normal
16/6/22	10:41:36	22	0.1	240	50.5	2400	2328	G	24.786307	86.240605	Normal
16/6/22	10:41:36	22	0.1	310	40.4	3100	2908	G	24.786307	86.240605	Normal
Length		22	3.2								
				Total IRI		97605					
				Average IRI		3050.156					

$$Y = 0 * X^2 + 0.828 * X + 341.6$$

$$X = 3100$$

$$Y = 2908$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001


Executive Engineer
 Rural Work Department
 Works Division -Jamui
 30/6/22

Name of Customer: Karnataka Kumar Ashwath
 Name of Work/ Road: bid to Laidya Bishnur Road
 Lab Job number: 16-06-2022
 Date: 16-06-2022
 Section No. 22

Test Date: 16-06-2022 Road Name: bid to Laidya Bishnur Road
 Machine No: 339 Road Type: (R) RUPAL ROAD
 Start S No: 0.000 Side: Internal
 Start E No: 1.200 U/V Range: 1113 To 5000 mm/km
 Weather: Dist Range: 0 To 13 01 * 1000 m
 Start Location: Elevation: Y=0.0 X=2.0 0.023 X=341.6
 End Location:

Road Generate Report and Graph Redraw Graph Map View

File: ASPT\Main policy offline Rappeta\Ashwath\VALU\Jan\Jhanda Ashwath\1651428.XL Section No. 22 Egn
 Name of Customer: Karnataka Kumar Ashwath Name of Work/ Road: Jhanda Ashwath PWD road to

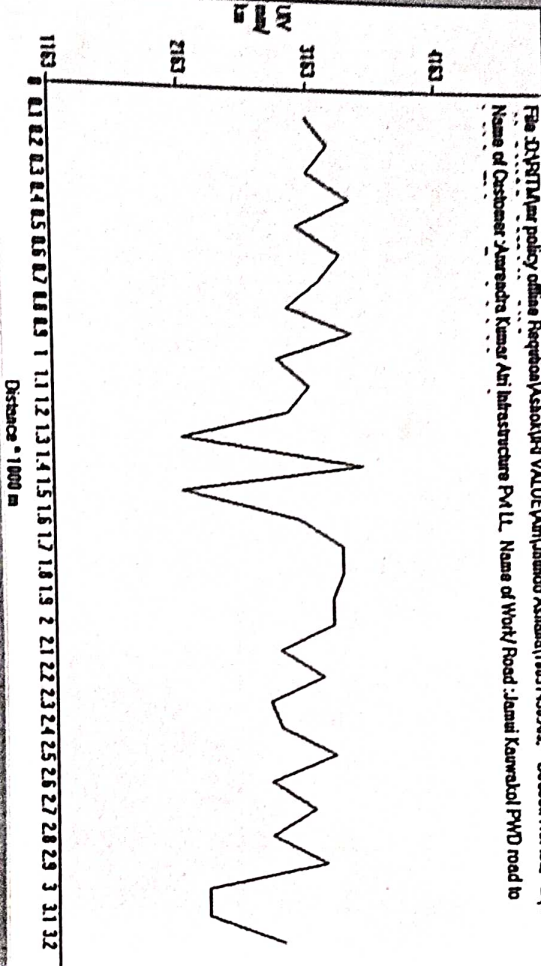

30/4/22
 30/4/22
