

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, जमुई ।

पत्रांक ...971/2022

जमुई, दिनांक 30.6.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, जमुई ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:-

शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में ।


महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष MR New Maintenance Policy 2018
योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण के पथों का पथवार मांगी जाने वाली आवंटन की सूची पत्र के
साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है ।

सूचनार्थ सादर समर्पित ।

अनु०- यथोक्त

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जमुई ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- R.W.D(WD), Jamui

Block Name:- Islamnagar Aliganj

1	Name of the Road	Construction of Road from Arha Chamartolee Chowk on Nawada-Sikandra PWD Road to Mathalwa village.		
2	Batch No.	RM/JA/JAM/19/0010		
3	Project ID	28411032593		
4	Total Lenth of Road (in KM)	2.34		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	2.34		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	22.25588		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.11279		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.11279


Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

(Signature)

Signature of person inspecting road


 Certify by E/I [signature] Date:-
 Executive Engineer
 Rural Works Department
 Works Division, Jamui

Requestion Formet for Scheme Head MR (3054) Under Bihar Rural Road Maintenance Policy-2012 (Rural Rectification and Surface Renewal)

1 Year (1st Quarter)

RWD, Works Division Jamtal
Government Of Bihar

OM401
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road from Const of road from Aha Chamar Tol chok on Newwala Standra PWD Road to Mahwa
Village

(Package No.-BM/JA/JAM/19/0010)

Length of Road :- 2.34km

Inspector :- JE RWD Sub Division :Jamnagar Algan

To:-

Executive Engineer
R.M.D, Works Division Jamtal

Date:- 23.6.2022

Position :- JE

No	Standard Or Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM4100	Sealed pavement	Lmt											
OM4101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found
OM4102	Surface Depression and Rut patching	m3	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM4103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM4104	(a) Loss of Aggregate (Surface Raveling)	m ³	Nil	Nil	Nil	Nil							No Loss Of Aggregate (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Deposits	m ²	N/A	N/A	N/A	N/A							
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							
	Other activities												
OM4200	Shoulder												
	Unsealed Shoulder												
OM4201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM4202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Guts)												Not Required
OM4300	Drainage including culverts major												
OM4301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM4302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM4303	Culvert and pit Repair	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whinew washing)	M ²	Nil	Nil	Nil	Nil							Not Required

3 of 6/22

No	Standard Of Work Item	Work Unit	Unit Of Required In each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
0M400	Vegetation												Comments
	Gross Control												
	(a) Roadside- General tidy	Hq	Nil	Nil	Nil	Nil	Nil						Not Required
0M401	(b) Clear near Safety Sign, kilometre posts and roadside furniture	Hq	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil	Nil						Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil	Nil						Not Required
0M402	Cutting Of Shrubs from Road Way	No	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
0M500	Safety Signage and Road		Nil										Not Required
0M501	Signs Maintenance	No	Nil	Nil	Nil	Nil	Nil						Not Required
0M502	Guard Stones	Lm	N/A	N/A	N/A	N/A	N/A						Not Required
0M503	Distance Stones	No	N/A	N/A	N/A	N/A	N/A						Not Required
0M504	Road Marking	M ²	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities												

Executive Engineer, R.W.D. Works Division-Jamui

Division, Jamui

unl 25/12/21

Subder

Work-Construction of Road from Arha Chamartolee Chowk on Nawada-Sikandra PWD Road to Mathahwa village.

Name of Contractor-Rajeev Kumar

$$Y = 0 * X^2 + 0.828 * X + 341.6$$

$$X = 3800$$

$$Y = 3487$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Date	Time	Section No.	Length In km	Bumps In mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
13/6/22	11:21:9	66	0.1	300	0	3000	2825	G	24.93869	85.839057	Normal
13/6/22	11:21:9	66	0.1	360	10.1	3600	3322	G	24.93844	85.84002	Normal
13/6/22	11:22:0	66	0.1	310	10.1	3100	2908	G	24.9381	85.840942	Normal
13/6/22	11:22:20	66	0.1	390	10.1	3900	3570	G	24.93746	85.841632	Normal
13/6/22	11:22:20	66	0.1	370	10.1	3700	3405	G	24.93659	85.841902	Normal
13/6/22	11:23:0	66	0.1	360	10.1	3600	3322	G	24.93574	85.842272	Normal
13/6/22	11:23:0	66	0.1	350	20.2	3500	3239	G	24.93487	85.842592	Normal
13/6/22	11:23:31	66	0.1	330	10.1	3300	3073	G	24.93405	85.842272	Normal
13/6/22	11:24:0	66	0.1	320	20.2	3200	2991	G	24.9334	85.841532	Normal
13/6/22	11:24:6	66	0.1	240	20.2	2400	2328	G	24.93256	85.84106	Normal
13/6/22	11:24:6	66	0.1	290	20.2	2900	2742	G	24.93165	85.841027	Normal
13/6/22	11:24:41	66	0.1	260	20.2	2600	2494	G	24.93076	85.840992	Normal
13/6/22	11:25:0	66	0.1	340	10.1	3400	3156	G	24.92991	85.84111	Normal
13/6/22	11:25:16	66	0.1	300	20.2	3000	2825	G	24.92987	85.84212	Normal
13/6/22	11:25:16	66	0.1	390	20.2	3900	3570	G	24.92972	85.843147	Normal
13/6/22	11:26:0	66	0.1	310	20.2	3100	2908	G	24.92884	85.843047	Normal
13/6/22	11:26:0	66	0.1	200	20.2	2000	1997	G	24.92798	85.842793	Normal
13/6/22	11:26:27	66	0.1	260	20.2	2600	2494	G	24.92709	85.84239	Culvert
13/6/22	11:26:27	66	0.1	290	20.2	2900	2742	G	24.92621	85.84207	Normal
13/6/22	11:27:2	66	0.1	370	10.1	3700	3405	G	24.92531	85.84202	Normal
13/6/22	11:28:13	66	0.1	360	20.2	3600	3322	G	24.92438	85.841985	Normal
13/6/22	11:29:0	66	0.1	350	10.1	3500	3239	G	24.92352	85.84182	Normal
13/6/22	11:29:23	66	0.1	380	10.1	3800	3487	G	24.92371	85.840558	Normal
Length		2.3				Total IRI	69364				
						Average IRI	3015.83				


Executive Engineer
Rural Work Department
Works Division-Jamui

4th 30/6/22

Name of Customer: **RAJEEV KUMAR**
 Name of Work/Construction of Road from Aha Road:
 Lab Job number:
 Date: **13-06-2022**
 Section No. **56**

Test Date: **13-06-2022** Road Name: **Construction of Road from Aha**
 Machine No: **399** Road Type: **(R) RURAL ROAD**
 Start S No: **10000** Side:
 Start E No: **23** Interval:
 Weather:
 Start Location:
 End Location:
 Equation: **$Y = 0 \cdot X^2 + 0.823 \cdot X + 341.6$**

Print Generate Report and Graph Redraw Graph Map View

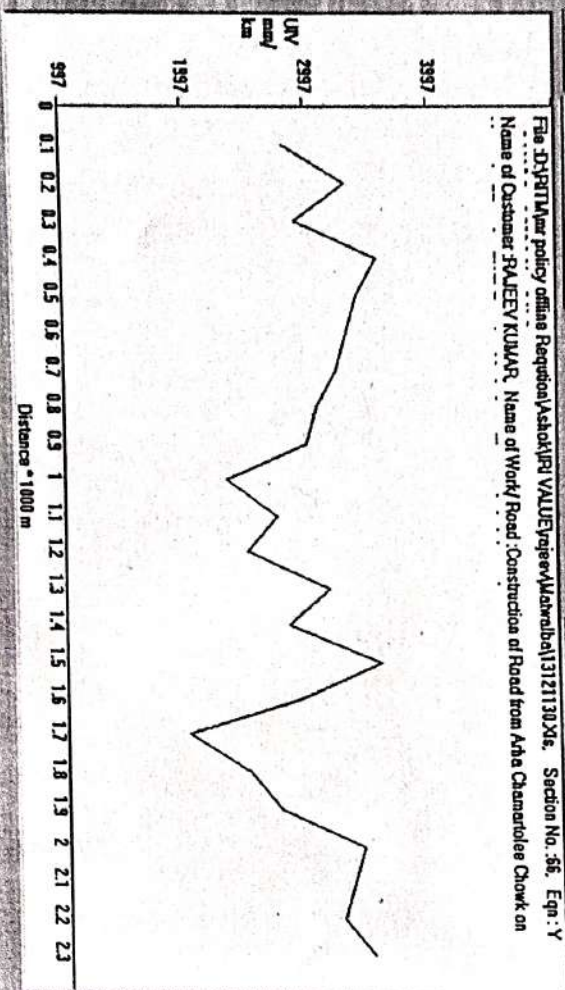

unv
 56/1/12
