

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, जमुई ।

पत्रांक ५६७/२०२२

जमुई, दिनांक ३०/६/२०२२

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, जमुई ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:-

शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में ।


महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष MR New Maintenance Policy 2018
योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण के पथों का पथवार मांगी जाने वाली आवंटन की सूची पत्र के
साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है ।

सूचनार्थ सादर समर्पित ।

अनु०- यथोक्त

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जमुई ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD(WD), Jamui
Block Name:- Khaira


1	Name of the Road	Khaira Sono REO road to Nariyana via Pachrukhi to Kharainch		
2	Batch No.	RM/JA/JAM/19/0015		
3	Project ID	28411031803		
4	Total Lenth of Road (in KM)	2.0		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	2.0		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	18.97744		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.94887		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.94887

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

(Signature)



Signature of person inspecting road

Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Jamui

Requisition Form for Scheme Head MR-13054 Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name Of Work Division:- Jamul

1 Year (3rd Quarter)

Government Of Bihar

OMO1

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From: Khaira Soro RCO Road to Nanyana via Pedmukhi to Hararinch
(Package No.-RM/JAM/19/0015)
Length of Road :- 2.0km
Inspector :- J.E RWD Sub Division : Khaira

To:-

Executive Engineer
RWD, Works Division Jamul

Date:- 30.6.2022

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required In each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Payment												No Pot Hole Found.
OM101	Pothole Patching	m ²	NIL	NIL	NIL	NIL							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL	NIL	NIL							No Crack sealing Found
OM103	Crack Sealing	Lm	NIL	NIL	NIL	NIL							
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	NIL	NIL	NIL	NIL							No Loss Of Aggregate (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL	NIL							No Bleeding/ Flushing Required
	(c) Crocodile Cracking	m ²	NIL	NIL	NIL	NIL							No Crocodile Cracking Found
105	Edge Repair	m ²	NIL	NIL	NIL	NIL							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	NIL	NIL	NIL	NIL							No Edge Drop-Off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL	NIL							Not Required
	(c) Holding water	Lm	NIL	NIL	NIL	NIL							No Holding Water Found
OM202	Embankment Repair	M ³	NIL	NIL	NIL	NIL							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	NIL	NIL	NIL	NIL							Not Required
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL	NIL							Not Required
	Other activities (Willow washing)	M ²	NIL	NIL	NIL	NIL							Not Required

lmh

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

with 3 of 1/12

Bidder

Executive Engineer, R.W.D. Works Division-Jamui

Division, Jamui

of Work-Khaira Sono REO road to Narhyana via Pachrukhi to Khairinch

Name of Contractor-Amrendra Kumar Atri Infrastructure Private Limited

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	ATEGOR ROAD	Latitude	Longitude	Event
11/6/22	9:21:23	16	0.1	290	0	2900	2742	G	24.86877	86.23923	Normal
11/6/22	9:21:23	16	0.1	310	20.2	3100	2908	G	24.86787	86.23887	Normal
11/6/22	9:22:0	16	0.1	340	20.2	3400	3156	G	24.86696	86.23872	Normal
11/6/22	9:22:0	16	0.1	350	20.2	3500	3239	G	24.86613	86.2388	Normal
11/6/22	9:22:0	16	0.1	290	20.2	2900	2742	G	24.86525	86.23894	Normal
11/6/22	9:22:34	16	0.1	290	20.2	2900	2742	G	24.86435	86.23865	Normal
11/6/22	9:22:34	16	0.1	310	20.2	3100	2908	G	24.86353	86.23811	Normal
11/6/22	9:23:9	16	0.1	340	20.2	3400	3156	G	24.86279	86.23781	Normal
11/6/22	9:23:9	16	0.1	310	20.2	3100	2908	G	24.86201	86.23736	Normal
11/6/22	9:23:9	16	0.1	340	20.2	3400	3156	G	24.86119	86.23702	Normal
11/6/22	9:23:44	16	0.1	310	20.2	3100	2908	G	24.86031	86.23724	Normal
11/6/22	9:24:0	16	0.1	380	20.2	3800	3487	G	24.85947	86.23736	Normal
11/6/22	9:24:20	16	0.1	250	20.2	2500	2411	G	24.85924	86.238	Normal
11/6/22	9:24:20	16	0.1	340	30.3	3400	3156	G	24.85897	86.23926	Normal
11/6/22	9:24:20	16	0.1	370	20.2	3700	3405	G	24.85834	86.2399	Normal
11/6/22	9:25:0	16	0.1	280	30.3	2800	2659	G	24.8575	86.23965	Normal
11/6/22	9:25:0	16	0.1	360	20.2	3600	3322	G	24.85685	86.23891	Normal
11/6/22	9:25:0	16	0.1	380	20.2	3800	3487	G	24.85597	86.23882	Normal
11/6/22	9:25:30	16	0.1	320	20.2	3200	2991	G	24.85516	86.23923	Normal
11/6/22	9:26:5	16	0.1	350	10.1	3500	3239	G	24.85423	86.23938	Normal
Length		2		Total IRI		60722					
				Average IRI		3036.1					

$$Y = 0 * X^2 + 0.828 * X + 341.6$$

$$X = 3500$$

$$Y = 3239$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

Executive Engineer
 Rural Work Department
 Works Division-Jamui


Name of Customer: Amarendra Kumar Agri Infrastructure
 Name of Work/ Road: Kharsa Soro REO road to Naga
 Lab Job number:
 Date: 11-06-2022
 Section No. 16

Test Date: 11-06-2022 Road Name: Kharsa Soro REO road to Naga
 Machine No: 339 Road Type: (R) RURAL ROAD
 Start S No: 01000 Side: Interval:
 Start E No: 20
 Weather: UV Range: 1411 To 4000 mm/day
 Start Location: Dist Range: 0 To 21 01 = 1000 m
 End Location: Equation: $Y = 0 \cdot X^2 + 0.828 \cdot X + 341.6$

Print Generate Report and Graph

Redraw Graph

Map View

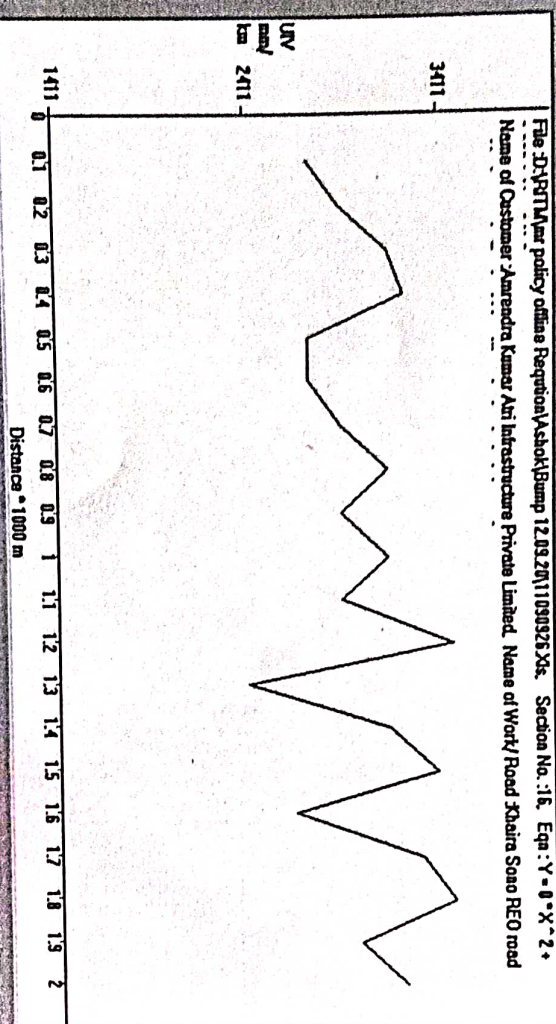

und 30/6/22
