

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:- १०१ ३१७०

सासाराम/दिनांक:- 30.5.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229 / 2021-97 अनु0 / पटना दिनांक 07.01.2022


महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(30/06/2021 -29/09/2021)

1	Name of the Road	Adampur Bazar - Kajhon (Kathawan)		
2	Batch No.	RM/RO/SAS/19/0023		
3	Project ID	10301002146		
4	Total Length of Road (In Km)	2.18 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	2.18 Km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	17.63782		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.88189		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.00000	10%	0.00000
V	VEGETATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.88189

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

Name of Road : Aadampur Bazar -Kajhon (Kathawn)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
27/5/22	16:7:5	10	0.1	290	10.1	2900	3426	G	24.877535	83.873687	Normal
27/5/22	16:7:40	10	0.1	310	20.2	3100	3654	G	24.878392	83.873568	Normal
27/5/22	16:7:40	10	0.1	290	20.2	2900	3426	G	24.879193	83.87347	Normal
27/5/22	16:8:0	10	0.1	330	20.2	3300	3881	G	24.878915	83.872727	Normal
27/5/22	16:8:17	10	0.1	340	10.1	3400	3994	G	24.878818	83.871835	Normal
27/5/22	16:9:0	10	0.1	330	10.1	3300	3881	G	24.878257	83.871245	Speed Breaker
27/5/22	16:9:27	10	0.1	330	10.1	3300	3881	G	24.877605	83.870925	Normal
27/5/22	16:10:2	10	0.1	290	10.1	2900	3426	G	24.876782	83.87106	Normal
27/5/22	16:10:2	10	0.1	340	20.2	3400	3994	G	24.875972	83.871245	Normal
27/5/22	16:10:38	10	0.1	290	20.2	2900	3426	G	24.875287	83.871397	Normal
27/5/22	16:11:0	10	0.1	220	10.1	2200	2631	G	24.875802	83.872205	Normal
27/5/22	16:11:13	10	0.1	300	30.3	3000	3540	G	24.876335	83.873063	Normal
27/5/22	16:11:13	10	0.1	250	30.3	2500	2972	G	24.876835	83.873855	Normal
27/5/22	16:11:13	10	0.1	330	40.4	3300	3881	G	24.877313	83.87468	Normal
27/5/22	16:11:13	10	0.1	240	40.4	2400	2858	G	24.8778	83.875522	Normal
27/5/22	16:12:0	10	0.1	340	20.2	3400	3994	G	24.87819	83.876497	Normal
27/5/22	16:12:0	10	0.1	330	20.2	3300	3881	G	24.87858	83.877222	Normal
27/5/22	16:12:24	10	0.1	340	20.2	3400	3994	G	24.878937	83.878265	Normal
27/5/22	16:12:24	10	0.1	300	20.2	3000	3540	G	24.879242	83.879157	Normal
27/5/22	16:13:0	10	0.1	320	20.2	3200	3767	G	24.879497	83.88013	Normal
27/5/22	16:13:0	10	0.1	300	10.1	3000	3540	G	24.87963	83.881093	Normal
Average IRI							3599				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good
<4000

Average Poor
4001-5000 >5001

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

28/5/22
A.E.

28/5/22

Name of Customer :	SHIVSHANKAR SINGH IFRA F
Name of Work/ Road :	AAADAMPUR BAZAR SE KATH
Lab Job number :	10
Date :	27-05-2022
Section No. :	10

Test Date :	28-04-2010	Road Name :	AAADAMPUR BAZAR SE KATH
Machine No. :	331	Road Type :	(P) RURAL ROAD
Start S No. :	312	Side :	SHEOSAGAR
Start E No. :	332	Interval :	
Weather :	NORMAL	UV Range :	1631 To 5000 mm/Km
Start Location :	24.87535	Dist Range :	0 To 1008 0.028 - 1000 m
End Location :	24.87963	Equation :	test


Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BOM INDICATOR REPORT\27-5-22\1 TO 5.xlsx Section No. : 10. Egn : test

Name of Customer : SHIVSHANKAR SINGH IFRA PVT. LTD. Name of Work/ Road : AAADAMPUR BAZAR SE KATHAV.

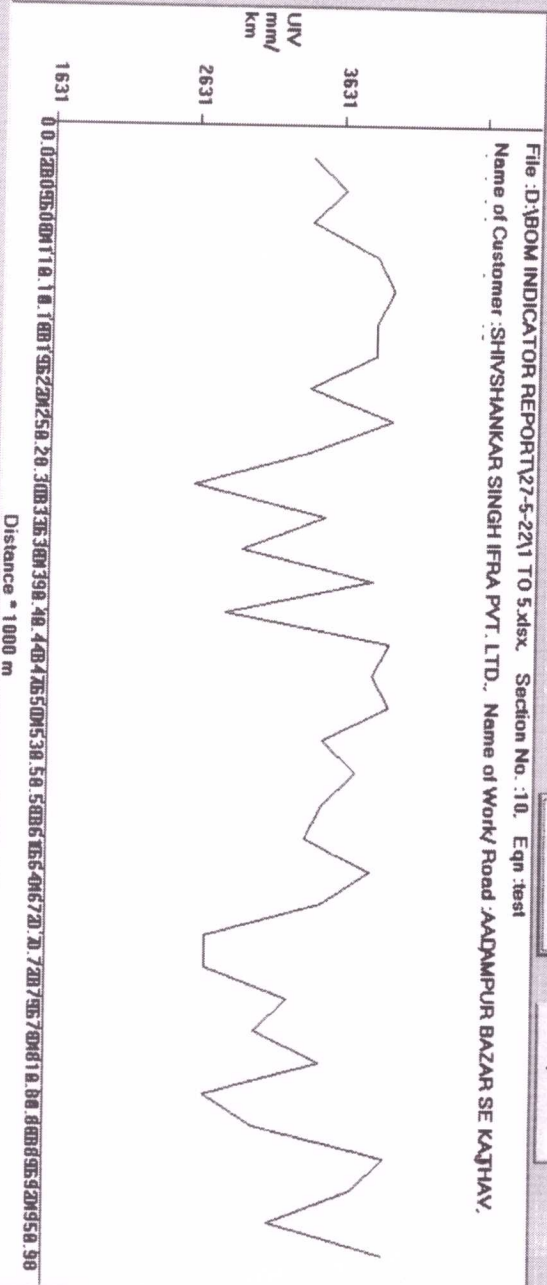

Shiv Shankar Singh

AE

28/5/22
