

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- १०६ ३१३०

सासाराम/दिनांक:- ३१.५.२०२२

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुस्क्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुस्क्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुस्क्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।


प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुस्क्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सूचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।
सूचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(30/06/2021 - 29/09/2021)

1	Name of the Road	Beda Darshandih Road - Baruan		
2	Batch No.	RM/RO/SAS/19/0023		
3	Project ID	10301002149		
4	Total Length of Road (In Km)	2.3 Km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	2.3 Km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	18.92025		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.94601		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.000000	10%	0.000000
V	VEGETATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.94601

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Puneshwar Yadav
JE

Name and Designation of person inspection road

Signature
28.05.22
JE

Date

Signature of person inspection road

Signature
28/5/22
A.E

Certify by E/I [signature] Date:-

Signature
28/5/22

Name of Road : BEDA DARSHANDIH SE BRUA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
27/5/22	14:57:24	6	0.1	330	30.3	3300	3881 G		24.92596	83.954747	Normal
27/5/22	14:57:24	6	0.1	250	30.3	2500	2972 G		24.926037	83.953377	Normal
27/5/22	14:58:0	6	0.1	200	30.3	2000	2404 G		24.926075	83.952777	Normal
27/5/22	14:58:0	6	0.1	300	30.3	3000	3540 G		24.926468	83.951902	Normal
27/5/22	14:58:0	6	0.1	330	20.2	3300	3881 G		24.92725	83.95177	Normal
27/5/22	14:58:0	6	0.1	240	30.3	2400	2858 G		24.9274	83.950875	Normal
27/5/22	14:58:35	6	0.1	330	30.3	3300	3881 G		24.92763	83.949915	Normal
27/5/22	14:58:35	6	0.1	260	30.3	2600	3086 G		24.927925	83.948872	Normal
27/5/22	14:59:0	6	0.1	250	30.3	2500	2972 G		24.92818	83.947978	Normal
27/5/22	14:59:10	6	0.1	320	20.2	3200	3767 G		24.927858	83.947305	Normal
27/5/22	14:59:10	6	0.1	320	30.3	3200	3767 G		24.927008	83.947037	Normal
27/5/22	14:59:10	6	0.1	330	30.3	3300	3881 G		24.926123	83.94677	Normal
27/5/22	14:59:45	6	0.1	340	20.2	3400	3994 G		24.92599	83.945975	Normal
27/5/22	15:0:0	6	0.1	340	30.3	3400	3994 G		24.926227	83.944982	Normal
27/5/22	15:0:0	6	0.1	280	40.4	2800	3313 G		24.926347	83.944057	Normal
27/5/22	15:0:21	6	0.1	330	30.3	3300	3881 G		24.926495	83.943047	Normal
27/5/22	15:0:21	6	0.1	340	20.2	3400	3994 G		24.926505	83.94207	Normal
27/5/22	15:0:21	6	0.1	310	20.2	3100	3654 G		24.925628	83.941935	Normal
27/5/22	15:0:56	6	0.1	330	20.2	3300	3881 G		24.924695	83.94182	Speed Breaker
27/5/22	15:1:0	6	0.1	340	10.1	3400	3994 G		24.923782	83.941665	Normal
27/5/22	15:1:31	6	0.1	330	10.1	3300	3881 G		24.923013	83.941918	Speed Breaker
27/5/22	15:2:6	6	0.1	310	20.2	3100	3654 G		24.922157	83.941413	Speed Breaker
27/5/22	15:3:17	6	0.1	330	20.2	3300	3881 G		24.922205	83.941178	Normal
Average IRI									3609		

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Average
4001-5000
Poor

28.05.22
A.E

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

Name of Customer : SHIVSHANKAR SINGH INFRA
Name of Work/ Road : BEDA DARSHANDIH SE BRU
Lab Job number : 6
Date : 27-05-2022
Section No. : 6


Test Date : 27-05-2022
Road Name : BEDA DARSHANDIH SE BRU
Machine No. : 391
Road Type : (R) RURAL ROAD
Start S No. : 203
Side : SHEOSAGAP
Start E No. : 225
Interval :
Weather : NORMAL
U/V Range : 1404 To 5000 1000 mm/km
Start Location : 24 32596
Dist Range : 0 To 0.7 0.028 * 1000 m
End Location : 24 322205
Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print Generate Report and Graph

Redraw Graph

Map View

File : D:\BOM INDICATOR REPORT\27-5-22\123.Xls, Section No. : 6, Eqn : $Y = 0 * X^2 + 1.136 * X + 132.5$
 Name of Customer : SHIVSHANKAR SINGH INFRA PVT. LTD., Name of Work/ Road : BEDA DARSHANDIH SE

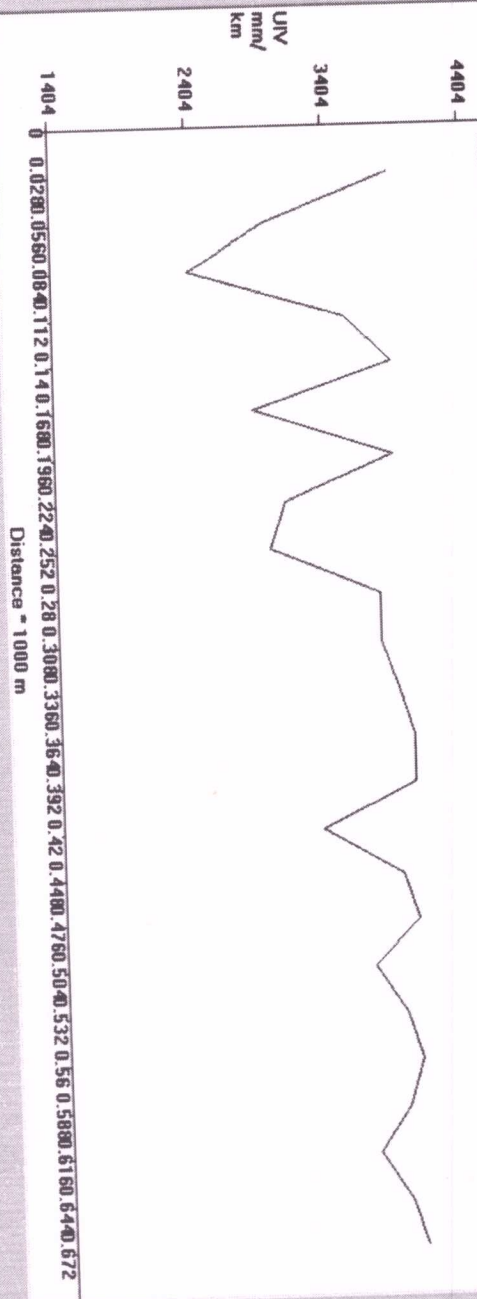

by 26.5.22

28/5/22 A.D

28/5/22
