

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल बक्सर

पत्रांक924..... बक्सर/ दिनांक15/07/22.....

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल बक्सर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
(BRRDA)

बिहार - पटना।

विषय :- MR (3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक- मु0अ0 04(मु0)3054-04-229/2021-1135 (अनु0)/ पटना, दिनांक- 09.03.2022 एवं पत्रांक- 97 दिनांक- 07.01.2022

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः MR (3054) New Maintenance Policy-2018 (Package No.- RM/BU/BUX/19/0003) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- Standard Formate for Roads
Quarterly Statement

विश्वासभाजन

15/07/22

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल बक्सर

15/07/22

STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (3rd Quarter)

PIU NAME :- Rural Works Deparetment Works Division Buxar

1	Name Of Road	Kajipur - Permanandpur		
2	Batch No.	RM/BU/BUX/19/0009		
3	Project ID	NEA220002114		
4	Total Length Of Road(in Km)	2.650		
5	Lenth Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	2.650		
6	NO. of Total Quarter (ie 3 Months as a unit) in 5 year	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	27.19750		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.35988		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.35988

date of Inpection by E/I Or His Agent

Prepared by Contractor's Self Control Unit

date

Signature of person inspecting road

Name and Designation of person inspecting road

(Signature)

Certify by E/I [Signature] date

Executive Engineer
R.W.D. (W.) Div., Buxar

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (3rd Quarter)

RWD, Works Division BUXAR
Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Kajipur - Permandapur
(Package No.RM/BU/BUX/19/0009)
Length of Road :- 2.650 Km
Inspector :- J.E RWD Sub Division : Simri

To:-

Executive Engineer
RWD, Works Division Buxar

Date:-

Position :- J.E.

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	@ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							No Edge Repair Required
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							N/A
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							N/A
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							N/A
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							N/A
	Other activities												

gahy GmC hny

Reed
13/07/22
Appendix J-E

15.02.22

Executive Engineer, Works Division, Buxar

Seco Analyzer


Name of Customer: VINOD KUMAR MISHRA
Name of Work/Road: KAJIPUR TO PA
Lab Job number:
Date: 11 Jul-20
Section No.: 79

Test Date: 09-Jul-20 Road Name: KAJIPUR TO PARMANP
Machine No: 368 Road Type: (R) RURAL ROAD
Start S No.: Side:
Start E No.: Interval
Weather: UV Range: 1577 To 5000 1000 mm/km
Start Location: KAJIPUR Dist Range: 0 To 2.9 0.1 *1000 m
End Location: PARMANP Equation: $Y = 0.0000X^2 + 0.0040X - 510.70$

Print Generate Report and Graph

Redraw Graph

Map View

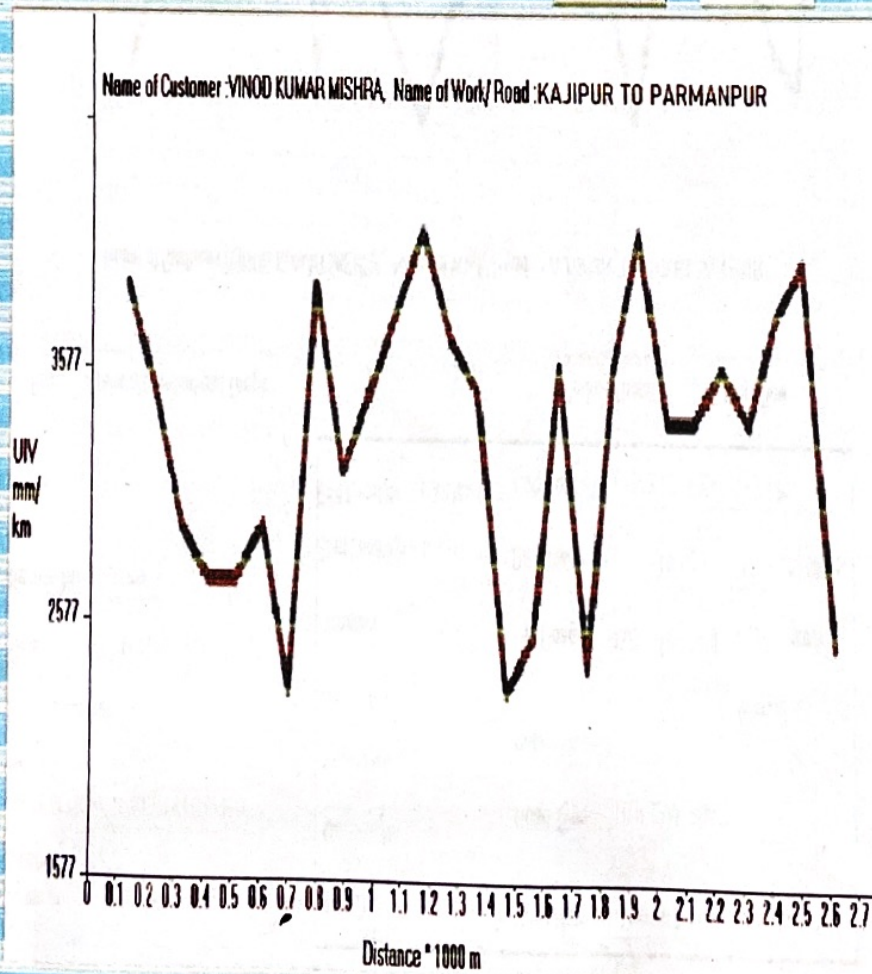

Handwritten signature
11/07/22
JE

Handwritten signature
11/07/22

ROAD NAME:- KAIJIPUR TO PARMANPUR

CONTRACTOR NAME - M/S VINOD KUMAR MISHRA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
11/07/2022	11:21:45	79	0.1	330	0	3300	3715 G		25.605789	84.152248	Normal
11/07/2022	11:22:0	79	0.1	290	20.2	2900	3315 G		25.60705	84.151295	Normal
11/07/2022	11:22:21	79	0.1	240	20.2	2400	2815 G		25.606102	84.151143	Normal
11/07/2022	11:22:21	79	0.1	220	30.3	2200	2615 G		25.60522	84.15101	Normal
11/07/2022	11:22:21	79	0.1	220	30.3	2200	2615 G		25.60431	84.150858	Normal
11/07/2022	11:22:21	79	0.1	240	30.3	2400	2815 G		25.60431	84.150858	Normal
11/07/2022	11:22:56	79	0.1	180	30.3	1800	2215 G		25.603357	84.150757	Normal
11/07/2022	11:23:0	79	0.1	330	10.1	3300	3715 G		25.602445	84.15074	Normal
11/07/2022	11:23:31	79	0.1	260	10.1	2600	3015 G		25.602248	84.1506	Normal
11/07/2022	11:23:31	79	0.1	290	20.2	2900	3315 G		25.601347	84.149763	Normal
11/07/2022	11:24:6	79	0.1	320	10.1	3200	3615 G		25.600887	84.149057	Normal
11/07/2022	11:24:6	79	0.1	350	10.1	3500	3915 G		25.59997	84.148855	Curve
11/07/2022	11:24:42	79	0.1	310	20.2	3100	3515 G		25.600002	84.147895	Normal
11/07/2022	11:25:0	79	0.1	290	20.2	2900	3315 G		25.60013	84.146885	Normal
11/07/2022	11:25:0	79	0.1	180	30.3	1800	2215 G		25.60028	84.145875	Normal
11/07/2022	11:25:17	79	0.1	200	30.3	2000	2415 G		25.600543	84.144982	Normal
11/07/2022	11:25:17	79	0.1	300	20.2	3000	3415 G		25.600715	84.143905	Normal
11/07/2022	11:25:17	79	0.1	190	30.3	1900	2315 G		25.60091	84.142978	Normal
11/07/2022	11:26:0	79	0.1	300	20.2	3000	3415 G		25.600975	84.141985	Curve
11/07/2022	11:26:0	79	0.1	350	20.2	3500	3915 G		25.600678	84.141228	Normal
11/07/2022	11:26:0	79	0.1	280	30.3	2800	3215 G		25.601125	84.140318	Curve
11/07/2022	11:26:0	79	0.1	280	20.2	2800	3215 G		25.601335	84.149308	Curve
11/07/2022	11:26:28	79	0.1	300	20.2	3000	3415 G		25.601998	84.149393	Normal
11/07/2022	11:26:28	79	0.1	280	20.2	2800	3215 G		25.601998	84.149393	Normal
11/07/2022	11:27:2	79	0.1	320	20.2	3200	3615 G		25.602885	84.149865	Normal
11/07/2022	11:27:2	79	0.1	340	30.3	3400	3815 G		25.603427	84.140572	Normal
11/07/2022	11:27:2	79	0.1	200	20.2	2000	2415 G		25.603762	84.14143	Normal

$$Y = 0 * X \wedge 2 + 1.000 * X + 415.2$$

$$X = 1800$$

$$Y = 2215$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

11/07/22
J.E

15-07-22
