

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम — 1

पत्रांक:- 1116 3190

सासाराम/दिनांक:- 11.07.2022

प्रेषक,

कार्यपालक अभियंता,
 ग्रामीण कार्य विभाग,
 कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
 3054 एम0आर0 नई अनुरक्षण नीति-2018
 ग्रामीण कार्य विभाग
 बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

11.07.22

कार्यपालक अभियंता,
 ग्रामीण कार्य विभाग,
 कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-

Sq.gram-1

4th Quarter

1	Name of the Road	Darigawn - Malhipur Road to Rampus		
2	Batch No.	R.M/R.O/SAE/19/0006		
3	Project ID	1030102024		
4	Total Length of Road (In Km)	0.95 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	-		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	4.92024 M129-		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.246 M129-		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	-	60%	-
II	SHOULDERS AND EMBANKMENTS	-	10%	-
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	-	15%	-
IV	SIGNAGE AND ROAD SAFETY	-	10%	-
V	VEGETATION	-	5%	-
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		-
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.246 M129-

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspection road

Puneshwar - Yodan

(Signature)

Date

Signature of person inspection road

Certify by E/I [signature] Date:-

10

Name of Road : MR 3054 DARIGAWA MALHIPUR ROAD SE RAMPUR

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
25/5/22	8:39:17	77	0.1	250	10.1	2500	2972	G	24.865205	83.819073	Normal
25/5/22	8:39:52	77	0.1	300	30.3	3000	3540	G	24.864315	83.819057	Normal
25/5/22	8:40:0	77	0.1	250	20.2	2500	2972	G	24.863958	83.81843	Curve
25/5/22	8:40:28	77	0.1	340	10.1	3400	3994	G	24.863357	83.817945	Curve
25/5/22	8:40:28	77	0.1	310	20.2	3100	3654	G	24.862502	83.817793	Normal
25/5/22	8:41:3	77	0.1	280	20.2	2800	3313	G	24.861592	83.817625	Normal
25/5/22	8:41:3	77	0.1	280	20.2	2800	3313	G	24.860685	83.817457	Normal
Average IRI							3394				

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3000$$

$$Y = 3540$$

(R) RURAL ROAD

Good

<4000

Average Poor
4001-5000 >5001

96.05.22
16

25/07/22

Executive Engineer
Rural Work's Department
Work Division, Sasaram-1

11.07.22


Name of Customer: BHOLE SHANKAR CONSTRU
Name of Work: MR 3054 DARIGAWA MALHIPUR
Road:
Lab Job number: 77
Date: 25-05-2022
Section No.: 77

Test Date: 25-05-2022
Road Name: MR 3054 DARIGAWA MALHIPUR
Machine No.: 391
Road Type: (R) RURAL ROAD
Start S No.: 889
Side: SHEOSAGAP
Start E No.: 895
Weather: NORMAL
Interval:
U/V Range: 1137 To 5000 mm/km
Dist Range: 0 To 0.364 0.028 * 1000 m
Start Location: 24.865205
End Location: 24.860685
Equation: test

Print Generate Report and Graph

Redraw Graph

Map View

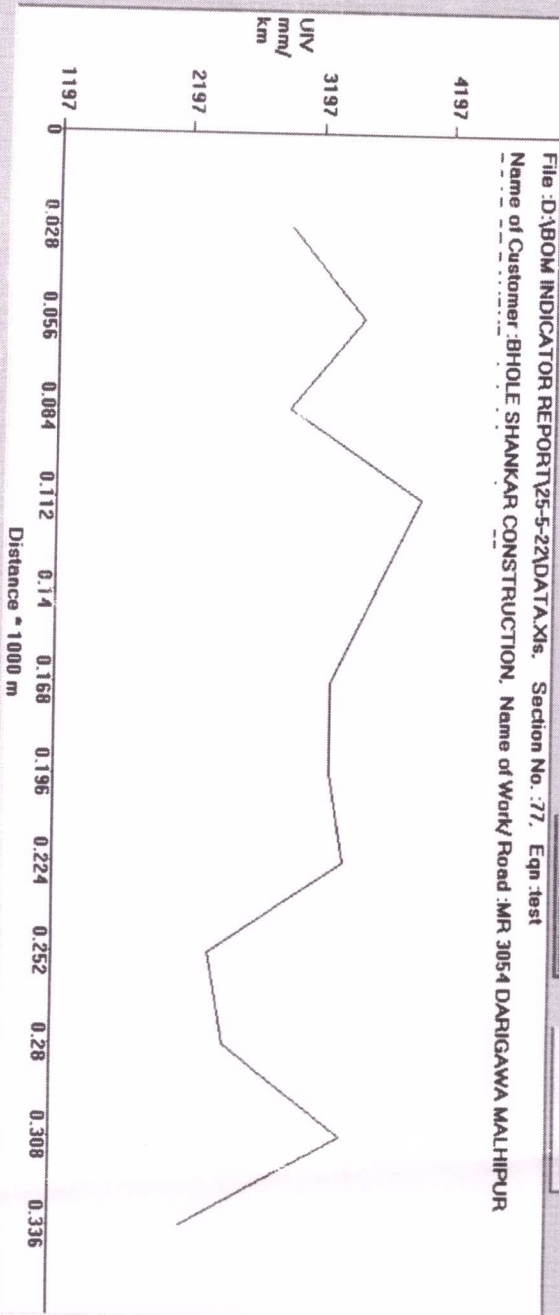

July 26.05.22

25/5/22

Nigam
