

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल बेतिया।

पत्रांक:- 2041 / बेतिया दिनांक:- 27/7/22

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बेतिया

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार राज्य ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:-

MR(3054) New Maintenance Policy 2018 योजना अन्तर्गत पंचवर्षीय अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR(3054) New Maintenance Policy 2018 योजना अन्तर्गत पंचवर्षीय अनुरक्षण कार्य का भुगतान हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः निवेदन है कि अधियाचित राशि विमुक्त करने की कृपा की जाय ताकि कराये गये कार्य का भुगतान किया जा सके।

अनु0- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेतिया

ज्ञापक- 2041

दिनांक- 27/7/22

प्रतिलिपि:- नोडल पदाधिकारी, MR(3054) New Maintenance Policy 2018, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेतिया

Requisition Form for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Circle :- Bettiah

Sl. No	Package No.	Name of Road	Project ID as per MIS	Administrative Sanction Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Requisitioned Amount of 5 Year Maintenance (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)					
1	2	3	4	5	6	7	8	9	10	11	12		14
1	MR-N/19-20 BETTIAH-07	LALBEGIYA RIVER - LALBEGIYA	31808902057	It 2067, 04.07.2019	4.660	154.420	94.05706	44.74195	119 MBD/3054MR-N/2019-20	11.11.20	10.02.2021	2.23710	1st Quarter
2	MR-N/19-20 BETTIAH-07	LALBEGIYA RIVER - LALBEGIYA	31808902057	It 2067, 04.07.2019	4.660	154.420	94.05706	44.74195	119 MBD/3054MR-N/2019-20	11.11.20	10.02.2021	2.23710	2nd Quarter
3	MR-N/19-20 BETTIAH-07	LALBEGIYA RIVER - LALBEGIYA	31808902057	It 2067, 04.07.2019	4.660	154.420	94.05706	44.74195	119 MBD/3054MR-N/2019-20	11.11.20	10.02.2021	2.23710	3rd Quarter
4	MR-N/19-20 BETTIAH-07	LALBEGIYA RIVER - LALBEGIYA	31808902057	It 2067, 04.07.2019	4.660	154.420	94.05706	44.74195	119 MBD/3054MR-N/2019-20	11.11.20	10.02.2021	2.23710	4th Quarter

27.07.2022

DIVISIONAL ACCOUNTS OFFICER
R.W.D. Works Division, Bettiah

Executive Engineer
R.W.D. Works Division Bettiah

FORM GFR 19-A**(See Government of India's decision (I) below rule- 150)****Form of Utilization certificate up to the month of June - 2022****PIU:- E.E RWD(W)DIV-BETTIAH**

SL.N O.	Name of Schemes	Sanction No.& Date with Amount (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5
1	Maintenan ce Fund of MR(3054) New Maintenan ce Policy 2018	Lt- 51, Dated-30.04.2022	52.06162	Certified that out of Rs. 52.06162 Lacs of grants-in-aid sanctioned during the years 2020-21 in favour of Executive Engineer R. W. D. Works Division, Bettiah a sum of Rs. 51.05398 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maint Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 1.00764 Lac remaining unutilized at the end of the period under report.
		TOTAL	52.06162	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

27.07.2022

Divisional Accounts Officer
R.W.D. Works Division, Bettiah

27/07/22

EXECUTIVE ENGINEER
R.W.D. Works Division, Bettiah

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Bettiah

Quarter:- 2nd

Period- 20.06.2021
19.09.2021

1	Name of the Road	LALBEGIYA RIVER - LALBEGIYA		
2	Batch No.			
3	Project ID	31808902057		
4	Total Lenth of Road (in KM)	4.660		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	4.660		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	45.7064		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.28532		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	-	60%	-
II	SHOULDERS AND EMBANMENTS	-	10%	-
III	CROSS DRAINAGE INCLUDING CULVERTS	-	15%	-
IV	SIGNAGE AND ROAD SAFETY	-	10%	-
V	VEGATION	-	5%	-
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				

Date of inspection by E/I or his agent

ADITYA SUPER AUTO PVT. LTD.

Prepare by Contractor's self Control unit

DIRECTOR

Name and Designation of person inspecting road

Date

(Signature)

Signature of person inspecting road

Certify by E/I [signature] Date:-

Executive Engineer
Rural Works Department
Works Division, Bettiah

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)														
SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT														
Road From:- LALBEGIYA RIVER - LALBEGIYA														
Length of Road :- 4.660 K.M.														
Inspector :- Ram Dular Chauhan,														
No	standard Of Work Item	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment			-	-	-	-	-	-	-	-	-	-	
OM101	Pothole Patching		m2	-	-	-	-	-	-	-	-	-	-	
OM102	Surface Depression and Rut patching		m3	-	-	-	-	-	-	-	-	-	-	
OM103	Crack Sealing		Lm	-	-	-	-	-	-	-	-	-	-	
	Surface Treatment			-	-	-	-	-	-	-	-	-	-	
OM104	(a) Loss of Aggregate (Surface Ravelling)		m2	-	-	-	-	-	-	-	-	-	-	
	(b) Bleeding / Flushing		m2	-	-	-	-	-	-	-	-	-	-	
	© Crocodile Cracking		m2	-	-	-	-	-	-	-	-	-	-	
105	Edge Repair		m2	-	-	-	-	-	-	-	-	-	-	
106	Digouts		m2	-	-	-	-	-	-	-	-	-	-	
107	Concrete pavement		m3	-	-	-	-	-	-	-	-	-	-	
	Other activities			-	-	-	-	-	-	-	-	-	-	
OM200	Shoulder			-	-	-	-	-	-	-	-	-	-	
	Unsealed Shoulder			-	-	-	-	-	-	-	-	-	-	
OM201	(a) Edge Drop-off		Lm	-	2	-	4	-	-	-	-	-	-	
	(b) Roughness, Scouring or Potholes		Lm	-	-	3	2	-	-	-	-	-	-	
	(c) Holding water		Lm	1	-	2	-	-	-	-	-	-	-	
OM202	Embankment Repair		m3	-	-	-	-	-	-	-	-	-	-	
	Other activities (Rain Cuts)			-	-	-	-	-	-	-	-	-	-	
OM300	Drainage including culverts major			-	-	-	-	-	-	-	-	-	-	
OM301	Surface Drains & Verge		Lm	-	-	-	-	-	-	-	-	-	-	
OM302	Culvert Cleaning		No	-	-	-	-	-	-	-	-	-	-	
OM303	Culvert and pit Repair		m3	-	-	-	-	-	-	-	-	-	-	
	Other activities (Whilw washing)		m2	-	-	-	-	-	-	-	-	-	-	

ADITYA SUPER AUTO PVT. LTD.

ADITYA

DIRECTOR

Standard Of Work Item			Work	Unit OF Required in each Kilometere										Comments
No	Vegetation	Name		Unit	1	2	3	4	5	6	7	8	9	
OM400	Grass Control													
OM401	(a) Roadside- General Tidy													
	(b) Clear near Safety signs, kilometer posts and roadside furniture		Ha -		0.11									
OM402	Tree and Shrub Management		Ha -		-	0.11								
	Cutting Of Branches Of Trees		Ha -		-									
	Cutting Of Shrubs From Road Way		No											
	Other activities (Trimming of Grass)		No											
OM500	Safety Signage and Road		m ²											
OM501	Signs Maintenance													
OM502	Guard Stones		No -		-									
OM503	Distance Stones		Lm -		2									
OM504	Road Marking		No -		-		1							
	Other activities		No -		-									

Executive Engineer
Rural works Department
Works Division, Bettiah

Appendix

Bidder

ADITYA SUPER AUTO PVT. LTD.

[Signature]

DIRECTOR

[Signature]
25/11/2020
J.S.P.

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR		CATEGORY ROAD	IRI	Latitude	Longitude	Event
						mm/km	UIV					
8/7/22	18:45:10	95	0.1	340	20.2	3400	3369	G	4.46	26.67279969	84.5272936	Normal
8/7/22	18:45:10	95	0.1	310	10.1	3100	3078	G	4.12	26.67235868	84.52696032	Normal
8/7/22	18:45:45	95	0.1	330	20.2	3300	3272	G	4.35	26.67207106	84.52562995	Normal
8/7/22	18:46:0	95	0.1	280	20.2	2800	2787	G	3.77	26.67199063	84.5255327	Normal
8/6/22	18:46:20	95	0.1	270	20.2	2700	2690	G	3.65	26.66951461	84.52511707	Normal
8/7/22	18:46:20	95	0.1	250	20.2	2500	2497	G	3.42	26.66918447	84.52350075	Normal
8/7/22	18:47:0	95	0.1	310	20.2	3100	3078	G	4.12	26.66846916	84.52420885	Normal
8/7/22	18:47:0	95	0.1	250	20.2	2500	2497	G	3.42	26.66747872	84.52425503	Normal
8/7/22	18:47:31	95	0.1	250	20.2	2500	2497	G	3.42	26.66694525	84.52413781	Normal
8/7/22	18:48:0	95	0.1	330	10.1	3300	3272	G	4.35	26.66585851	84.52441489	Normal
8/7/22	18:48:6	95	0.1	290	10.1	2900	2884	G	3.88	26.6643564	84.52518614	Normal
8/7/22	18:48:6	95	0.1	280	20.2	2800	2787	G	3.77	26.66178392	84.52649459	Normal
8/7/22	18:49:0	95	0.1	340	10.1	3400	3369	G	4.46	26.66090348	84.52614054	Normal
8/7/22	18:49:17	95	0.1	260	20.2	2600	2593	G	3.53	26.65954154	84.5255248	Normal
8/7/22	18:49:17	95	0.1	310	20.2	3100	3078	G	4.12	26.65881241	84.52518614	Normal
8/7/22	18:49:52	95	0.1	300	20.2	3000	2981	G	4	26.658496	84.52501681	Normal
8/7/22	18:50:0	95	0.1	270	10.1	2700	2690	G	3.65	26.6578219	84.52483209	Normal
8/7/22	18:50:27	95	0.1	250	10.1	2500	2497	G	3.42	26.65719604	84.52472358	Normal
8/7/22	18:51:3	95	0.1	250	10.1	2500	2497	G	3.42	26.65695589	84.52456236	Normal
8/6/22	18:51:3	95	0.1	280	20.2	2800	2787	G	3.77	26.65651562	84.52441009	Normal
8/7/22	18:52:0	95	0.1	260	20.2	2600	2593	G	3.53	26.65637954	84.52433843	Normal
8/7/22	18:52:10	95	0.1	300	20.2	3000	2981	G	4	26.65625146	84.52425782	Normal

ADITYA SUPER AUTO PVT. LTD.

[Signature]

DIRECTOR

[Signature]

J.E.

CIS
26/07/22
AG

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR		CATEGORY ROAD	IRI	Latitude	Longitude	Event
						mm/km	UIV					
8/7/22	18:53:10	95	0.1	310	10.1	3100	3078	G	4.12	26.65610737	84.52426678	Normal
8/7/22	18:53:45	95	0.1	330	20.2	3300	3272	G	4.35	26.65589924	84.52433843	Normal
8/7/22	18:54:0	95	0.1	280	20.2	2800	2787	G	3.77	26.65542695	84.52430261	Normal
8/7/22	18:54:20	95	0.1	270	20.2	2700	2690	G	3.65	26.65545096	84.52430261	Normal
8/7/22	18:55:20	95	0.1	250	20.2	2500	2497	G	3.42	26.65473051	84.52414138	Normal
						Total	134588					
						Average	2863.5745					

Signature
09/07/22

Signature
09/07/22
J.E.

Test Date :	06-07-2022	Road Name :		LBEGYVA RIVF I - LBEGYVA	
Machine No :	402	Road Type :		(R) RURAL ROAD	
Start S No :		Side :			
Start E No :		Interval			
Weather :		UV Range :		1303 To 1400 1000 mm/km	
Start Location :	04.53863799	Dist Range :		0 To 10 0.1 = 1000 m	
End Location :	84.52414138	Equation :		$Y = 0.0000X^2 + 0.9600X + 74.60$	


Generale Report and Graph

Redraw Graph

Map View

File E:\REPORT DUMP\10-00-07-2022\95\23062295.Xls, Section No.:95, Eqn: $Y = 0 * X^2 + 0.969 * X + 74.60$

Name of Customer :BRANZO PROJECTS PRIVATE LIMITED, Name of Work/ Road :LAIBEGIYA RIVER -

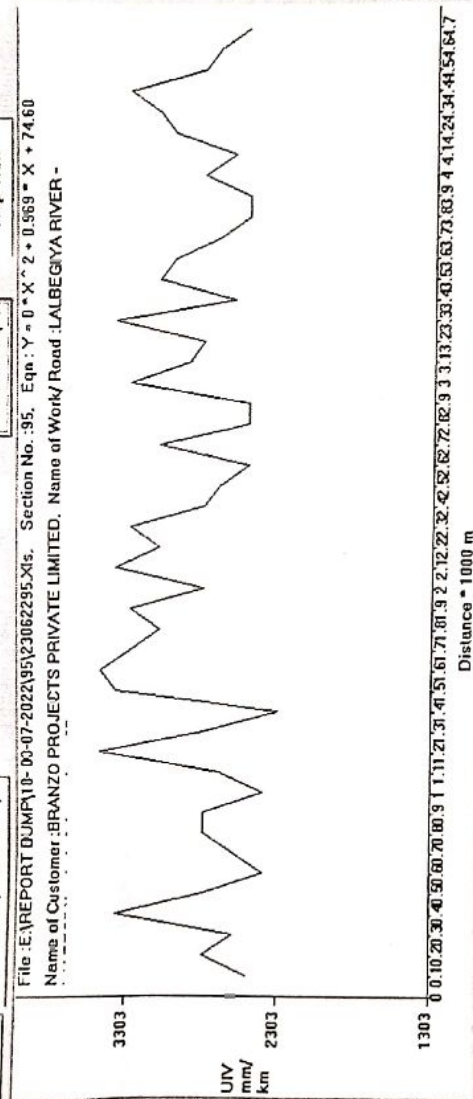

Distance = 1000 m

22/07/22

22 Feb 69

১৮
