

कार्यालय अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सासाराम - 1

पत्रांक:-1223 313

सासाराम/दिनांक:-28.07.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

सेवा में,

नोडल पदाधिकारी,
3054 एम0आर0 नई अनुरक्षण नीति-2018
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- शीर्ष 3054 एम0आर0 नई अनुरक्षण नीति-2018 के तहत पूर्ण कराये गये पथों के अनुरक्षण कार्य का आवंटन उपलब्ध कराने के संबंध में।

प्रसंग :- विभागीय पत्रांक मु0अ0-4(मु0)3054-04-229/2021-97 अनु0/पटना दिनांक 07.01.2022

सहाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के माध्यम से दिये गये निर्देश के आलोक में कहना है कि जिन पथों का अनुरक्षण कार्य पूर्ण कराया गया है। उन पथों से संबंधित वांछित सुचनाएँ विहित प्रपत्र में तैयार कर आवश्यक कार्यार्थ समर्पित की जाती है।

सुचनार्थ एवं आवश्यक कारवाई हेतु सादर समर्पित।

अनु0 :- यथोक्त।

विश्वासभाजन

N. K. Jha
28.07.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सासाराम-1

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:-Sasaram-1

2nd Quarter From(20/07/2021 -19/10/2021)

1	Name of the Road	Rohatas jila antargat karhanar prkhand me karagahar rajbaha se bilary nahar pul se saina tak path nirman		
2	Batch No.	RM/RO/SAS/19/0005		
3	Project ID	10301003017		
4	Total Length of Road (In Km)	1.5 km		
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) [1]	1.5 km		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	8.07232		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.40362		
Compliance Criteria	Standard job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0.00000	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0.00000	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00000	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0.000000	10%	0.000000
V	VEGATATION	0.00000	5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)		[5]		0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh)		[6]		0.40362

Date of inspection by E/I of his agent

Prepared by Contractor's self Control unit

Mohesh Prasad Sol
J.R.

Name and Designation of person inspection road

Mohesh Prasad Sol
25-07-22
(Signature)

Date

Signature of person inspection road
28/07/22 AE

Certify by E/I [signature] Date:-
28.07.22

Name of Road:- Rohatas jila antargat karhanar prkhand me karagahar rajbaha se bilary nahar pul se saina tak path

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
6/7/22	8:20:28	90	0.1	320	10.1	3200	3615	G	25.50275	83.92003	Normal
6/7/22	8:20:28	90	0.1	230	20.2	2300	2715	G	25.4932	83.919965	Normal
6/7/22	8:21:0	90	0.1	300	30.3	3000	3415	G	25.48438	83.919763	Normal
6/7/22	8:21:3	90	0.1	300	20.2	3000	3415	G	25.47728	83.919275	Curve
6/7/22	8:21:3	90	0.1	280	20.2	2800	3215	G	25.47977	83.91835	Normal
6/7/22	8:21:38	90	0.1	250	20.2	2500	2915	G	25.47487	83.917677	Normal
6/7/22	8:21:38	90	0.1	300	30.3	3000	3415	G	25.46645	83.917305	Normal
6/7/22	8:22:0	90	0.1	250	30.3	2500	2915	G	25.4587	83.916885	Normal
6/7/22	8:22:14	90	0.1	260	20.2	2600	3015	G	25.45012	83.916497	Culvert
6/7/22	8:22:14	90	0.1	300	30.3	3000	3415	G	25.4426	83.916027	Normal
6/7/22	8:22:14	90	0.1	260	30.3	2600	3015	G	25.43378	83.915723	Normal
6/7/22	8:22:49	90	0.1	340	30.3	3400	3815	G	25.42482	83.91542	Normal
6/7/22	8:23:0	90	0.1	250	30.3	2500	2915	G	25.41615	83.915337	Normal
6/7/22	8:23:0	90	0.1	300	30.3	3000	3415	G	25.40647	83.915302	Normal
6/7/22	8:23:24	90	0.13	330	10.1	2538	2953	G	25.39788	83.915318	Normal
Average IRI							3211				

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 3300$$

$$Y = 3715$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Handwritten signature
25-07-22
J.P

Handwritten signature
28/07/22
AE

Executive Engineer
Rural Work's Department
Works Division, Sasaram-1
28.07.22

Name of Customer :	Rinki Devi
Name of Work/ Road :	har pul se saina tak path nirman
Lab Job number :	90
Date :	7/6/2022
Section No. :	90


Test Date :	7/6/2022	Road Name :	har pul se saina tak path nirman
Machine No. :	391	Road Type :	(R) RURAL ROAD
Start S No. :	65	Side :	Kargahar
Start E No. :	79	Interval :	
Weather :	Normal	U/V Range :	744 To 5000 mm/km
Start Location :	0275.83.92003	Dist Range :	0 To 0.7 0.028 * 1000 m
End Location :	788.83.915318	Equation :	$Y = 0 * X^2 + 1.000 * X + 415.2$

Print
Generate Report and Graph

Redraw Graph

Map View

File : F:\Bomp Machine report\06-07-2022\06070957 - Copy.Xls. Section No. : 90. Egn : $Y = 0 * X^2 + 1.000 * X +$
 Name of Customer : Rinki Devi. Name of Work/ Road : Rohatas jila antargat karhanar ptkhand me karagahar rajbaha

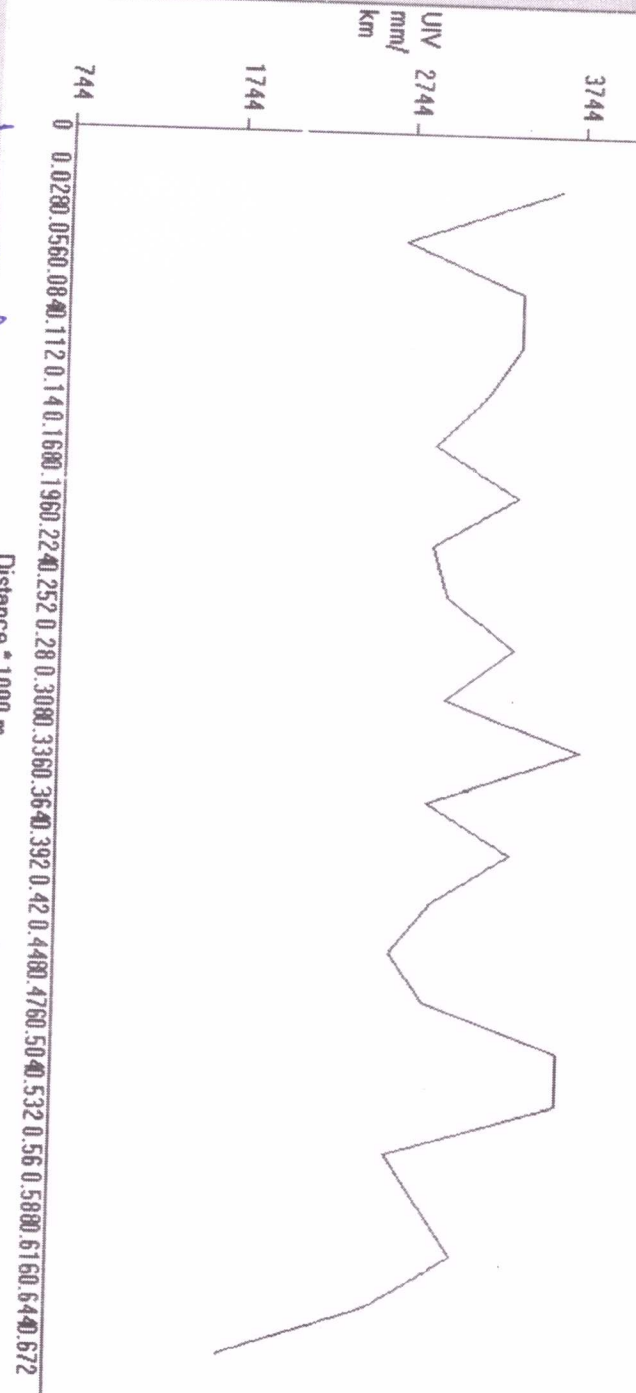

WpoodadSL
25-07-22

NK
28/07/22
AE

WpoodadSL
28-07-22
AE
