

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल इमामगंज

पत्रांक: 7/10..... इमामगंज/ दिनांक: 25/07/2022

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल इमामगंज

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
(BRRDA)
बिहार - पटना।

विषय :- MR (3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग :- अभियन्ता प्रमुख, ग्रामीण कार्य विभाग, बिहार पटना के पत्रांक- मु0अ0 04(मु0)3054-04-229/2021-1135 (अनु0)/ पटना, दिनांक- 09.03.2022 एवं पत्रांक- 97 दिनांक- 07.01.2022


महाशय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः MR (3054) New Maintenance Policy-2018 (Package No.- RM/GA/IMA/20/0005) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- Standard Format for Roads
Quarterly Statement

विश्वासभाजन


कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल इमामगंज



STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (1st Quarter)

PIU NAME :- Rural Works Department Works Division Imamganj

1	Name Of Road	IMAMGANJ-DUMARIA RD - GANSHA		
2	Batch No.	RM/GA/IMA/20/0005		
3	Project ID	NEA22000479		
4	Total Length Of Road(in Km)	4.2		
5	Length Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	4.2		
6	NO. of Total Quarter (ie 3 Months as a unit) in 5 year	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	34.72800		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.73640		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.73640

date of Inpection by E/I Or His Agent
Prepared by Contractor's Self Control Unit

Signature of Contractor

Name and Designation of person inspecting road

date

Signature of person inspecting road

Signature of person inspecting road
23/07/22

(Signature)
Signature
23/07/22
Executive Engineer
RWD Works Division
Imamganj (Gaya)

Requisition Form for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
Name Of Woks Division:- Imamganj			1 Year (1st Quarter)										
Government Of Bihar OM01 Rural Works Department			SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT										
Road From:- Imamganj Dumaria Road to Gensha (Package No.MR-N/19-20 Imamganj/20/0005) Length of Road :- 4.200 Km Period :- From:- 10-04-2021 To 09-07-2021 Inspector :- J.E, Block :Dumaria			To:- Executive Engineer RWD, Works Division Imamganj Position :- J.E Date:-										
No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
	Name		1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pothole Found
OM102	Surface Depression and Rut Patching	m ³	Nil	Nil	Nil	Nil							Not Required
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							Not Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							Not Found
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N/A	N/A	N/A	N/A							Not Required
107	Concrete pavement	m ³	N/A	N/A	N/A	N/A							N/A
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							Not Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage Including culverts major												
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							N/A
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OMS00	Safety Signage and Road		Nil										Not Required
OMS01	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OMS02	Guard Stones	Lm	Nil	Nil	Nil	Nil							Not Required
OMS03	Distance Stones	No	Nil	Nil	Nil	Nil							Not Required
OMS04	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

02/07/22

Appendix

02/07/22

Executive Engineer, Works Division, Imamganj

02/07/22


Name of Customer :	AJAY KUMAR	Test Date :	19-07-2022	Road Name :	MAMGANJ DUMARIYA MAIN
Name of Work/ Road :	IMAMGANJ DUMARIYA ROAD	Machine No :	212	Road Type :	(R) RURAL ROAD
Lab Job number :		Start S No :		Side :	DUMARIYA
Date :	19-07-2022	Start E No :		Interval	
Section No. :	28	Weather :	NORMAL	UIV Range :	1615 To 5000 1000 mm/km
		Start Location :	MAMGANJ DU	Dist Range :	0 To 4.3 0.1 * 1000 m
		End Location :	GANSA	Equation :	$Y = 0 * X^2 + 1.000 * X + 415.2$

Print

Generate Report and Graph

Redraw Graph

Map View

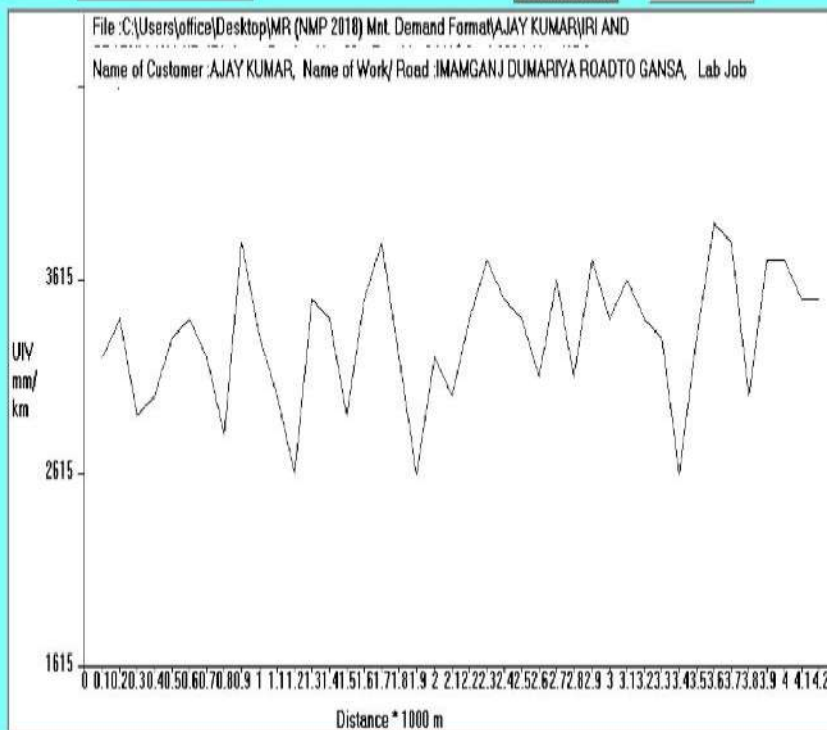

23/07/22

23/07/22

Date	Time	Section No.	Length in km	Bumps in mm	Speed		OR mm/km	IRI		Latitude	Longitude	Event
					Rate			mm/km	ROAD			
19-07-2022	11:44:27	28	0.1	280		0	2800	3215	G	24.42022	84.42387	Normal
19-07-2022	11:44:37	28	0.1	300	20.2		3000	3415	G	24.42617	84.42218	Normal
19-07-2022	11:44:51	28	0.1	250	20.2		2500	2915	G	24.42526	84.4208	Normal
19-07-2022	11:45:0	28	0.1	260	20.6		2600	3015	G	24.42438	84.41982	Normal
19-07-2022	11:45:0	28	0.1	290	20.6		2900	3315	G	24.42343	84.41932	Normal
19-07-2022	11:45:0	28	0.1	300	20.6		3000	3415	G	24.42251	84.41948	Normal
19-07-2022	11:45:26	28	0.1	280	20.6		2800	3215	G	24.42158	84.41848	Normal
19-07-2022	11:45:26	28	0.1	240	30.3		2400	2815	G	24.42064	84.41882	Normal
19-07-2022	11:45:26	28	0.1	340	30.3		3400	3815	G	24.42975	84.41915	Curve
19-07-2022	11:46:0	28	0.1	290	30.3		2900	3315	G	24.42876	84.41865	Normal
19-07-2022	11:46:2	28	0.1	260	20.2		2600	3015	G	24.42788	84.41797	Normal
19-07-2022	11:46:2	28	0.1	220	20.2		2200	2615	G	24.42699	84.4168	Normal
19-07-2022	11:46:2	28	0.1	310	30.3		3100	3515	G	24.42602	84.41578	Normal
19-07-2022	11:46:2	28	0.1	300	30.3		3000	3415	G	24.42508	84.41393	Normal
19-07-2022	11:46:37	28	0.1	250	20.2		2500	2915	G	24.42418	84.41107	Normal
19-07-2022	11:47:0	28	0.1	310	30.3		3100	3515	G	24.42342	84.41628	Normal
19-07-2022	11:47:0	28	0.1	340	30.3		3400	3815	G	24.42273	84.42252	Normal
19-07-2022	11:47:12	28	0.1	280	30.3		2800	3215	G	24.42202	84.42908	Normal
19-07-2022	11:47:12	28	0.1	220	30.3		2200	2615	G	24.42132	84.43565	Normal
19-07-2022	11:47:12	28	0.1	280	30.3		2800	3215	G	24.42702	84.44153	Normal
19-07-2022	11:47:47	28	0.1	260	20.2		2600	3015	G	24.42617	84.44845	Normal
19-07-2022	11:47:47	28	0.1	300	30.3		3000	3415	G	24.42526	84.4543	Normal
19-07-2022	11:48:0	28	0.1	330	30.3		3300	3715	G	24.42438	84.4609	Normal
19-07-2022	11:48:0	28	0.1	310	30.3		3100	3515	G	24.42343	84.4609	Normal
19-07-2022	11:48:0	28	0.1	300	30.3		3000	3415	G	24.42251	84.4673	Normal
19-07-2022	11:48:23	28	0.1	270	10.1		2700	3115	G	24.42158	84.4637	Normal
19-07-2022	11:48:23	28	0.1	320	10.1		3200	3615	G	24.42064	84.46043	Normal
19-07-2022	11:48:23	28	0.1	270	30.3		2700	3115	G	24.42975	84.46648	Normal
19-07-2022	11:48:23	28	0.1	330	0		3300	3715	G	24.42876	84.47305	Speed breaker
19-07-2022	11:49:0	28	0.1	300	30.5		3000	3415	G	24.42788	84.47978	Normal
19-07-2022	11:50:9	28	0.1	320	30.5		3200	3615	G	24.42699	84.55001	Normal
19-07-2022	11:50:44	28	0.1	300	30.5		3000	3415	G	24.42602	84.52007	Normal

Y = 0 * X ^

X = 2900

Y = 3364

(R) RURAL

Good

<4000

19-07-2022	11: 51: 0	28	0.1	290	30.5	2900	3315 G	24,42508	84,52662	Normal
19-07-2022	11: 51: 0	28	0.1	220	30.5	2200	2615 G	24,42418	84,52662	Normal
19-07-2022	11: 51: 0	28	0.1	290	30.5	2900	3315 G	24,42342	84,52645	Normal
19-07-2022	11: 51: 19	28	0.1	350	35.4	3500	3915 G	24,42273	84,49595	Normal
19-07-2022	11: 51: 19	28	0.1	340	35.4	3400	3815 G	24,42202	84,49353	Normal
19-07-2022	11: 51: 19	28	0.1	260	35.4	2600	3015 G	24,42132	84,47328	Normal
19-07-2022	11: 52: 0	28	0.1	330	35.4	3300	3715 G	24,42058	84,47288	Normal
19-07-2022	11: 52: 0	28	0.1	330	35.4	3300	3715 G	24,42988	84,47298	Normal
19-07-2022	11: 52: 0	28	0.1	310	29.1	3100	3515 G	24,42914	84,4743	Normal
19-07-2022	11: 52: 0	28	0.1	310	29.1	3100	3515 G	24,4292	84,47446	Normal

23/07/22

23/07/22
