

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक- 1082-

दिनांक- 28/5/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) "नई अनुरक्षण नीति 2018" योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाराज,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) "नई अनुरक्षण
नीति 2018" योजनान्तर्गत पथ:-

1. BETTIAH P.W.D. PATH ME KOERGANWA CHOWK SE HARSARI
HARIJAN TOLI HOTE HUE PURANIYA MUKHYA PATH TAK
KALIKARAN
2. P.W.D. ROAD NARKATIAGANJ BETTIAH MAIN ROAD
KOIERAGANWA CHOWK SE VIKRAMPUR HOTE HUE RAJPUR
P.M.G.S.Y TAK SADAK NIRMAN

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना
विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल नरकटियागंज



**Office Of The Executive Engineer
Rural Works Department
Works Division, Narkatiaganj**

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IR (in mm/Km)	Thickness of Bitumen Layer in mm.	Value of Bitumen content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	MR-N728-21 NARKATIAGANJ	BETTIAH P.W.D. PATH ME KOERGANWA CHOWK SE HARSARI HARDAN TOLI HOTE HUE PURANIYA MUKHYA PATH TAK KALIKARAN	31808901002	1099 31.03.2021	2.520	75.16000	58.96329	14.19664	01/01-21 11.01.2021	20-02-2023		2692	SDBC-15mm	SDBC-7	0.00000	0.00000	57.58329	Surface Complete
2	MR-N728-21 NARKATIAGANJ	P.W.D. ROAD NARKATIAGANJ BETTIAH MAIN ROAD KOERGANWA CHOWK SE VIKRAMPUR HOTE HUE RAJAPUR P.M.G.S.Y TAK SADAK NIRMAN	31808901012	1099 31.03.2021	2.245	75.94400	59.94665	13.55131	01/01-21 11.01.2021	20-02-2023		2951	SDBC-15mm	SDBC-7	0.00000	0.00000	57.52465	Surface Complete

[Signature]
Provisional Account Officer
Rural Works Department
Works Division Narkatiaganj

[Signature]
Executive Engineer
Rural Works Department
Works Division Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ
FROM GFR 19 - A

(See Government of India's Decision (I) below Rule - 150)
 Form of Utilisation Certificate upto the month of May-2022

Name of the Head :- New Maintenance Policy 2018

Month:- MAY- 2022 (27.05.2022)

Sl. No.	Name of Scheme	Sanctioned No/ Date	Amount Received (in Lacs Rs.)	Particulars
1	2	3	4	5
1	New Maintenance Policy 2018	Up to letter no. 01 Dt. 20.05.2022	10322.18308	Certified that out of Rs. 10322.18308 Lacs received during the year 2022-23 in favour of Executive Engineer R.W.D. Works Division, Narkatiaganj, Bihar a sum of Rs 10314.43268 Lacs has been utilized for the purpose of New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 7.75040 Lacs remaining un-utilized at the end of the period under.
	Total -		10322.18308	


- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was Sanctioned.


Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

3 **Physical Progress achieved :-**

- Construction of Road Works.
- Construction of CD. Works.


 Divisional Accounts Officer
 RWD Works Division
 Narkatiaganj


 Executive Engineer
 RWD Works Division
 Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- BETTIAH P.W.D. PATH ME KOERGANWA CHOWK SE HARSARI
:- HARIJAN TOLI HOTE HUE PURANIYA MUKHYA PATH TAK
KALIKARAN

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- MADAN MOHAN MISHRA


Length of Road :- 2.520 KM

Project ID :- 31808901002


Package No. :- MR-N/20-21 NARKATIAGANJ/04

Name of Block :- Narkatiaganj


Certified that all item wise 100% measurement has been taken by me


27/05/2022
S.R.

Certified that all item wise 50% measurement has been verified by me


27/05/2022
A.E.

Certified that all item wise 10% measurement has been verified by me



कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल
नरकटियागंज

Name of Road - BETTIAH P.W.D. PATH ME KOERGANWA CHOWK SE HARSARI HARIJAN TOLI HOTE HUE
PURANIYA MUKHYA PATH TAK KALIKARAN [Sec-27]

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/ 5/ 22	16: 21: 55	27	0.1	260	0	2600	2645	G	27.71165	84.484528	Normal
25/ 5/ 22	16: 22: 0	27	0.1	230	20.1	2300	2341	G	27.7161	84.483687	Normal
25/ 5/ 22	16: 22: 32	27	0.1	220	20.2	2200	2237	G	27.72143	84.482978	Normal
25/ 5/ 22	16: 22: 32	27	0.1	260	20.2	2600	2627	G	27.72598	84.482137	Curve
25/ 5/ 22	16: 23: 0	27	0.1	300	20.2	3000	3033	G	27.72662	84.481195	Normal
25/ 5/ 22	16: 23: 7	27	0.1	250	20.2	2500	2563	G	27.726	84.480168	Normal
25/ 5/ 22	16: 23: 7	27	0.1	230	20.1	2300	2349	G	27.72637	84.479192	Normal
25/ 5/ 22	16: 24: 0	27	0.1	310	20.1	3100	3103	G	27.72562	84.478198	Normal
25/ 5/ 22	16: 24: 18	27	0.1	300	10.1	3000	3028	G	27.7276	84.477238	Normal
25/ 5/ 22	16: 24: 53	27	0.1	330	10.1	3300	3327	G	27.72405	84.476582	Normal
25/ 5/ 22	16: 25: 0	27	0.1	270	20.2	2700	2734	G	27.71508	84.476582	Normal
25/ 5/ 22	16: 25: 28	27	0.1	270	20.2	2700	2748	G	27.7063	84.477	Normal
25/ 5/ 22	16: 25: 28	27	0.1	250	20.2	2500	2567	G	27.69773	84.47682	Normal
25/ 5/ 22	16: 26: 3	27	0.1	270	20.2	2700	2745	G	27.6891	84.476852	Normal
25/ 5/ 22	16: 26: 3	27	0.1	250	20.2	2500	2541	G	27.68028	84.47672	Normal
25/ 5/ 22	16: 26: 39	27	0.1	220	20.2	2200	2235	G	27.672	84.476447	Normal
25/ 5/ 22	16: 27: 0	27	0.1	280	20.2	2800	2827	G	27.66407	84.47601	Curve
25/ 5/ 22	16: 27: 14	27	0.1	310	20.2	3100	3133	G	27.6557	84.475638	Curve
25/ 5/ 22	16: 27: 14	27	0.1	260	10.1	2600	2664	G	27.6482	84.47611	Curve
25/ 5/ 22	16: 27: 49	27	0.1	240	20.2	2400	2439	G	27.64287	84.475437	Normal
25/ 5/ 22	16: 28: 0	27	0.1	300	20.2	3000	3031	G	27.63835	84.474595	Normal
25/ 5/ 22	16: 28: 25	27	0.1	310	20.2	3100	3131	G	27.6376	84.473585	Normal
25/ 5/ 22	16: 28: 25	27	0.1	230	20.2	2300	2337	G	27.64063	84.472677	Normal
25/ 5/ 22	16: 29: 0	27	0.1	320	20.2	3200	3235	G	27.64193	84.4717	Normal
25/ 5/ 22	16: 29: 0	27	0.1	310	20.2	3100	3133	G	27.64605	84.470875	Normal
25/ 5/ 22	16: 29: 0	27	0.1	230	20.2	2365	0.25	G	27.64975	84.469982	Normal
25/ 5/ 22	16: 29: 35	27	0.023	250	20.2	2531	0.25	G	27.65025	84.469713	Normal

Name of Road - BETTIAH P.W.D. PATH ME KOERGANWA CHOWK SE HARSARI HARIJAN TOLI HOTE HUE
PURANIYA MUKHYA PATH TAK KALIKARAN [Sec-27]

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			

Average IRI Value=2692

27/05/22
S.R.

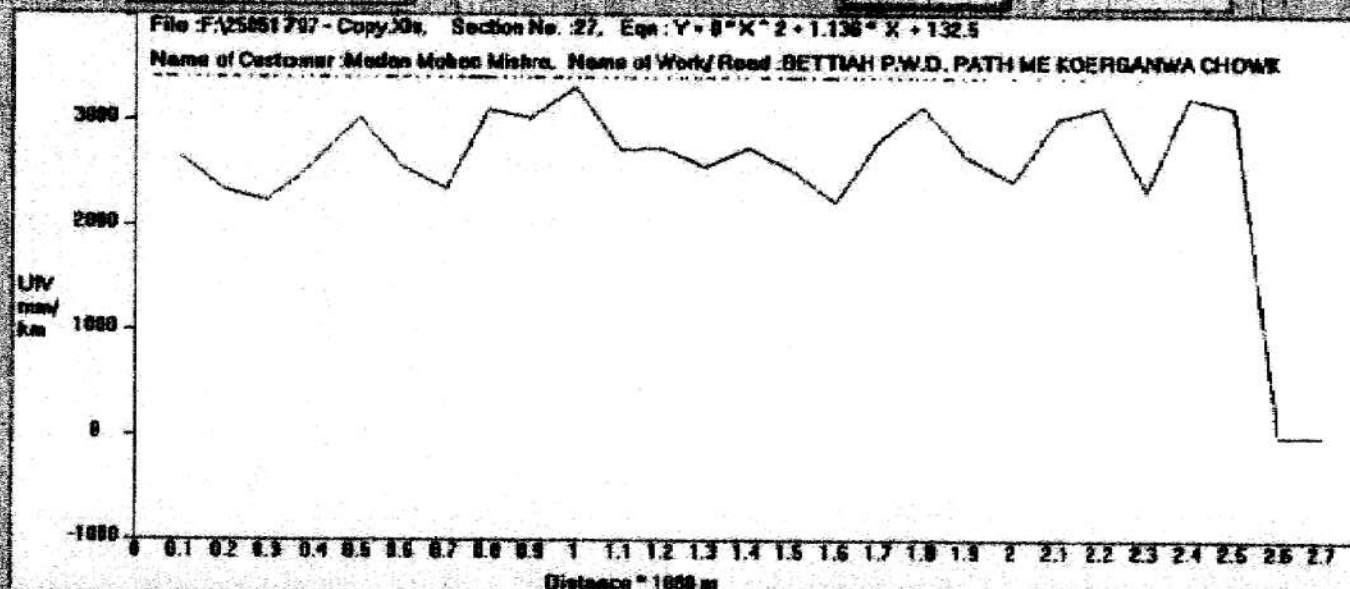
27/05/22
A.E.
Nankahigay

27/05/22
कार्यपालक अभियंता
जनकपुर महानगरपालिका
नगर कार्यपालिका

Name of Customer : Madan Mohan Mishra
 Name of Work/ Road : BETTAH P.W.D. PATH ME KE
 Lab Job number :
 Date : 25-May-22
 Section No. : 27

Test Date	25-May-22	Section Name	BETTAH P.W.D. PATH ME KE		
Machine No.	402	Station Name	(R) RURAL ROAD		
Start E. No.		Station			
Start E. No.		Station			
Station		Station	-1000	To	4000
Station		Station	0	To	2.8
Station		Station	0	To	0.1
Station		Station	Y = 0 * X^2 + 1.138 * X + 132.5		

Print Generate Report and Graph Radio Graph Map View



Signature
 Date
 Place
