

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....905 अर्द्ध 0

दिनांक.....17/5/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 18.18298 (अठारह लाख अठारह हजार दो सौ अठानबे) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन


17-5-22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- Muzaffarpur East-1

Name of Works Division:- Muzaffarpur East-I																														
Road Details				Actual Date of Completion	AA Details		Agreement								Actual Maintenance Expenditure							Length as per Bump Report	IRI As per bump Report	Current Maintenance Demand						Remarks
Sl. No.	Name of Raods	Batch No.	Project ID		Main Work Amount (in Lakh	Maintenan ce Amount (in lakh)	Main Work Amount (in Lakh)	Agre emen t-1	Agree ment-2	Agree ment-3	Agree ment-4	Agree ment-5	Total Maintenan ce	Length (in KM)	1st. Year Maint enanc e	2nd. Year Mainte nance	3rd. Year Mainte nance	4th Year Mainte nance	5th Year Mainte nance	Total Maintan ance Expendi ure	1st QTR Mainte nance			2nd QTR Mainte nance	3rd QTR Mainte nance	4th QTR Mainte nance	5th QTR Mainte nance	Total		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	30	31	
1	Kaffen Dania Chhapra - Pupri	RMMUMUZ 190016	31507202148	12/7/2020	57.87700	31.07900	52.08400	1.70552	3.12190	7.81683	3.73417	8.57021	24.94863	2.950	0.000	0.000	0.000	0.000	0.000	0.000	2.95	2956.233	1.24743	1.24743	1.24743	1.24743	1.24743	6.23716		
2	Mohanath manianiari - Nirpur	RMMUMUZ 190016	31507202192	13-07-2020	53.79600	27.20400	48.31300	1.45302	2.70505	6.85031	3.25925	7.52846	21.79609	2.500	0.000	0.000	0.000	0.000	0.000	0.000	2.50	2561.115	1.08980	1.08980	1.08980	1.08980	1.08980	5.44902		
3	Silaur Bimal - Silaur Basdew	RMMUMUZ 190016	31507202272	9/7/2020	63.61000	29.49000	56.83000	1.71665	3.21873	8.17778	3.88313	8.99090	25.98719	3.110	0.000	0.000	0.000	0.000	0.000	0.000	3.11	2589.258	1.29936	1.29936	1.29936	1.29936	1.29936	6.49680		
Total																												18.18298		



 Executive Engineer
 R.W.D. Works Division
 Muzaffarpur East-1


Road name :- Silaut vimal to Silaut Basdev

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	TEGORY ROAD	IRI	Latitude	ongitude	Event
7/5/22	15:51:0	34	0.1	260	0	2600	2557	G	3.49	26.41788	85.48737	Normal
7/5/22	15:51:24	34	0.1	320	20.2	3200	3151	G	4.2	26.42055	85.48635	Normal
7/5/22	15:52:0	34	0.1	250	10.1	2500	2458	G	3.37	26.43945	85.48551	Normal
7/5/22	15:53:0	34	0.1	240	10.1	2400	2360	G	3.25	26.4442	85.48444	Normal
7/5/22	15:57:22	34	0.1	250	20.2	2500	2458	G	3.37	26.441	85.47534	Normal
7/5/22	15:58:0	34	0.1	290	10.1	2900	2854	G	3.85	26.43252	85.47493	Normal
7/5/22	15:58:10	34	0.1	310	20.2	3100	3052	G	4.09	26.42387	85.4747	Normal
7/5/22	15:58:32	34	0.1	270	20.2	2700	2656	G	3.61	26.41427	85.47434	Normal
7/5/22	15:59:0	34	0.1	330	20.2	3300	3250	G	4.32	26.40607	85.47407	Normal
7/5/22	15:59:7	34	0.1	270	10.1	2700	2656	G	3.61	26.3933	85.47423	Normal
7/5/22	16:0:0	34	0.1	320	10.1	3200	3151	G	4.2	26.38385	85.47428	Normal
7/5/22	16:1:34	34	0.1	230	20.2	2300	2261	G	3.13	26.35852	85.47194	Normal
7/5/22	16:1:34	34	0.1	170	30.3	1700	1667	G	2.38	26.3504	85.47231	Normal
7/5/22	16:2:8	34	0.1	310	30.3	3100	3052	G	4.09	26.3428	85.47288	Normal
7/5/22	16:2:28	34	0.1	200	30.3	2000	1964	G	2.76	26.33628	85.47354	Normal
7/5/22	16:2:38	34	0.1	210	30.3	2100	2063	G	2.88	26.4959	85.47421	Normal
7/5/22	16:2:47	34	0.1	270	30.3	2700	2656	G	3.61	26.48855	85.47488	Normal
7/5/22	16:2:54	34	0.1	260	20.2	2600	2557	G	3.49	26.48038	85.47547	Normal
7/5/22	16:3:0	34	0.1	280	10.1	2800	2755	G	3.73	26.47308	85.47596	Normal
7/5/22	16:3:19	34	0.1	220	20.2	2200	2162	G	3	26.46502	85.47652	Normal
7/5/22	16:3:19	34	0.1	280	20.2	2800	2755	G	3.73	26.45758	85.477	Normal
7/5/22	16:4:0	34	0.1	300	10.1	3000	2953	G	3.97	26.45025	85.47756	Normal
7/5/22	16:4:10	34	0.1	230	30.3	2300	2261	G	3.13	26.44268	85.47818	Normal
7/5/22	16:4:20	34	0.1	240	30.3	2400	2360	G	3.25	26.43515	85.47882	Normal
7/5/22	16:4:29	34	0.1	210	30.3	2100	2063	G	2.88	26.42842	85.47951	Normal
7/5/22	16:4:29	34	0.1	270	30.3	2700	2656	G	3.61	26.4225	85.48017	Normal
7/5/22	16:5:0	34	0.1	180	20.2	1800	1766	G	2.51	26.39798	85.48335	Normal
7/5/22	16:5:19	34	0.1	330	10.1	3300	3250	G	4.32	26.39152	85.483	Normal
7/5/22	16:6:0	34	0.1	360	10.1	3600	3546	G	4.67	26.38448	85.48246	Normal
7/5/22	16:6:12	34	0.1	310	20.2	3100	3052	G	4.09	26.37577	85.48202	Normal
7/5/22	16:7:0	34	0.1	190	10.1	1900	1865	G	2.63	26.3686	85.4803	Normal
Average									2589.258			

$Y = 0 * X^2 + 0.989 * X - 13.58$
 $X = 1900$
 $Y = 1865$
(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001


11/05/2022
J-B


11/05/2022
AE

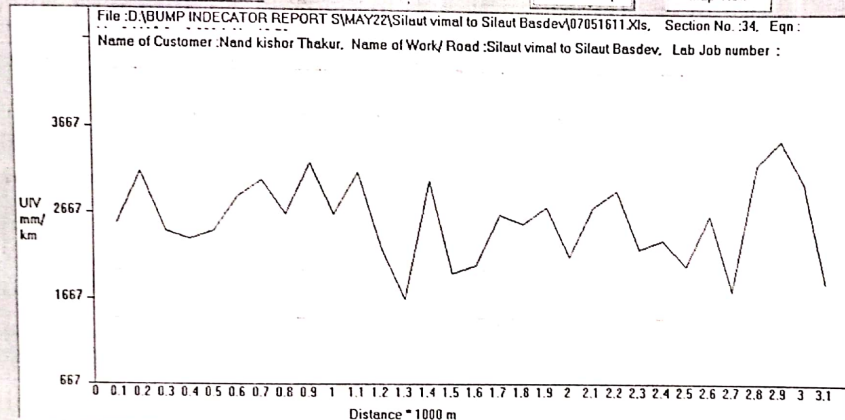

17.5.22

Name of Customer : Nand kishor Thakur
 Name of Work/ Road : Silaut vimal to Silaut Basdev
 Lab Job number :
 Date : 02-06-2009
 Section No. : 34

Test Date : 28-04-2010 Road Name : Silaut vimal to Silaut Basdev
 Machine No : 376 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 667 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 32 01 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.989 * X - 13.58$

Print Generate Report and Graph

Redraw Graph Map View



11/05/2009
 S.C.

11/05/2009
 AE

17-5-22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Silaur Bimal - Silaut Basdew		
2	Batch No.	RM/MU/MUZ/19/0016		
3	Project ID	31507202272		
4	Total Length of Road (in Km)	3.11		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.11		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	25.98719		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.29936		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.29936

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-I

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Silaur Bimal - Silaut Basdev
Length of Road: 3.11 KM
Periode : From.....
Inspector: A.E RWD Sub Division, Kudhani

To: Executive Engineer
RWD Works Division Muzaffarpur East-I Date:
Position: A.E

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required


Date

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil							Not Required
	OM 400 Vegetation												
OM401	Grass Control												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and shrub management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Nand Kishore Thakur
Bidder


Appendix
3-6


7-5-22
AE


7-5-22
Executive Engineer, Rural Work Department, Work
Division, Muzaffarpur East 1
