

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्यप्रमंडल, चकिया, (पूर्वी चम्पारण),

पत्रांक: 722 अनु0 / चकिया, दिनांक: 21 / 06 / 2022

प्रेषक

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई अनुरक्षण नीति-2018 M.R (3054) योजना के अन्तर्गत पंचवर्षीय अनुरक्षण कार्य के लिए निधि उपलब्ध कराने के संबंध में।

प्रसंग- अभियंता प्रमुख, ग्रा0का0वि0, बिहार, पटना के पत्रांक-मु0अ0-4(मु0)
3054-04-229 / 2021-1135 (अनु0) / पटना, दिनांक-09.03.2022

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः M.R (3054) नई अनुरक्षण नीति-2018 (Package No.RM/EA/CHA/20/0009) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दशाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया, कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:- 1. अधियाचना प्रपत्र।

2. 19ए प्रपत्र।

3. Signed Hard Copy and of recorded IRI is enclosed

4. Standard Format for Roads Quarterly Statement

विश्वासभाजन,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

21/06/22

Form GER 19-A
(See Government of India's decision (1) bellow Rule - 150)
Form of utilization certificate up to the month up to 06/2022
M.R. (3054)

PIU - RWD , W.D- CHAKIA

Sl. No.	Name of Scheme	Sanction No. / Date with Amount (in RS. Laes)	Amount Received (in RS. Laes)	particulars
1	M.R. (3054) New Maintenance Policy- 2018	0.00000	0.00000	Certified that out of Rs.0.00 Laes Riceive upto the year 2022-23 Executive Engineer RWD, (W) DIV, Chakia a sum of RS.0.00 of M.R. (3054) Schemes given in the margin for which it was sanctioned and that the balance of Rs.0.00 laes remaining unutilized at this end of June-2022

2. Certificate that I have satisfied myself that the conditions on which the grand's-in-aid was sanctioned have been duly fulfilled/ate being fulfilled and that have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned kinds of cheks exercised:-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.

3. Physical Progress achieved :-

- Construction of M.R. (3054) New maintenance Policy-2018 (Details in Progress report)
- Construction of Road Works. (.....Do.....)
- GSB entered in MB has been badly damage due to flood in Dekha Bandh to Ajit Singh ke Tola Tak Path

EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT
WORKS DIVISION- CHAKIA.

21/06/22

No	Standard Of Work Item	Work Unit	Unit OF Required in each Kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation	Unit											
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
	Tree and Shrub Management	No	Nil	Nil									Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil									Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil									Not Required
	Other activities (Trimming of Grass)	M ²	111.46	89.31									Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil									Not Required
OM502	Guard Stones	Lm	Nil	Nil									Not Required
OM503	Distance Stones	No	Nil	Nil									Not Required
OM504	Road Marking	M ²	Nil	Nil									Not Required
	Other activities												


13/06/22
 AE


 Executive Engineer,
 Works Division, Chakia

Bidder
 Appendix

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT (3rd Quarter)

PIU Name :- RWD, WD, CHAKIA

1	Name of the Road -	Bahadurpur chowk to Kataha		
2	Batch No. -	RM/EA/CHA/20/0009		
3	Project ID -	317841000000		
4	Total Length of Road (in KM) -	2.000		
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	2.000		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	28.55023		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.42751		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGATATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUATRER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.42751

Date of Inpection by E/ I or his agent
Prepared by Contractor's self Control unit

Name and Designation of Person inspecting road

Date

Zalir
13/6/22

PAKSeer
13/06/22

(Signature)

[Signature]

Signature of Person inspecting road

Certify by E/ I or his agent
कार्यपालक अभियंता
प्रमण्डल, चकोया

Requisition Form for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
1 Year (3rd Quarter)													
SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT													
To:- Executive Engineer RWD, Works Division Chakia Date: Position :- A E													
Road From:- Bahadurpur Chowk to Kataha (Package No RM/EA/CHA/20/0009) Length of Road :- 2.000 Km Period :- From:- 29.07.2021 To 28.10.2021 Inspector :- A.E RWD Sub Division : Mehsi													
standard Of Work Item		Work	Unit Of Required in each Kilometer										
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment	m ²	Nil	Nil									No Pot Hole Found
OM101	Pothole Patching	m ³	Nil	Nil									Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	Lm	Nil	Nil									No Crack sealing Found
OM103	Crack Sealing												No Loss Of Aggregates (Surface Ravelling) Found
OM104	Surface Treatment	m ²	Nil	Nil									No Bleeding/ Flushing Required
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil									No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil	Nil									No Edge Repair Required
	(c) Crocodile Cracking	m ²	Nil	Nil									
105	Edge Repair	m ²	Nil	Nil									
106	Digouts	m ²	Nil	Nil									
107	Concrete pavement	m ³	N.A	N.A									
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil									No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil									Not Required
	(c) Holding water	Lm	Nil	Nil									No Holding Water Found
OM202	Embankment Repair	M ³	12.71	8.46									
	Other activities (Rain Cuts)		N.A	N.A									Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A									Not Required
OM302	Culvert Cleaning	No	Nil	Nil									Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil									Not Required
	Other activities (Whilw washing)	M ²	Nil	Nil									Not Required

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometers										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	No	Nil	Nil									Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil									Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil									Not Required
	Other activities (Trimming of Grass)	M ²	221.41	101.93									Not Required
OM500	Safety Signage and Road												
OM501	Signs Maintenance	No	Nil	Nil									Not Required
OM502	Guard Stones	Lm	Nil	Nil									Not Required
OM503	Distance Stones	No	Nil	Nil									Not Required
OM504	Road Marking	M ²	Nil	Nil									Not Required
	Other activities												

P. H. San
13/06/22

[Signature]
Executive Engineer,
Works Division, Chakia

Bidder
Appendix

Name of Customer : KRISHNA MAHTO
Name of Work/ Road : BAHADUR PUR CHAUK SE K/ Lab Job number :
Date : 24-04-2022
Section No. : 24

Test Date : 24-04-2022
Machine No : 406
Start S No :
Start E No :
Weather :
Start Location : IR CHAUK SE
End Location : KATAHA
Road Name : OUR PUR CHAUK SE KATAH
Road Type : (A) ASPHALTIC
Side :
Interval
UIV Range : 1057 To 4000
Dist Range : 0 To 2.1
Equation : test


Print

Generate Report and Graph

Redraw Graph

Map View

File : F:\bump report\24.4.2022\krishna mahto\bahadur chauk se katah\24.xlsx Section No. : 24. Eqn : test
Name of Customer : KRISHNA MAHTO , Name of Work/ Road : BAHADUR PUR CHAUK SE KATAHA Lab Job

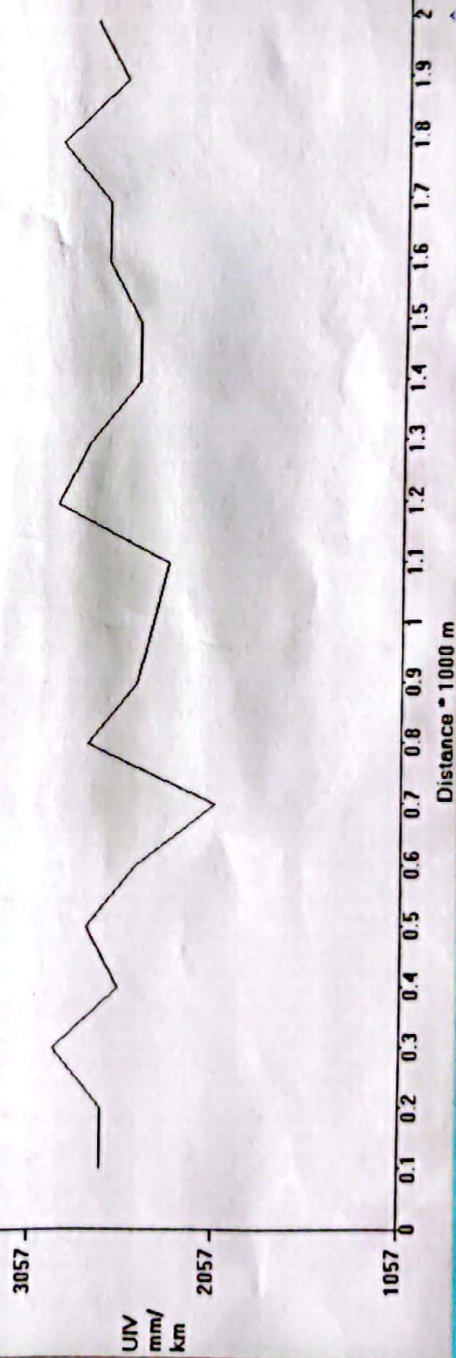

Zuli
24/4/22
NE

PKSaw
24/4/22
NE

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकरीया

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI, TEGORY ROAD	Latitude onglitude	Event	Y = 0 * X ^ 2 + 0.869 * X + 232.9
ROAD- BAHADUR PUR CHAUK SE KATAHA										
24/4/22	14:42:12	24	0.1	280	20.2	2800	2666 G	26.3615	85.14051 Normal	
24/4/22	14:43:0	24	0.1	280	20.2	2800	2666 G	26.36112	85.13963 Normal	X = 2111
24/4/22	14:43:0	24	0.1	310	20.2	3100	2926 G	26.36076	85.1387 Normal	Y = 2067
24/4/22	14:43:22	24	0.1	270	20.2	2700	2579 G	26.36056	85.13776 Normal	
24/4/22	14:43:22	24	0.1	290	20.2	2900	2752 G	26.36038	85.13678 Normal	
24/4/22	14:44:0	24	0.1	260	20.2	2600	2492 G	26.36019	85.13574 Normal	(R) RURAL ROAD
24/4/22	14:44:0	24	0.1	210	20.2	2100	2057 G	26.36001	85.13481 Normal	Good
24/4/22	14:44:0	24	0.1	290	20.2	2900	2752 G	26.35982	85.13382 Normal	Average
24/4/22	14:44:33	24	0.1	260	20.2	2600	2492 G	26.35945	85.13291 Normal	Poor
24/4/22	14:44:33	24	0.1	250	20.2	2500	2405 G	26.35902	85.13199 Normal	4001-5000 >5001
24/4/22	14:45:8	24	0.1	240	20.2	2400	2318 G	26.35882	85.13106 Normal	
24/4/22	14:45:8	24	0.1	310	20.2	3100	2926 G	26.35871	85.13007 Normal	
24/4/22	14:45:43	24	0.1	290	20.2	2900	2752 G	26.35856	85.12909 Normal	
24/4/22	14:45:43	24	0.1	260	20.2	2600	2492 G	26.35834	85.12818 Normal	
24/4/22	14:46:0	24	0.1	260	20.2	2600	2492 G	26.35793	85.12724 Normal	
24/4/22	14:46:19	24	0.1	280	20.2	2800	2666 G	26.3575	85.12635 Normal	
24/4/22	14:46:19	24	0.1	280	20.2	2800	2666 G	26.3569	85.12564 Normal	
24/4/22	14:46:19	24	0.1	310	20.2	3100	2926 G	26.35623	85.125 Normal	
24/4/22	14:47:0	24	0.1	270	20.2	2700	2579 G	26.35583	85.12418 Normal	
24/4/22	14:47:0	24	0.1	290	20.2	2900	2752 G	26.35538	85.12333 Normal	
TOTAL							52356			
AVERAGE							2617.8			

AKSAR
24/4/22
AF

24/4/22
AF

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, चकीबो
