

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 588 मकु

रक्सौल, / दिनांक :- 06/06/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।


अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।



Standard Format For Roads Quarterly Statement (1st Quarter)

PIU Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	PWD Road at Barwa to Maghi		
2	Batch No.	RM/EA/RAX/20/0001		
3	Project ID	317851032000		
4	Total Length of Road (In Km)	2.580		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	2.580		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	26.89605		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.34480		
Compliance Criteria	Standard Job Description	Non Compliance		
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	Reduction Payment [6] = [3]/[1]*[2]*[4]
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0
IV	Signage and Road Safety	1	10%	0.05212
V	Vegataion	1	5%	0.02606
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.07819
To be Paid for the Quarter / Demand (In Lakh) [6]				1.26662

Date of Inspection by E/I or his agent 05/06/22

Prepared by Contractor's self Control Unit

Sanjay Kumar Asst. Engineer
Name and Designation of person inspecting road

Date: 5/6/22

Signature of person inspecting road

(Signature)

Certify by E/I [Signature] Date 5/6/22

1st Quarter Summary of Ordinary Maintenance Inspection Report

To: Maghi

Length of Road. 2.580 Km

Period: From 02.05.2021 to 01.08.2021

Inspector: A.E., RWD, Works Sub Division, Adapur

Position Good

Date ... 05/05/22 ...

[illegible]

Standard Work Item		Work	Unit of work required in each kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA								Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil								Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil								Not Required
	Other activities												Not Required
OM400 Vegetation													
	Grass Control												Not Required
OM401	(a) Roadside General Tidy	Ha	Nil	Nil	Nil								Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM502	Guard stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Markings	No	Nil	Nil	Nil								Not Required
	Other activities												

M/s ANSAR CONSTRUCTION

Abdul Hafeez Ansari
Managing Partner

Bidder

Appendix

10/11/22
5/10/22
A.E.

RWD, Works Division, Raxaul

Executive Engineer,

Chandra
21/10/22

Name of Road:-PWD Path To Barwa Se Maghi
Name of Contractor:-M/s Ansar Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR UIV	CATEGORY	Latitude	ongitude	Event
9/3/22	16:43:22	63	0.1	220	0	2200	ROAD	26.9276	84.89997	Normal
9/3/22	16:43:50	63	0.1	320	10.1	3200		26.92674	84.8999	Normal
9/3/22	16:44:20	63	0.1	340	10.1	3400		26.92583	84.89981	Culvert
9/3/22	16:44:52	63	0.1	320	10.1	3200		26.92497	84.89973	Normal
9/3/22	16:45:20	63	0.1	300	10.1	3000		26.92404	84.89968	Normal
9/3/22	16:45:48	63	0.1	320	10.1	3200		26.92317	84.89973	Curve
9/3/22	16:46:13	63	0.1	320	10.1	3200		26.92261	84.89919	Normal
9/3/22	16:46:38	63	0.1	250	10.1	2500		26.92221	84.89852	Normal
9/3/22	16:47:10	63	0.1	350	10.1	3500		26.92142	84.8981	Normal
9/3/22	16:47:41	63	0.1	290	10.1	2900		26.92063	84.89759	Speed Breaker
9/3/22	16:48:8	63	0.1	340	20.2	3400		26.91987	84.89715	Normal
9/3/22	16:48:39	63	0.1	260	30.3	2600		26.91903	84.89697	Normal
9/3/22	16:49:9	63	0.1	250	30.3	2500		26.91816	84.897	Normal
9/3/22	16:49:35	63	0.1	300	30.3	3000		26.91731	84.89635	Normal
9/3/22	16:50:4	63	0.1	250	30.3	2500		26.91651	84.89591	Normal
9/3/22	16:50:34	63	0.1	310	30.3	3100		26.91567	84.8954	Normal
9/3/22	16:51:5	63	0.1	350	20.2	3500		26.91488	84.89502	Normal
9/3/22	16:51:39	63	0.1	320	10.1	3200		26.91421	84.89444	Normal
9/3/22	16:52:5	63	0.1	300	10.1	3000		26.91406	84.89372	Normal
9/3/22	16:52:35	63	0.1	300	10.1	3000		26.91336	84.89325	Normal
9/3/22	16:53:0	63	0.1	310	20.2	3100		26.91244	84.89308	Normal
9/3/22	16:53:25	63	0.1	300	20.2	3000		26.91156	84.8933	Curve
9/3/22	16:53:58	63	0.1	340	20.2	3400		26.91085	84.89369	Normal
9/3/22	16:54:31	63	0.1	290	20.2	2900		26.91017	84.89382	Normal
9/3/22	16:54:59	63	0.1	300	20.2	3261		26.90932	84.89352	Normal
9/3/22	16:55:29	63	0.1	250	30.3	2500		26.91816	84.89700	Normal
		Total IRI		80940						
		Average IRI		3113.077						

$$Y = 0 * X^4 + 2 * 0.998 * X + 109.5$$

$$X = 3261$$

$$Y = 3363$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

9/13/22
J.E.

9/13/22
A.E.

9/13/22
K.611/1/22

Name of Customer : M/S Ansar Construction
 Name of Work : PWD Path To Barwa Se Maghi
 Road :
 Lab Job number : 22
 Date : 09-03-2022
 Section No. : 63

Test Date : 09-03-2022
 Machine No : 378
 Start S No : 0.0000m
 Start E No : 2.580
 Weather : Normal
 Road Name : PWD Path To Barwa Se Maghi
 Road Type : (R) RURAL ROAD
 Side :
 Interval :
 UIV Range : 1305 To 5000 mm/km
 Dist Range : 0 To 27 01 1000 m
 Start Location : PWD Path
 End Location : Barwa Se Ma
 Equation : $Y = 0.4X^2 + 0.998X + 109.5$


Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\RWD-ATTM\Desktop\Bump Motihari\Excel 09.03.2022\PWD Path To Barwa Se Maghi\090316.xls.

Name of Customer : M/S Ansar Construction, Name of Work/Road : PWD Path To Barwa Se Maghi, Lab Job number

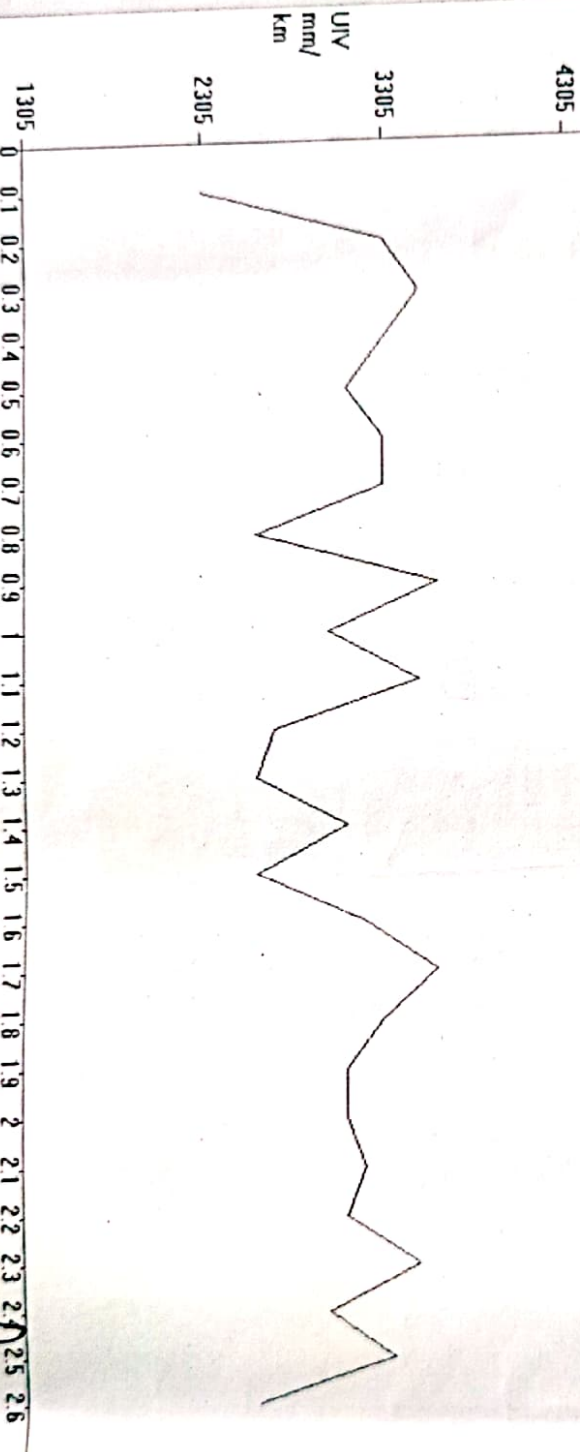



Distance * 1000 m

Amr
 9/3/22
 J.E.

Amr
 09/03/22
 J.E.

Amr
 09/03/22
 J.E.

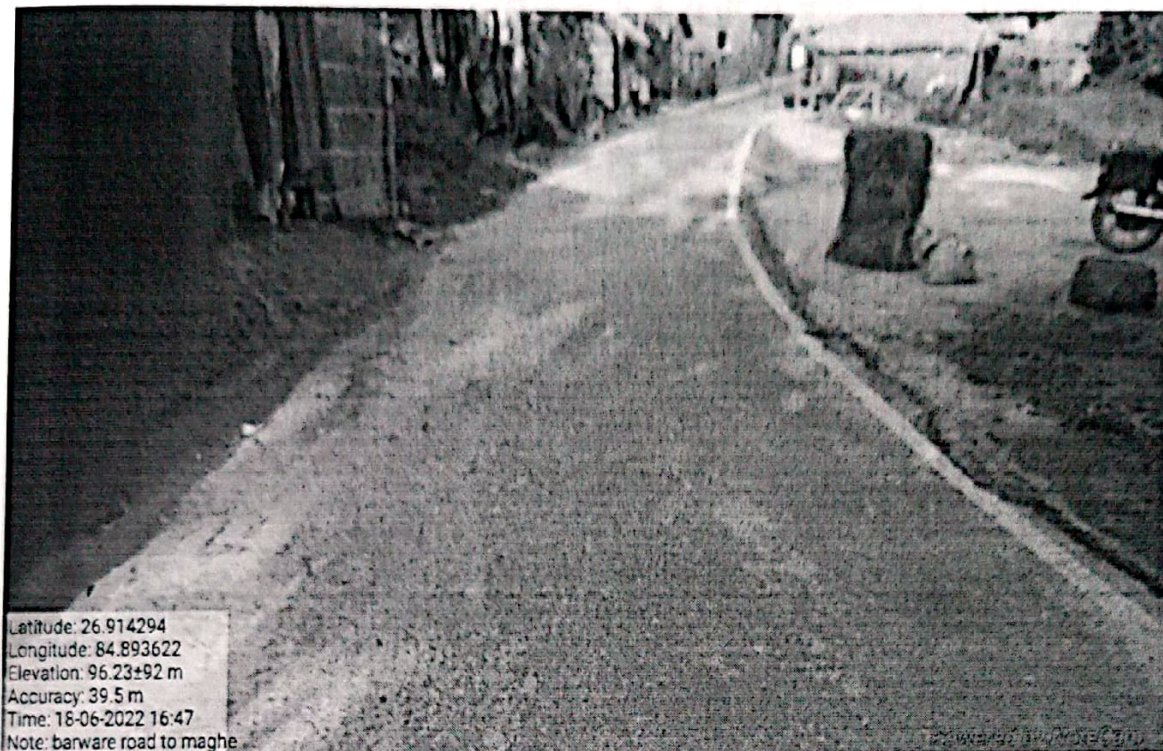

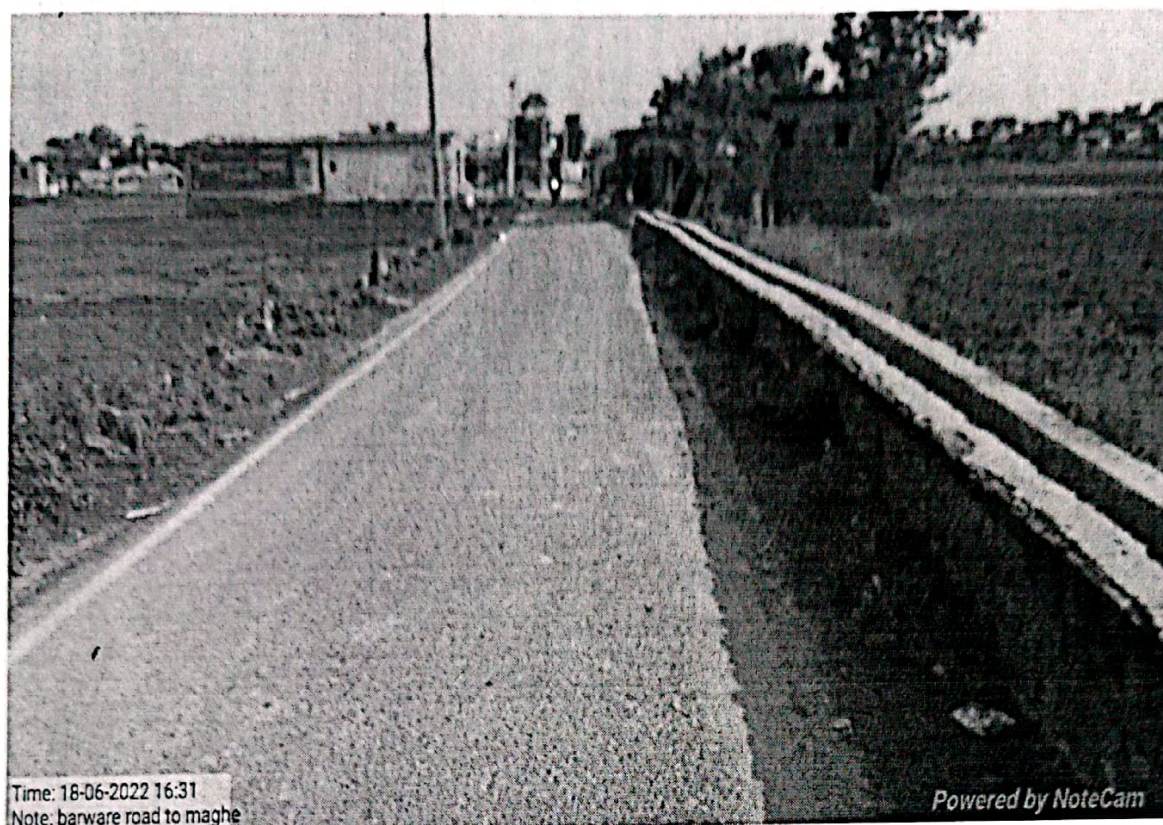

Time: 18-06-2022 16:31
Note: barware road to maghe

Powered by NoteCam



Time: 18-06-2022 16:43
Note: barware road to maghe

Powered by NoteCam



Time: 18-06-2022 16:46
Note: barware road to maghe

Powered by iVee.com



Time: 18-06-2022 16:38
Note: barware road to maghe
