

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....1225

दिनांक 24/06/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2022-23 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 14.64677 (चौदह लाख चौसठ हजार छह सौ सतहतर) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन



24.06.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- Muzaffarpur East-1

Name of Works Division:- Muzaffarpur East-I				Actual Date of Completion	AA Details		Agreement							Actual Maintenance Expenditure						Length as per Bump Report	IRI As per bump Report	Current Maintenance Demand							Remarks	
Road Details					Main Work Amount (in Lakh	Maintenan ce Amount (in lakh)	Main Work Amount (in Lakh)	Agre emen t-1	Agree ment-2	Agree ment-3	Agreem ent-4	Agree ment-5	Total Maintenan ce	Length (in KM)	1st. Year Mainte nance	2nd. Year Mainte nance	3rd. Year Mainte nance	4th Year Mainte nance	5th Year Mainte nance			Total Maintan ance Expendit ure	1st QTR Maintena nce	2nd QTR Mainten ance	3rd QTR Mainte nance	4th QTR Mainte nance	5th QTR Mainte nance	6th QTR Mainten ance		Total
Sl. No.	Name of Raods	Batch No.	Project ID		6	7	8	9	10	11	12	13	14	15	16	17	18	19	20			21	22	23	24	25	26	27		28
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
1	GORIGAMA DIH PMGSY ROAD TO GORIGAMA VILLAGE	RM/MU/MU Z/19/0002	10108643	02.07.2020	29.95900	12.60100	26.54500	0.76852	1.43192	3.20406	2.19254	3.74218	11.33922	0.900	0.000	0.000	0.000	0.000	0.000	0.000	0.900	2764.85	0.56696	0.56696	0.56696	0.56696	0.56696		2.83481	
2	Narayanpur - Narayanpur Path	RM/MU/MU Z/19/0002	NEA22000223	20.05.2020	34.71300	20.40000	30.51500	1.25377	2.30209	5.17595	3.56619	6.03969	18.33769	1.450	0.000	0.000	0.000	0.000	0.000	0.000	1.450	2648.86	0.91688	0.91688	0.91688	0.91688	0.91688	0.91688	5.50131	
3	REO ROAD - GORIGAWAN DIH	RM/MU/MU Z/19/0002	NEA220002304	03.07.2020	42.93800	28.07400	37.99600	1.72430	3.19622	7.10485	4.88678	8.33049	25.24264	2.000	0.000	0.000	0.000	0.000	0.000	0.000	2.000	2662.00	1.26213	1.26213	1.26213	1.26213	1.26213		6.31066	
Total -----																													14.64677	


 24.06.22
 Executive Engineer
 R.W.D. Works Division
 Muzaffarpur East-1

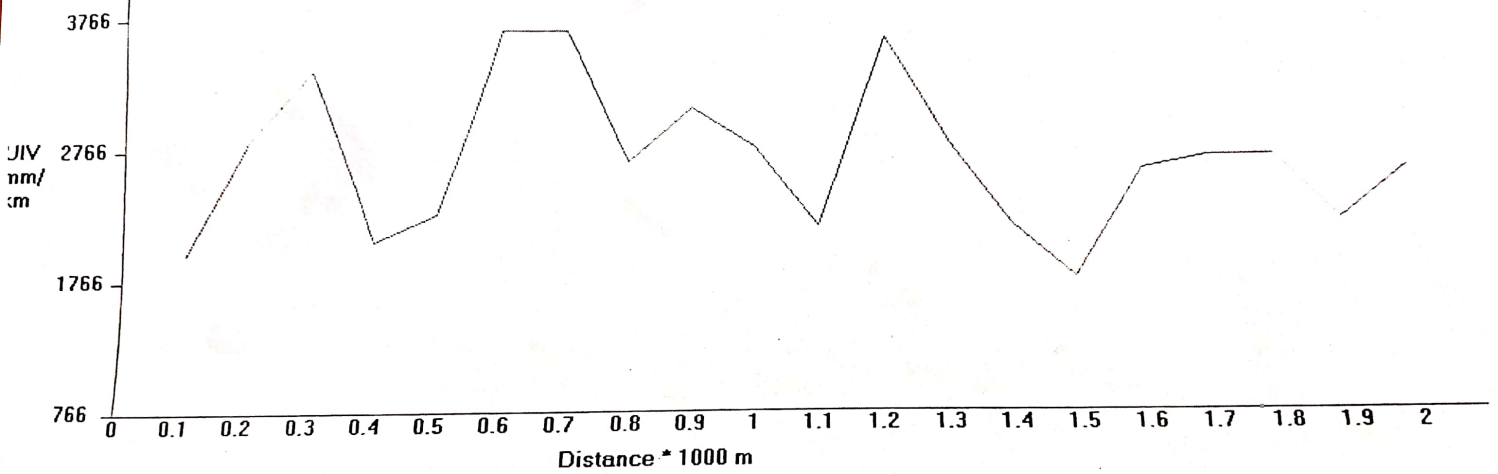
Road Name:-REO Road to Gorigawan Dih

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEG ORY ROAD	IRI	Latitude	Longitu de	Event	
													$Y = 0 * X^2 + 0.989 * X - 13.58$
9/1/22	11:45:0	62	0.1	200	0	2000	1964	G	2.76	26.18538	85.67137	Normal	X = 2200
9/1/22	11:45:27	62	0.1	290	20.2	2900	2854	G	3.85	26.19463	85.67255	Normal	Y = 2563
9/1/22	11:45:27	62	0.1	340	20.2	3400	3349	G	4.44	26.20368	85.6734	Normal	
9/1/22	11:46:0	62	0.1	210	30.3	2100	2063	G	2.88	26.2128	85.67575	Normal	
9/1/22	11:46:2	62	0.1	230	30.3	2300	2261	G	3.13	26.22078	85.67978	Normal	(R) RURAL ROAD
9/1/22	11:46:2	62	0.1	370	40.4	3700	3645	G	4.79	26.22922	85.6848	Normal	Good Average Poor
9/1/22	11:46:2	62	0.1	370	30.3	3700	3645	G	4.79	26.23755	85.68888	Speed Brez	<4000 4001-5000 >5001
9/1/22	11:46:37	62	0.1	270	30.3	2700	2656	G	3.61	26.24402	8.69493	Normal	
9/1/22	11:46:37	62	0.1	310	30.3	3100	3052	G	4.09	26.2517	85.69865	Normal	
9/1/22	11:47:0	62	0.1	280	30.3	2800	2755	G	3.73	26.28318	85.7207	Normal	
9/1/22	11:47:12	62	0.1	220	30.3	2200	2162	G	3	26.29605	85.72473	Normal	
9/1/22	11:47:12	62	0.1	360	30.3	3600	3546	G	4.67	26.30597	85.7249	Speed Breaker	
9/1/22	11:47:12	62	0.1	280	30.3	2800	2755	G	3.73	26.32347	85.7244	Normal	
9/1/22	11:47:47	62	0.1	220	30.3	2200	2162	G	3	26.33328	85.72407	Normal	
9/1/22	11:48:0	62	0.1	180	30.3	1800	1766	G	2.51	26.34255	85.72407	Normal	
9/1/22	11:48:0	62	0.1	260	30.3	2600	2557	G	3.49	26.3443	85.73063	Normal	
9/1/22	11:48:22	62	0.1	270	10.1	2700	2656	G	3.61	26.34248	85.74107	Normal	
9/1/22	11:48:22	62	0.1	270	10.1	2700	2656	G	3.61	26.33997	85.7502	Normal	
9/1/22	11:49:0	62	0.1	120	20.2	2275	2173	G	1.74	26.33812	85.7601	Normal	
9/1/22	11:49:0	62	0.1	120	20.2	2200	2563	G	1.74	26.3357	85.7702		
					AVG:-	2662.00							

24/06/22
55

24.06.22

File : C:\Users\BRRDA9\Desktop\Ram Swarath Ray\REO Road to Gorigawan Dih1.xls, Section No. 62, Egn Y = 0
Name of Customer : Ram Swarath Ray, Name of Work/ Road : REO Road to Gorigawan Dih, Lab Job number



Handwritten signature
24/06/22
JR

Handwritten signature
24.06.22

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
Name of Works Division :- Muzaffarpur East-I													
Government of Bihar OM01 Rural works Department			SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT										
Road From- REO ROAD - GORIGAWAN DIH Length of Road: 2.00 KM Period : From Inspector: A.E RWD Sub Division, Saraiya			To: Executive Engineer RWD Works Division Muzaffarpur East-1 Position: A.E			Date:							
Standard Work item	Work	Units of work required in each kilometre										Comments	
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil							Not Required
	OM 400 Vegetation												
OM401	Grass Contorol												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and shrub management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Aplicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Aplicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

समस्वाधी ११५
Bidder

४४०८
२५/०६/२२
जेर Appendix

२५.०६.२२
Executive Engineer, Rural Work Department, Work
Division, Muzaffarpur East I

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	REO ROAD - GORIGAWAN DIH
2	Batch No.	RM/MU/MUZ/19/0002
3	Project ID	NEA220002404
4	Total Length of Road (in Km)	2.00
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	2.00
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	25.24264
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.26213

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.00000
				1.26213

Date of inspection by E/I or his agent Prepared by Contractor's self Control unit

24/06/22
JK

Name and Designation of person inspecting road
(Signature)

24.06.22

Date

Signature of person inspecting road

Certify by E/I (signature) Date
