

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....37/813

दिनांक.....05/03/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2021-22 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2021-22 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार **34.10594** (चौतीस लाख दस हजार पाँच सौ चौरानबे) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन

 5.3.22


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Maintenance Requisition Formate for Scheme Head- MR (3


Name of Works Division:- Muzaffarpur East-1

Road Details				Actual Date of Completion	AA Details		Agreement					
Sl. No.	Name of Raods	Batch No.	Project ID		Main Work Amount (in Lakh	Maintenan ce Amount (in lakh)	Main Work Amount (in Lakh)	Agreem ent-1	Agreem ent-2	Agree ment-3	Agreem ent-4	Agreem ent-5
1	2	3	4	5	6	7	8	9	10	11	12	13
1	Improvement of Gobindpur main road to Basaitha main Road Via - Gobindpur Village road	RM/MU/MU Z/19/0001	31507201009	17/12/2020	43.7160	27.3800	38.4090	1.7027	3.1705	6.8952	4.7606	8.0885
2	Ragho Chapra - Gosai Chapra	RM/MU/MU Z/19/0001	31507202241	17/12/2020	26.6430	16.2550	25.9980	1.0467	1.8472	4.0962	2.8191	4.8167

Road Details				AA Details				Agreement							Actual Maintenance Expenditure							Current Maintenance Demand			Remarks		
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenan ce Amount (in lakh)	Main Work Amount (in Lakh)	Agreem ent-1	Agreem ent-2	Agree ment-3	Agreem ent-4	Agreem ent-5	Total Maintenance ce	Length (in KM)	1st. Year Maint enanc e	2nd. Year Maint enanc e	3rd. Year Maint enanc e	4th Year Maint enanc e	5th Year Maint enanc e	Total Maint enanc e	Length as per Bump Report	IRI As per Bump Report	1st QTR Mainte nance	2nd QTR Mainte nance		3rd QTR Main tenan ce	Total
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
7	Manikpur - Abubachak	RM/MU/MU/219/0001	NEA220002280	17/12/2020	40.2990	24.5750	35.8920	1.5404	2.7786	6.2229	4.2806	7.2659	22.0884	1.75	0.00	0.00	0.00	0.00	0.00	0.00	1.750	1859.00	1.10442	1.10442	1.10442	3.31327	
8	Bakhta - Damodarapur Chhapra	RM/MU/MU/219/0001	NEA220002351	17/12/2020	111.9810	60.7300	99.2270	3.6888	6.9347	15.4330	10.6057	17.9226	54.5848	4.35	0.00	0.00	0.00	0.00	0.00	0.00	4.350	2258.00	2.72924	2.72924	2.72924	8.18772	


 Executive Engineer
 R.V.D. Works Division
 Muzaffarpur East-1

File: C:\Users\BRRDA42\Desktop\MIS_Upload\BumpTest\29121250.Xls. Section No.: 55. Eqn: $Y = 0.0 \cdot X^{1.2} +$
 Name of Customer: Name of Work/Road: Lab Job number:

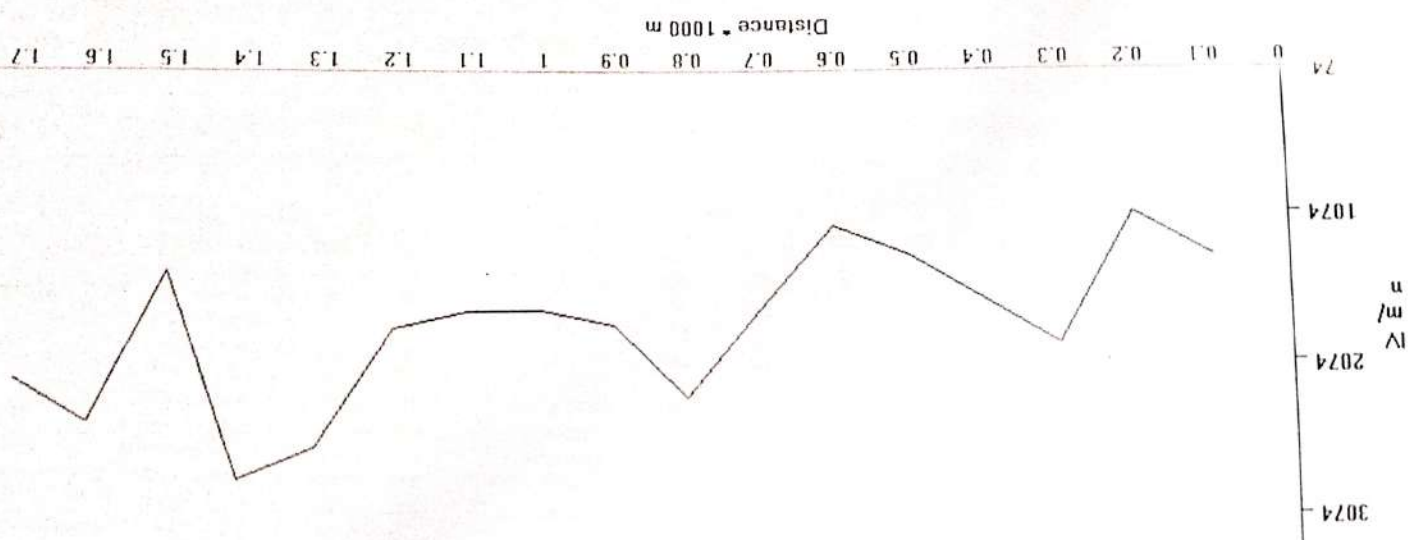

Handwritten signature
 29/12/2024
 16

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	IRI, TEGORY	Latitude	ongitude	Event
29/12/21	12:43:0	55	0.1	140	0	1400	1371 G	2	26.4752	85.12793 Normal
29/12/21	12:43:0	55	0.1	110	10.1	1100	1074 G	1.61	26.4632	85.12896 Curve
29/12/21	12:43:35	55	0.1	200	10.1	2000	1964 G	2.76	26.409	85.12944 Normal
29/12/21	12:44:0	55	0.1	170	20.2	1700	1667 G	2.38	26.406	85.13045 Curve
29/12/21	12:44:9	55	0.1	140	10.1	1400	1371 G	2	26.3172	85.13056 Curve
29/12/21	12:44:9	55	0.1	120	10.1	1200	1173 G	1.74	26.3003	85.13153 Normal
29/12/21	12:45:0	55	0.1	180	10.1	1800	1766 G	2.51	26.2208	85.13192 Normal
29/12/21	12:45:20	55	0.1	240	10.1	2400	2360 G	3.25	26.147	85.13244 Normal
29/12/21	12:46:0	55	0.1	190	10.1	1900	1865 G	2.63	26.1305	85.13342 Normal
29/12/21	12:46:30	55	0.1	180	10.1	1800	1766 G	2.51	26.1243	85.13446 Normal
29/12/21	12:47:6	55	0.1	180	10.1	1800	1766 G	2.51	26.1313	85.1354 Normal
29/12/21	12:47:6	55	0.1	190	10.1	1900	1865 G	2.63	26.1938	85.13604 Normal
29/12/21	12:48:0	55	0.1	270	10.1	2700	2656 G	3.61	26.1972	85.13685 Normal
29/12/21	12:48:16	55	0.1	290	10.1	2900	2854 G	3.85	26.1985	85.13786 Normal
29/12/21	12:48:16	55	0.1	150	10.1	1500	1469 G	2.13	26.2227	85.13857 Normal
29/12/21	12:49:0	55	0.1	250	10.1	2500	2458 G	3.37	26.2322	85.13953 Normal
29/12/21	12:49:27	55	0.1	220	10.1	2200	2162 G	3	26.2297	85.14051 Normal
AVG:-							1859			

$$Y = 0 * X^2 + 0.989 * X - 13.58$$

$$X = 2200$$

$$Y = 2162$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

Manikpur
29/12/2021
JE

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-1

Government of Bihar

OM01

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From-Manikpur - Abubachak

Length of Road: 1.75 KM

Period : From.....

Inspector: A.E RWD Sub Division, Saraiya

To: Executive Engineer
RWD Works Division Muzaffarpur East-1

Position: A.E

Date:

Standard Work item			Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM100 Sealed Pavement														
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.	
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found	
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found	
OM104	Surface Treatment												No Loss of Aggregate (Surface Ravelling) found	
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required	
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found	
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Edge Repair Required	
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil								
OM106	Digouts	m2	N/A	N/A	N/A	N/A								
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A								
Other activities		Lm												
OM200 Shoulder														
OM201	Unsealed Shoulder	No											No Edge Drop off Required	
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.	
	(b) Roughness, Securing or Potholes	Lm	Nil	3%	2%	Nil							No Holding water found	
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Embankment Repair Required	
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.	
	Other Activities (Raincut)		3%	1%	2%									
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required	
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time	
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required	

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil													Not Required
	OM 400 Vegetation																		
	Grass Contorol																		
OM401	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil													Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil													Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil													Not Required
OM402	Cutting trees	No	Nil	Nil	Nil	Nil													Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil													Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil													Not Required
OM500	Safety Signage and Road																		Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil													Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A													Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A													Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil													Not Required
	Other activities																		

Bidder

Handwritten signature and date: 23.03.22

Executive Engineer, Rural Work Department, Work Division, Muzaffarpur East I
