

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक.....384/3130

दिनांक.....5/03/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।


विषय: नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2021-22 में अनुरक्षण मद में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण नीति 2018 अंतर्गत वित्तीय वर्ष 2021-22 में अनुरक्षण मद में व्यय हेतु संलग्न विवरणी के अनुसार 41.87850 (एकतालिस लाख सतासी हजार आठ सौ पचास) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजन


5.3.22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Name of Works Division:- Muzaffarpur East-1

Executive Engineer
R.W.D. Works Division
Muraffarpur East-I

Name Of Road: NH28 culvert - barmatpur											
Date	Time	Section	Length	Bumps	Speed	OR n	MM/Km	TEGORY	Latitude	ongitude	Event
No.			in km	in mm	Rate	mm/km	UIV	ROAD			
29/11/21	13:1:0	71	0.1	300	0	3000	2953	G	26.10351	85.37114	Normal
29/11/21	13:1:0	71	0.1	150	10.1	1500	1469	G	26.10369	85.3702	Normal
29/11/21	13:1:34	71	0.1	250	10.1	2500	2458	G	26.10368	85.36921	Normal
29/11/21	13:2:9	71	0.1	140	20.2	1400	1371	G	26.10349	85.36822	Normal
29/11/21	13:2:9	71	0.1	190	10.1	1900	1865	G	26.10305	85.36758	Normal
29/11/21	13:2:44	71	0.1	240	20.2	2400	2360	G	26.1023	85.36699	Normal
29/11/21	13:3:0	71	0.1	190	10.1	1900	1865	G	26.10156	85.36648	Normal
29/11/21	13:3:20	71	0.1	250	10.1	2500	2458	G	26.10128	85.36566	Normal
29/11/21	13:3:55	71	0.1	250	10.1	2500	2458	G	26.10193	85.36542	Normal
29/11/21	13:4:0	71	0.1	190	20.2	1900	1865	G	26.10285	85.36567	Normal
29/11/21	13:4:0	71	0.1	240	20.2	2400	2360	G	26.10372	85.36554	Normal
29/11/21	13:4:30	71	0.1	200	10.1	2000	1964	G	26.10399	85.36456	Curve
29/11/21	13:5:5	71	0.1	240	10.1	2400	2360	G	26.10359	85.36375	Normal
29/11/21	13:5:5	71	0.1	190	10.1	1900	1865	G	26.10271	85.363	Normal
29/11/21	13:5:41	71	0.1	170	20.2	1700	1667	G	26.10182	85.36308	Normal
29/11/21	13:6:0	71	0.1	320	20.2	3200	3151	G	26.10096	85.36276	Normal
29/11/21	13:6:16	71	0.1	260	20.2	2600	2557	G	26.10008	85.36236	Normal
29/11/21	13:6:16	71	0.1	260	10.1	2600	2557	G	26.99192	85.3621	Normal
29/11/21	13:7:0	71	0.1	280	20.2	2800	2755	G	26.98435	85.36168	Normal
29/11/21	13:7:0	71	0.1	200	20.2	2000	1964	G	26.98173	85.36079	Normal
29/11/21	13:7:27	71	0.1	140	20.2	1400	1371	G	26.98122	85.3598	Normal
29/11/21	13:7:27	71	0.091	230	10.1	2527	2485	G	26.9816	85.3588	Normal
Avg						2189.9					

$$Y = 0 * X^2 + 0.989 * X - 13.58$$


$$X = 2527$$

$$Y = 2485$$

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

Amil Kumar
9/3/2022
16

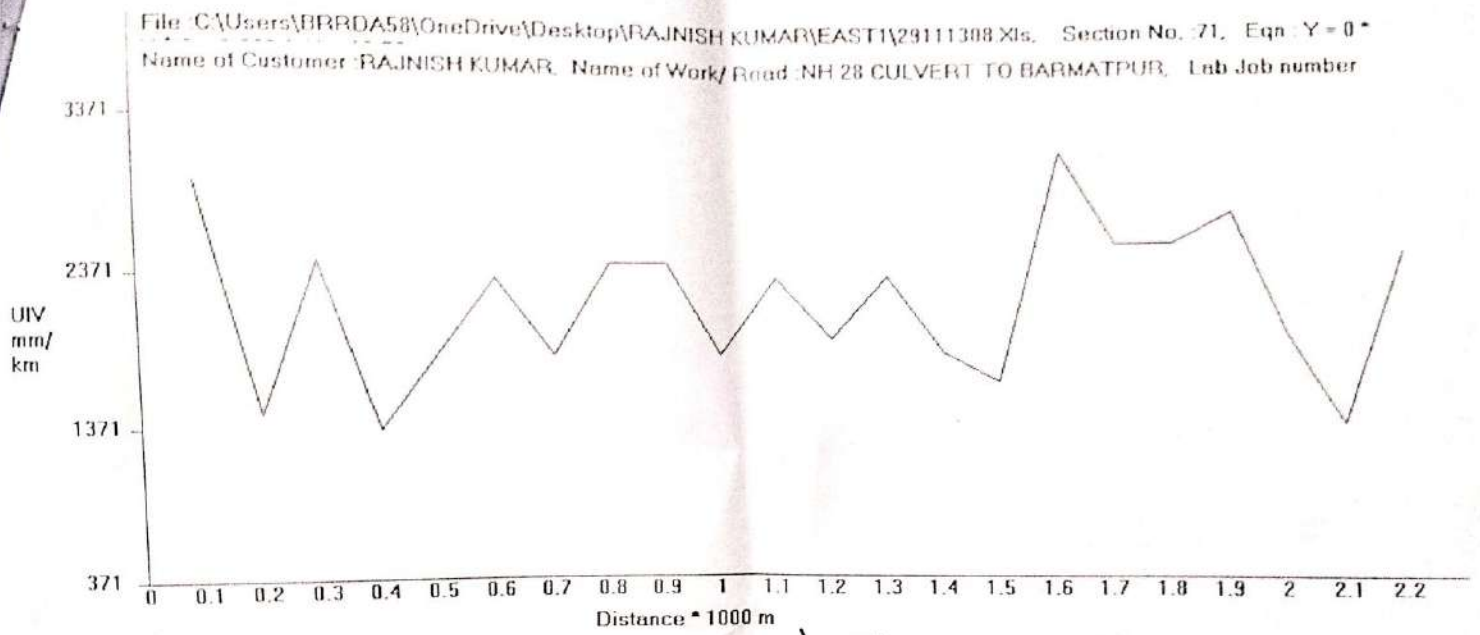

Rajkumar
4/3/2022
JS

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur East-1

Government of Bihar
OM101
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From - ~~Daska~~ - NH28 culvert - barmatpur
Length of Road: 2.30 KM
Period : From.....
Inspector: A.E RWD Sub Division, Mushari

To: Executive Engineer
RWD Works Division Muzaffarpur East-1
Position: A.E

Date:

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil							Not Required
	OM 400 Vegetation												
	Grass Control												
OM401	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and shrub management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Applicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Applicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

रजनीश कुमार
Bidder

Appendix
4/3/2022
JG

Executive Engineer, Rural Work Department, Work
Division, Muzaffarpur East I
