

कार्यपालक अभियन्ता का कार्यालय,

ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अनु०

/ हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : E E RWD WORKS DIVISION - HATHUA

1st Quarter

1	Name of the Road	Buxihamesh To Mirzapur		
2	Batch No.	RM/GC/HAT/M/0007		
3	Project ID	3/107001014		
	Total Length of Road (in Km)	1.550 Km		
4	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	1.550 Km		
5	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
6	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	13.82100		
7	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.69105		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	00
II	SHOULDERS AND EMBANKMENTS	00	10%	00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	00
IV	SIGNAGE AND ROAD SAFETY	00	10%	00
V	VEGETATION	00	5%	00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

[Signature]
J.E

Name and Designation of person inspecting road

[Signature]
(Signature) 10/2/22

Date 10.2.2022

Signature of person inspecting road

Certify by E/I [signature] Date:-

Name of work : Baridhanesh to Mirzapur
 Name of customer : Maa Ambey Construction


(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMPI(cm)	Speed(Km/Hr)	Ull(mm/Km)	Corrected Ull (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
15/03/22	08:25:49	29	0	0	0.0 cm	28.5 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3168281	N	84.2856002	E	Normal
15/03/22	08:37:19	29	100	100	36.0 cm	11.2 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:37:39	29	100	200	38.0 cm	18.1 Km/Hr	3600.0 mm/Km	3602	4.98	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:38:06	29	100	300	38.0 cm	13.2 Km/Hr	3600.0 mm/Km	3602	4.98	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:38:13	29	100	400	38.0 cm	5.1 Km/Hr	3600.0 mm/Km	3696	5.09	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:38:36	29	100	500	38.0 cm	15.7 Km/Hr	3600.0 mm/Km	3696	5.09	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:38:56	29	100	600	38.0 cm	17.6 Km/Hr	3600.0 mm/Km	3696	5.09	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:40:29	29	100	700	37.0 cm	11.2 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:41:02	29	100	800	35.0 cm	10.5 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3177175	N	84.2801142	E	Normal
15/03/22	08:41:32	29	100	900	32.0 cm	12.3 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3173113	N	84.2866346	E	Normal
15/03/22	08:42:00	29	100	1000	32.0 cm	12.8 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3170786	N	84.2868111	E	Normal
15/03/22	08:42:28	29	100	1100	31.0 cm	12.7 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.3173342	N	84.2906580	E	Normal
15/03/22	08:42:39	29	100	1200	32.0 cm	29.8 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3175993	N	84.2917337	E	Normal
15/03/22	08:42:47	29	100	1300	21.0 cm	43.2 Km/Hr	2100.0 mm/Km	2211	3.07	Good	26.3174887	N	84.2908560	E	Normal
15/03/22	08:43:03	29	100	1400	30.0 cm	25.8 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3172255	N	84.2831714	E	Normal
15/03/22	08:43:18	29	100	1500	34.0 cm	23.6 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3171606	N	84.2947245	E	Normal
15/03/22	08:44:09	29	100	1600	34.0 cm	6.8 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3168203	N	84.2956400	E	Normal

15/3/22

15/3/22

15/3/22

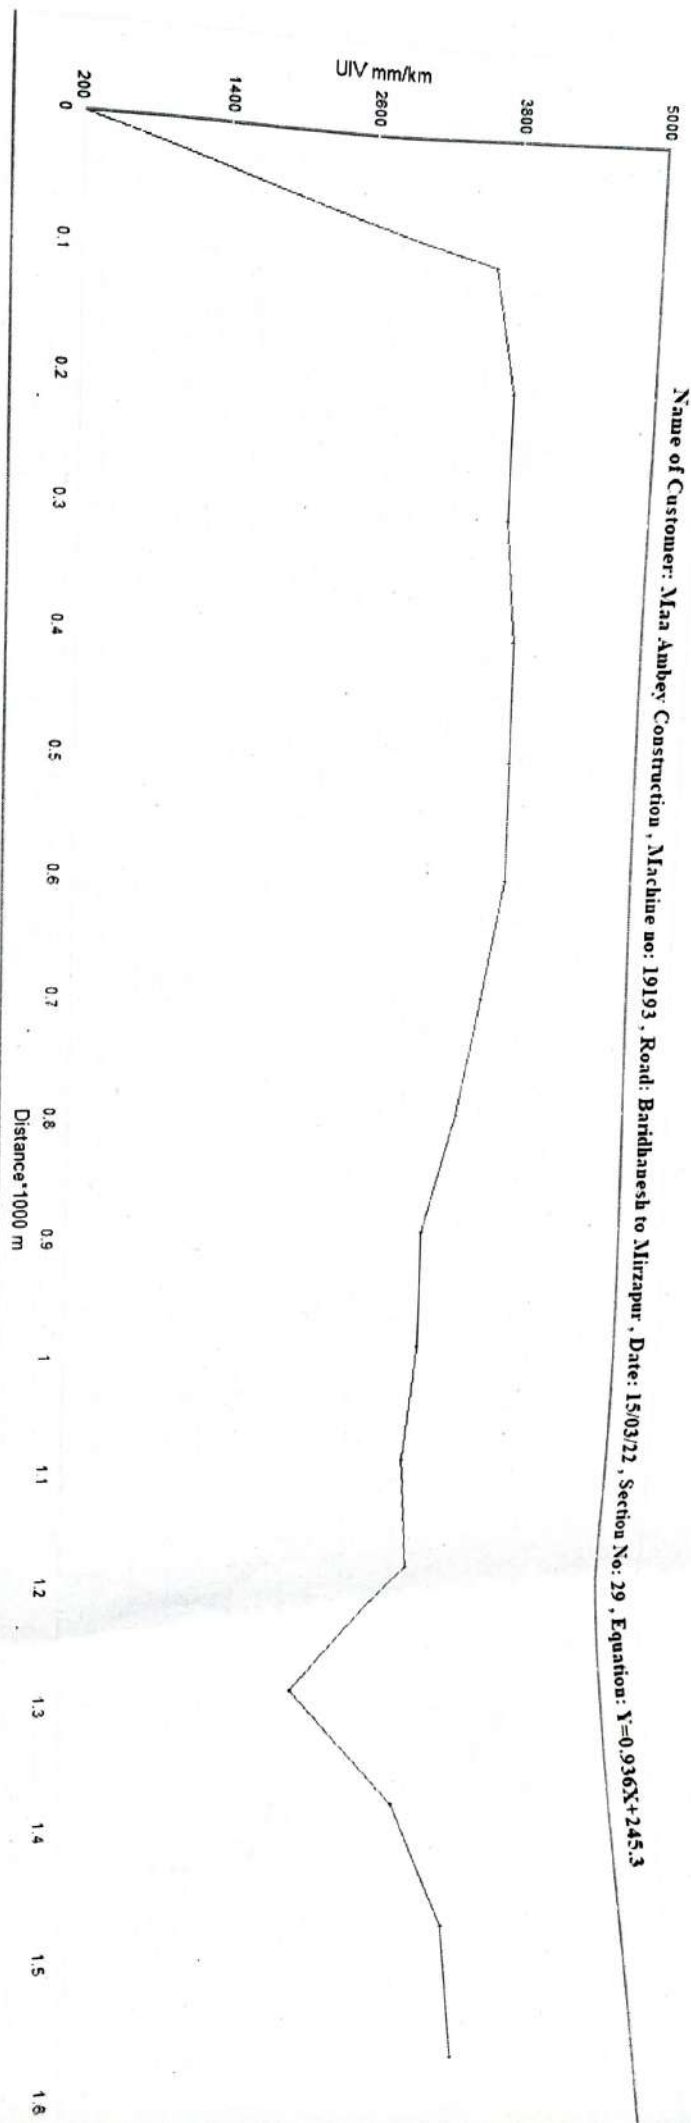

Signature
15/3/22

Signature
15/3/22
AA

Signature
15/3/22
AA

RWD, Works Division Hathua

Requisition Formet for Scheme Head MR (305A) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and Surface Renewal)

1 Year (1st Quarter)

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Bandhanesh to Mirzapur
(Package No. RM/SD/HAT/19/0007)
Length of Road :- 1.55 Km
Inspector :- J.E RWD Sub Division : Hathua

To:-

Executive Engineer
RWD, Works Division Hathua

Date:-

Position :- J.E

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
1	2	3	4	5	6	7	8	9	10				
OM100	Sealed payment	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Port Hole Found.
OM101	Pothole Patching	m ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	LM	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crack sealing Found
OM103	Crack Sealing	LM	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Loss Of Aggregates (Surface Ravelling) Found
	Surface Treatment												No Bleeding/ Flushing Required
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Edge Repair Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil				
105	Edge Repair	m ²	N.A	N.A	N.A	N.A	N.A	N.A	N.A				
106	Digouts	m ³	N.A	N.A	N.A	N.A	N.A	N.A	N.A				
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A	N.A	N.A				
	Other activities												
OM200	Shoulder												No Edge Drop-Off Required
	Unsealed Shoulder	LM	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
OM201	(a) Edge Drop-off	LM	Nil	Nil	Nil	Nil	Nil	Nil	Nil				No Holding Water Found
	(b) Roughness, Scouring or Potholes	LM	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
	(c) Holding water	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
OM202	Embankment Repair		Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
	Other activities (Rain Cuts)												Not Required
OM300	Drainage including culverts major	LM	N.A	N.A	N.A	N.A	N.A	N.A	N.A				Not Required
OM301	Surface Drains & Verge	M ⁰	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil				Not Required
	Other activities(White washing)	M ³	Nil	Nil	Nil	Nil	Nil	Nil	Nil				

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
OM402	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												Not Required

EXECUTIVE ENGINEER RWD WORKS DIVISION HATHUA

15/3/22

15/3/22

15/3/22
