

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- 498 अ० / हथुआ।

दिनांक:- 05/05/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,


कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

1st Quarter


STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : E E RWD WORKS DIVISION - HATHUA

1	Name of the Road	Barampur to Garai Pathi		
2	Batch No.			
3	Project ID			
	Total Length of Road (in Km)	1.40 Km		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	1.40 Km		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	12.526 lakh		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.626 lakh		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	
II	SHOULDERS AND EMBANMENTS	00	10%	
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	
IV	SIGNAGE AND ROAD SAFETY	00	10%	
V	VEGATAJON	00	5%	
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.626 lakh

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit


16/3/22
Name and Designation of person inspecting road

Date

Signature of person inspecting road


16/03/22
(Signature)

Certify by E/I (signature) Date:-

Name of work : Basaipur to Barai Pati	
Name of customer : Maa Ambey Construction	
(R) Rural Road	
Good	Average
< 4000	4001 - 5000
	> 5000
Poor	


Date	Time	Test No	Distance(m)	Total Distance(m)	Bulldoz(cm)	Speed(Km/Hr)	Ultrasonic(mm/Km)	Corrected UI (mm/Km)	RI	Status	Latitude	Direction	Longitude	Direction†	Remarks
27/03/22	21:32:25	9	0	0	0.0 cm	45.9 Km/Hr	0.0 mm/Km	245	0.43	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:45:51	9	100	100	26.0 cm	2.4 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:46:25	9	100	200	26.0 cm	10.3 Km/Hr	2800.0 mm/Km	2679	3.64	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:46:40	9	100	300	33.0 cm	24.0 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:46:52	9	100	400	38.0 cm	26.8 Km/Hr	3900.0 mm/Km	3896	5.09	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:47:04	9	100	500	35.0 cm	30.6 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:47:16	9	100	600	31.0 cm	30.3 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:47:30	9	100	700	30.0 cm	25.9 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:47:43	9	100	800	36.0 cm	27.3 Km/Hr	3600.0 mm/Km	3615	4.76	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:47:57	9	100	900	32.0 cm	25.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:48:11	9	100	1000	36.0 cm	26.4 Km/Hr	3600.0 mm/Km	3602	4.98	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:48:24	9	100	1100	27.0 cm	27.0 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:48:39	9	100	1200	24.0 cm	23.9 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:48:54	9	100	1300	27.0 cm	24.0 Km/Hr	2700.0 mm/Km	2773	3.75	Good	26.5042410	N	84.2403498	E	Normal
27/03/22	22:49:26	9	100	1400	22.0 cm	6.6 Km/Hr	2200.0 mm/Km	2305	3.18	Good	26.5042410	N	84.2403498	E	Normal

27/3/22

27/3/22

27/03/22

Name of Customer: Maa Ambey Construction . Machine no: 19193 . Road: Basarpur to Barai Pati , Date: 27/03/22 , Section No. 09 . Equation: $Y=0.936X+245.3$

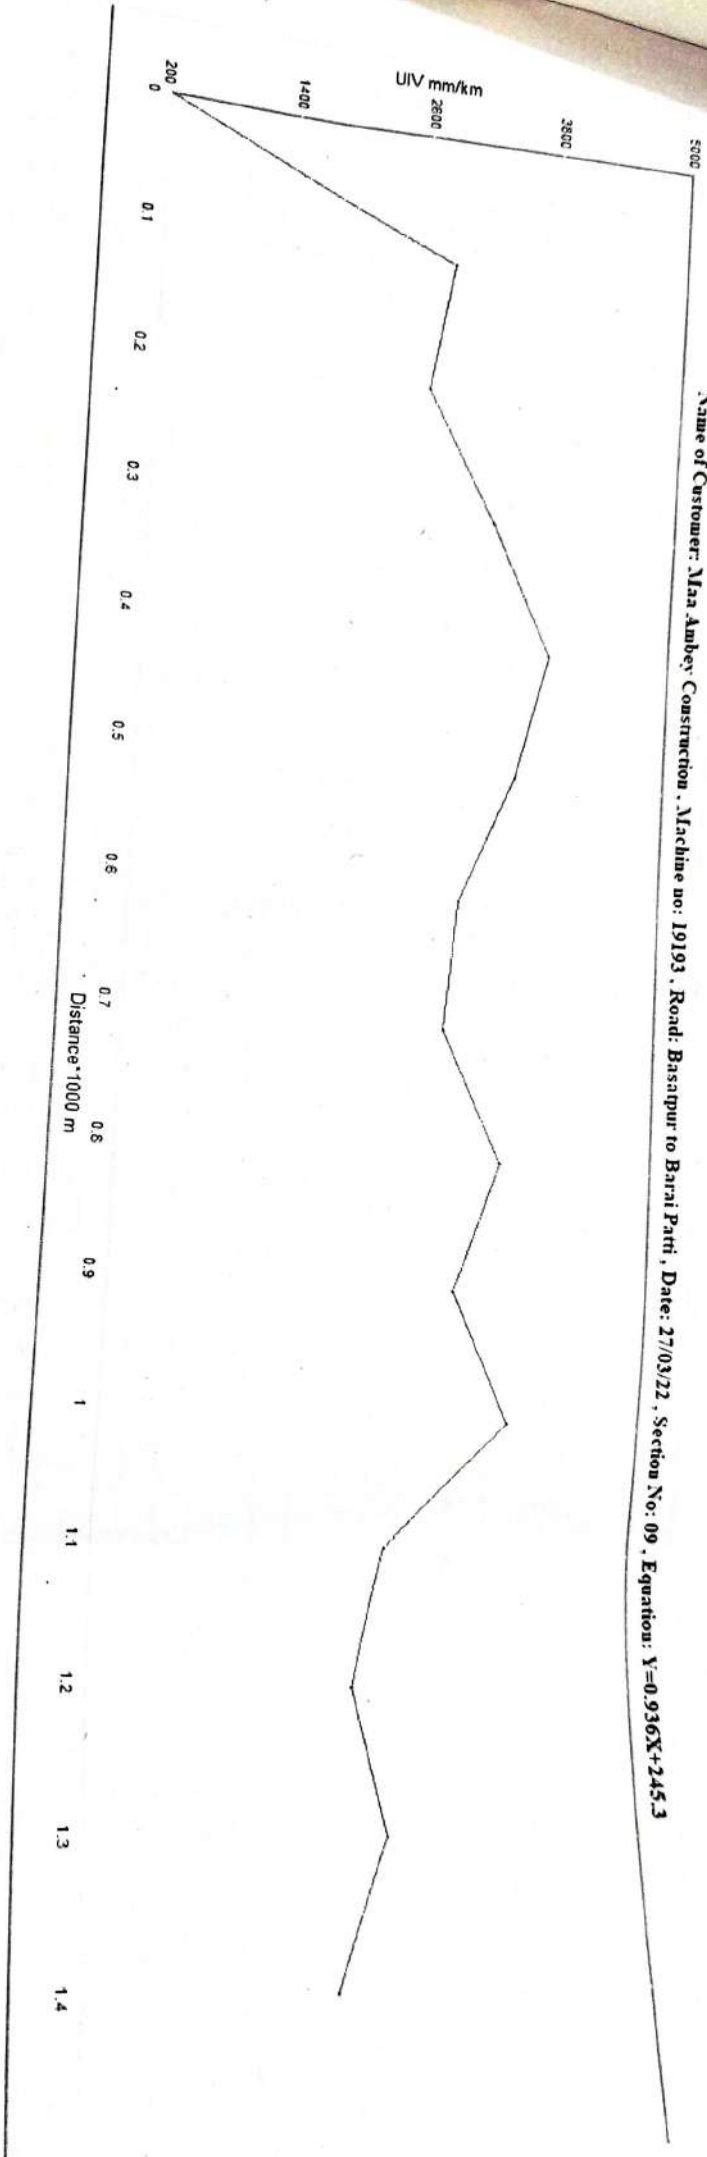

[Signature]
27/3/22
22

[Signature]
27/3/22
22

[Signature]
27/3/22

RWD, Works Division Hathua

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Route From: Barabur to Bara Path
 Package No: RM/ISO/MAI/75/0007
 Length of Road: 1.2 Km
 Inspector: J.E. RWD Sub Division Hathua

To:-
 Executive Engineer
 RWD, Works Division Hathua

Date:

Position: J.E

No.	Standard Of Work Item	Work	Unit Of Required In each Kilometer	1	2	3	4	5	6	7	8	9	10	Comments
OM106	Sealed pavement	Lm												
OM105	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM107	Surface Depression and Rut Patching	m ³	Nil	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM108	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil							No Crack sealing Found
OM109	Surface Treatment													
OM109	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
OM109	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
OM109	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
OM109	Edge Repair	m ³	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
OM109	Shoulders	m ³	N.A	N.A	N.A	N.A	N.A							
OM109	Concrete pavement	m ³	N.A	N.A	N.A	N.A	N.A							
OM109	Other activities													
OM109	Shoulder													
OM109	Unsealed Shoulder													
OM109	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM109	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM109	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding Water Found
OM109	Embankment Repair	m ³	Nil	Nil	Nil	Nil	Nil							Not Required
OM109	Other activities (Rain Cuts)													Not Required
OM109	Drainage including culverts major													Not Required
OM109	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A	N.A							Not Required
OM109	Culvert Cleaning	N/A	Nil	Nil	Nil	Nil	Nil							Not Required
OM109	Culvert and pit Repair	m ³	Nil	Nil	Nil	Nil	Nil							Not Required
OM109	Other activities (White washing)	m ²	Nil	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Comments
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												


 16/13/22

 16/13/22
 P.B.


 16/13/22
