

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल हथुआ।

पत्रांक:- ५१४ अ० / हथुआ।

दिनांक:- ०५/०५/२०२२

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय :- राशि उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सूचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु०- यथोक्त।

विश्वासभाजन,



कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हथुआ।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : E E RWD WORKS DIVISION - HATHUA

1st Quarter

1	Name of the Road	Semraon to Surwaria		
2	Batch No.	RM/60/HAT/19/0012		
3	Project ID	NEA29000690		
	Total Length of Road (in Km)	5.20 KM		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	5.20 KM		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	47.317 Lakh		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	2.365 Lakh		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payments [6] = [3] / [1] * [2] * [4]
		Length Non-Compliant [3]	Weighted value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	00	60%	
II	SHOULDERS AND EMBANMENTS	00	10%	
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	00	15%	
IV	SIGNAGE AND ROAD SAFETY	00	10%	
V	VEGATAION	00	5%	
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				2.365 Lakh

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

Name and Designation of person inspecting road

Date

Signature of person inspecting road

Certify by E/I [signature] Date:-

Name of work : Semraw - Surwaria

Name of customer : Shailcon Construction

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	U/mmm/Km	Corrected U/mmm/Km	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
15/03/22	10:11:31	31	0	0	0.0 cm	4.1 Km/Hr	0.0 mm/Km	245	0.43	Good	26.3596773	N	84.2570221	E	Normal
15/03/22	10:25:06	31	100	100	37.0 cm	7.1 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:25:20	31	100	200	32.0 cm	32.4 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:25:31	31	100	300	24.0 cm	31.3 Km/Hr	2400.0 mm/Km	2492	3.41	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:25:44	31	100	400	32.0 cm	28.2 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:26:05	31	100	500	33.0 cm	16.2 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:26:20	31	100	600	37.0 cm	24.7 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:26:35	31	100	700	30.0 cm	22.4 Km/Hr	3000.0 mm/Km	3053	4.09	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:26:54	31	100	800	31.0 cm	19.8 Km/Hr	3100.0 mm/Km	3147	4.2	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:04	31	100	900	29.0 cm	24.5 Km/Hr	2900.0 mm/Km	2960	3.98	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:20	31	100	1000	35.0 cm	22.5 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:30	31	100	1100	28.0 cm	37.4 Km/Hr	2800.0 mm/Km	2866	3.87	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:38	31	100	1200	25.0 cm	45.0 Km/Hr	2500.0 mm/Km	2560	3.98	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:45	31	100	1300	32.0 cm	48.5 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:52	31	100	1400	33.0 cm	52.6 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:27:59	31	100	1500	33.0 cm	50.4 Km/Hr	3300.0 mm/Km	3334	4.43	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:28:10	31	100	1600	32.0 cm	36.0 Km/Hr	3200.0 mm/Km	3241	4.32	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:28:20	31	100	1700	34.0 cm	35.2 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:28:31	31	100	1800	34.0 cm	34.5 Km/Hr	3400.0 mm/Km	3428	4.54	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:28:46	31	100	1900	35.0 cm	22.8 Km/Hr	3500.0 mm/Km	3521	4.65	Good	26.3628988	N	84.2596145	E	Normal
15/03/22	10:29:00	31	100	2000	37.0 cm	26.2 Km/Hr	3700.0 mm/Km	3709	4.87	Good	26.3628988	N	84.2596145	E	Normal

15/3/22
15/3/22
15/3/22


15/3/22
15/3/22
15/3/22

18/3/22
15/3/22
15/3/22
15/3/22

15/3/22
15/3/22
15/3/22
15/3/22

Name of work :		Semraw - Survania													
Name of customer :		Shalicon Construction													
		(R)Rural Road													
		Good				Average				Poor					
		< 4000				4001 - 5000				> 5000					
1503/22	10-48-16	31	100	4300	21.0 cm	30.9 Km/Hr	2100.0 mm/Km	2211	3.07	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-48-30	31	100	4400	29.0 cm	25.8 Km/Hr	2900.0 mm/Km	2960	3.98	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-48-45	31	100	4500	32.0 cm	22.6 Km/Hr	3200.0 mm/Km	3241	4.32	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-47-08	31	100	4600	36.0 cm	16.6 Km/Hr	3600.0 mm/Km	3615	4.78	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-47-22	31	100	4700	34.0 cm	25.4 Km/Hr	3400.0 mm/Km	3428	4.54	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-47-32	31	100	4800	32.0 cm	34.9 Km/Hr	3200.0 mm/Km	3241	4.32	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-47-42	31	100	4900	38.0 cm	36.3 Km/Hr	3800.0 mm/Km	3866	5.09	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-47-56	31	100	5000	32.0 cm	27.0 Km/Hr	3200.0 mm/Km	3241	4.32	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-48-32	31	100	5100	30.0 cm	10.0 Km/Hr	3000.0 mm/Km	3053	4.09	Good	28.3628988	N	84.2586145	E	Normal
1503/22	10-48-46	31	100	5200	35.0 cm	24.9 Km/Hr	3500.0 mm/Km	3521	4.65	Good	28.3628988	N	84.2586145	E	Normal

Name of Customer: Shailton Construction, Machine no: 19193, Road: Semraw - Surwaha, Date: 15/03/22, Section No: 31, Equation: $Y=0.936X+245.3$

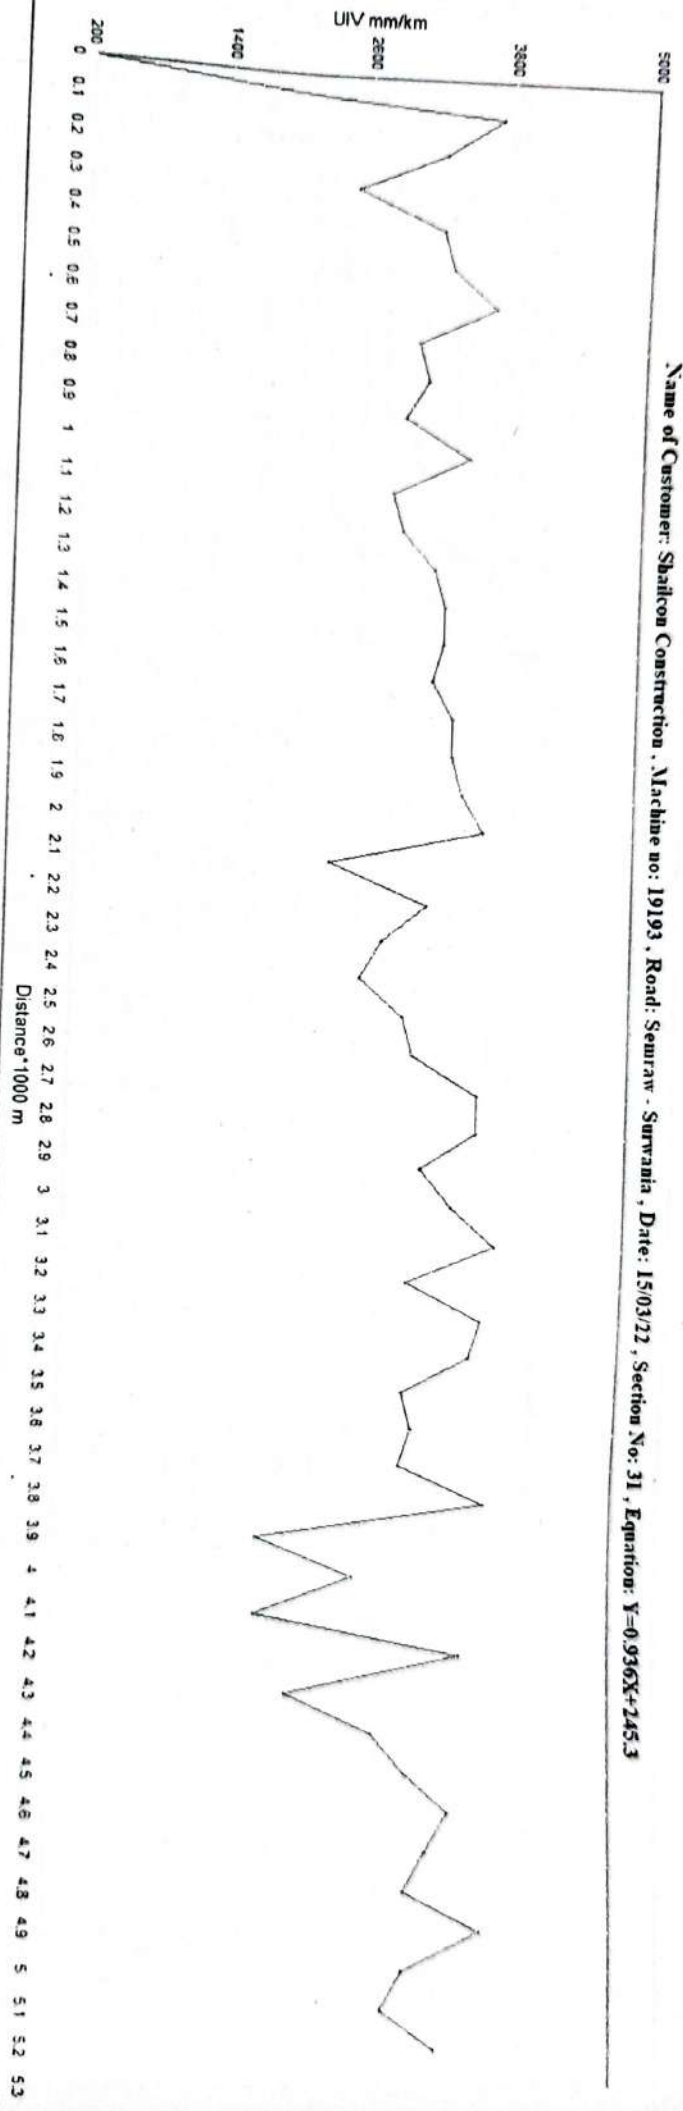

NA
15/3/22
R
NA
15/3/22
R

NA
15/03/22
R

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Semraw - Surwanla
(Package No.RM/SO/HAT/19/0012)
Length of Road :- 5.200 Km
Inspector :- J.E RWD Sub Division : hathua

To:-
Executive Engineer
RWD, Works Division Hathua

Position :- J.E

Date:-

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												Comments
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	⊗ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	m ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whitw washing)	m ²	Nil	Nil	Nil	Nil							Not Required

No	standard Of Work Item	Work	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation	Unit											
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Required
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												


 20/3/22
 22


 20/3/22
 AS


 20/3/22
