

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

पत्रांक 1769 अनु सोनपुर, दिनांक 20.10.2022

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक
पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण
(BRRDA)
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरक्षण निति-2018 के अंतर्गत पथों का अनुरक्षण की राशि की मांग रुपये 2,97,884.00 (दो लाख सतान्बे हजार आठ सौ चौरासी) मात्र विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:-Standard Formate for Roads
Quarterly Statement

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर
20/10/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **October-2022**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18 (Maintenance)		66.42492	Certified that out of Rs 66.42492 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 66.35226 Lakh has been utilized for the purpose of New Maintenance Policy-18 (Maintenance) Scheme as given in the margin for which it was sanctioned and that the balance of Rs 0.07266 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

- Words have been supervised be Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works

[Signature]
20.10.22
D.A.O

R.W.D. Works Division Sonpur.

[Signature]
20/10/22
EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.

[Signature]
20/10/22

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- SONPUR

Road Details				AA Details		Agreement								Actual Maintenance Expenditure						Current Maintenance Demand		Remarks							
SL No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh	Maintenace Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report		IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4 th QTR Maintenance	Total	
1	Fulwariya NH-102 se Bisunpur piprahi	RM/SA/SON /20/0017	313641034930	31-08-2021	79.06000	34.11500	75.04100	6.75509	6.75509	6.75009	6.75509	6.75509	33.77045	4.110	0.000	0.000	0.000	0.000	0.000	0.000	0.000	1.900	2540	1.68852	0.00000	0.00000	0.00000	1.68852	1.68852
	Chapra jila antargat maker panchayat lakshi kaituka natak sala bazar se panchayat bhawan lakshi kaituka hote hue anusuchi jati tola (nat tola) hote hue madiya vidhyalay piprahi mukhya sarak tak path nirman.	RM/SA/SON /20/0006	31306404001	16-06-2021	52.32800	26.39000	60.38200	2.44911	3.34275	7.61300	4.21106	8.19037	25.80629	2.300	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.300	2431	1.29031	0.00000	0.00000	0.00000	1.29031	1.29031
Total																												2.97884	

[Signature]
20.10.2022
DAOI

[Signature]
20/10/22
Executive Engineer
R.W.D. Works Division
SONPUR

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Fulwariya NH-102 se Bisunpur piprahi		
2	Batch No.	RM/SA/SON/20/0017		
3	Project ID	313641034930		
4	Total Length of Road (in Km)	4.110		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	1.900		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	33.77045		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	1.68852		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.68852

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Certified by (Signature) Date
Rural Works Department
Work Division, Sonapur

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Sonpur

1st Quarter

Government of Bihar
OM01

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Rural works Department

Road From- Fulwariya NH-102 se Bisunpur piprahi

To: Executive Engineer

Length of Road: 4.110KM

RWD Works Division Sonpur

Date:

Period : From.....

Inspector: A.E RWD Sub Division, Maker

Position: A.E

Standard Work item			Work	Units of work required in each kilometre										Comments
S No	Name	Units		1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement														
OM101	Pothole Patching	m2												No. Pothole found
OM102	Surface Depression and Rut Patching	m2												No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm												No Crack Sealing found
Surface Treatment														
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2												No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2												No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2												No Crocodile Cracking found
OM105	Edge Repair	m2												No Edge Repair Required
OM106	Digouts	m2												
OM107	Concrete Pavement	m3												
	Other activities	Lm												
OM200 Shoulder														
OM201	Unsealed Shoulder	No												No Edge Drop off Required
	(a) Edge Drop off	Lm												Not required
	(b) Roughness, Scouring or Potholes	Lm												
	(c) Holding Water	Lm												No Holding water found
OM202	Embankment Repair	No												No Embankment Repair Required
	Other Activite (Raincut)													Defects rectified within stipulated time.
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge	Lm												Not Required
OM302	Culvert Cleaning	Lm												Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2												Not Required

[Signature]

[Signature]

[Signature]
19/10/2019

Name of work : Fulwariya NH-102 se Bisunpur piprahi	
Name of customer : Jay Shankar Prakash	
(R) Rural Road	
Good	Average
< 4000	4001 - 5000
	Poor
	> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ul(mm/Km)	Corrected Ul (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
25/06/22	12:24:47	35	100	100	23.0 cm	16.2 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9444476	N	84.9681025	E	Normal
25/06/22	12:25:11	35	100	200	36.0 cm	15.0 Km/Hr	3600.0 mm/Km	3468	4.59	Good	25.9458704	N	84.9696970	E	Normal
25/06/22	12:25:50	35	100	300	28.0 cm	19.5 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9458704	N	84.9696970	E	Normal
25/06/22	12:26:30	35	100	400	28.0 cm	18.7 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9458094	N	84.9738322	E	Normal
25/06/22	12:26:58	35	100	500	26.0 cm	12.9 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.7617273	N	84.0260248	E	Normal
25/06/22	12:27:40	35	100	600	29.0 cm	18.5 Km/Hr	2900.0 mm/Km	2819	3.81	Good	25.9479304	N	84.9759455	E	Normal
25/06/22	12:28:17	35	100	700	28.0 cm	19.4 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9458089	N	84.9738312	E	Normal
25/06/22	12:28:40	35	100	800	32.0 cm	15.7 Km/Hr	3200.0 mm/Km	3097	4.14	Good	25.9458094	N	84.9738322	E	Normal
25/06/22	12:29:02	35	100	900	22.0 cm	16.3 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.9458025	N	84.9738319	E	Normal
25/06/22	12:30:17	35	100	1000	17.0 cm	15.0 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.9416113	N	84.9784327	E	Normal
25/06/22	12:31:10	35	100	1100	14.0 cm	26.4 Km/Hr	1400.0 mm/Km	1426	2.07	Good	25.9420500	N	84.9784327	E	Normal
25/06/22	12:31:33	35	100	1200	23.0 cm	16.0 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.9430151	N	84.9789210	E	Normal
25/06/22	12:31:53	35	100	1300	30.0 cm	17.8 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.9431735	N	84.9782267	E	Normal
25/06/22	12:32:31	35	100	1400	31.0 cm	19.5 Km/Hr	3100.0 mm/Km	3004	4.03	Good	25.9432784	N	84.9772273	E	Normal
25/06/22	12:33:10	35	100	1500	26.0 cm	22.9 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.9434863	N	84.9764338	E	Normal
25/06/22	12:33:37	35	100	1600	28.0 cm	23.6 Km/Hr	2800.0 mm/Km	2726	3.7	Good	25.9445487	N	84.9761439	E	Normal
25/06/22	12:34:09	35	100	1700	25.0 cm	21.1 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.9452239	N	84.9758311	E	Normal
25/06/22	12:35:52	35	100	1800	35.0 cm	23.4 Km/Hr	3500.0 mm/Km	3375	4.48	Good	25.9461279	N	84.9755183	E	Normal
25/06/22	12:36:12	35	100	1900	13.0 cm	27.6 Km/Hr	1300.0 mm/Km	1334	1.95	Good	25.9462977	N	84.9761210	E	Normal

Done
19/10/22
T.E.

Subdhan

Executive Engineer
Rural Works Department
Work Division, Sonapur

Name of Customer: Jay Shankar Prakash , Machine no: 19205 , Road: Fulwariya NH-102 se Bisunpur piprahi , Date: 25-06-22 , Section No: 35 , Equation: $Y=0.928X+127.3$

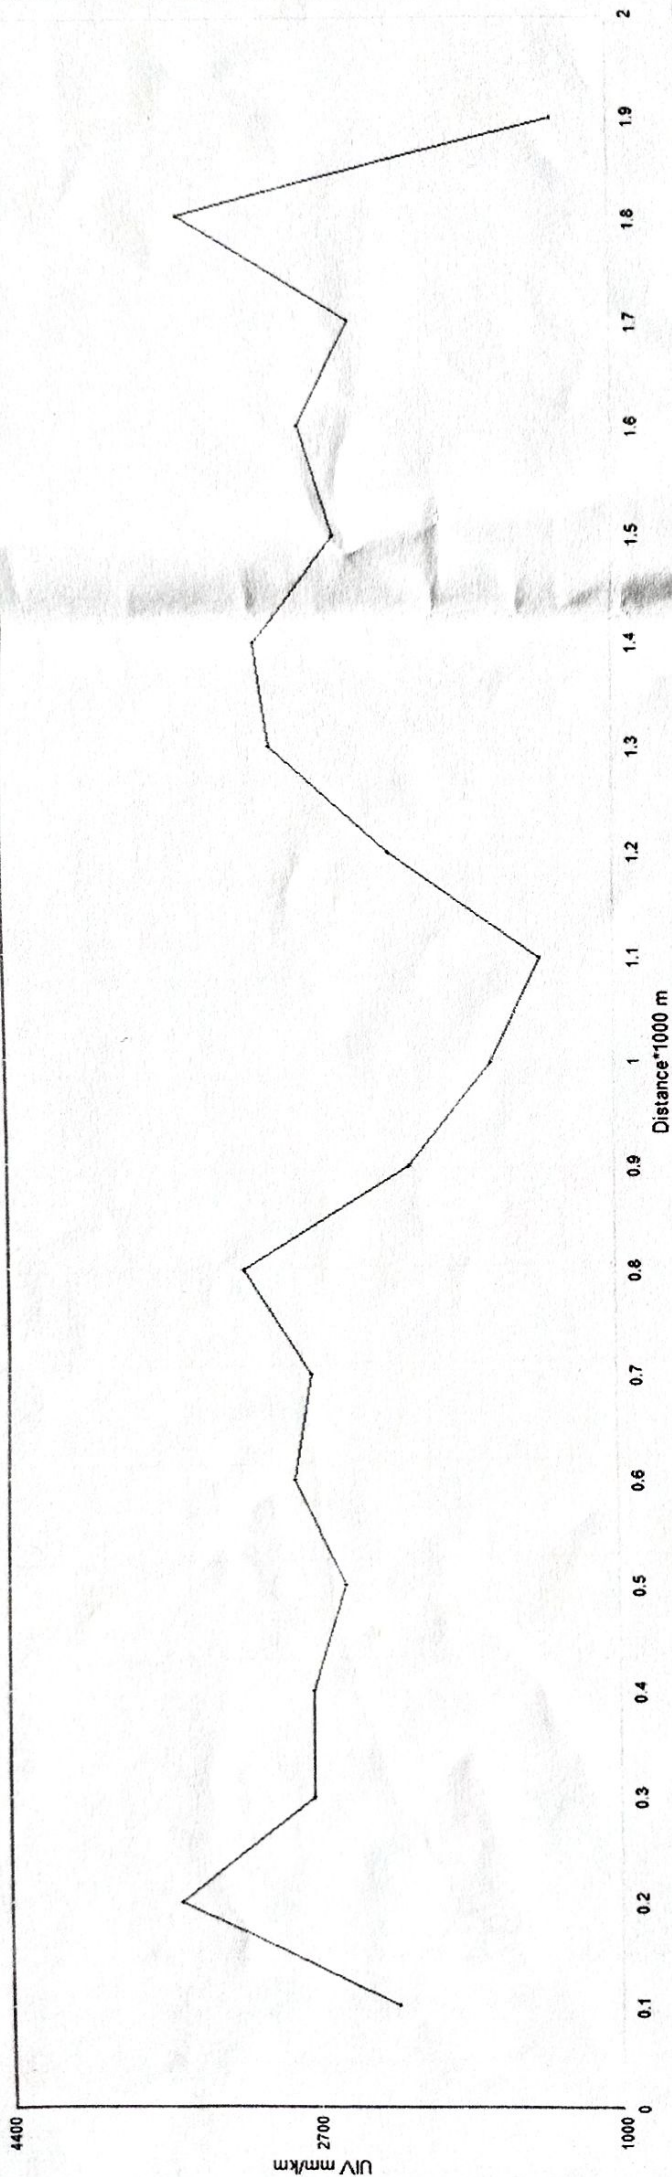

20/7/22
J.E.

20/7/22
J.E.

Executive Engineer
Rural Works Department
Work Division, Sonepur
