

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

पत्रांक.....1866.....सोनपुर, दिनांक 04-11-2022

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक
पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण
(BRRDA)
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरक्षण निति-2018 के अंतर्गत पथों का अनुरक्षण की राशि की मांग रुपये 2,24,099.00 (दो लाख चौबीस हजार निन्यानबे) मात्र विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0:-Standard Formate for Roads
Quarterly Statement

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

20
11/11/2022

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **October-2022**


PIU:- E.E.,R.W.D. Works Division Sonpur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18 (Maintenance)		66.42492	Certified that out of Rs 66.42492 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonpur a sum of Rs 66.35226 Lakh has been utilized for the purpose of New Maintenance Policy-18 (Maintenance) Scheme as given in the margin for which it was sanctioned and that the balance of Rs 0.07266 Lakh remaining unutilized at the end of the period under report.


Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-


- Words have been supervised be Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works


D.A.O.

R.W.D. Works Division Sonpur.


EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.


4/11/2022

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Name of Works Division:- SONPUR

Road Details			AA Details		Agreement							Actual Maintenance Expenditure					Current Maintenance Demand				Remarks
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length as per Bump Report	IRI As per Report	1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th QTR Maintenance	Total	
1	SITALPUR PARSA ROAD - RAJAPUR	RM/SA/SON/20/0013	31306402078	03.03.2021	96.72500	45.38500	92.68500	8.96395	8.96395	8.96395	8.96395	8.96395	44.81975	4.000	2540	0.000	0.000	0.000	0.0000	2.24099	2.24099
Total																					2.24099

[Signature]
04-11-2022
DPO 2

[Signature]
Executive Engineer
R.W.D. Works Division
SONPUR
4/11/22

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	SITALPUR PARSA ROAD - RAJAPUR		
2	Batch No.	RM/SA/SON/20/0013		
3	Project ID	31306402078		
4	Total Length of Road (in Km)	4.000		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	4.000		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	44.81975		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	2.24099		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				2.24099

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

Executive Engineer
Rural Works Department
Work Division, Sonapatna

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
Name of Works Division :- Sonpur		1st Quarter											
Government of Bihar		SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT											
Rural works Department		To: Executive Engineer RWD Works Division Sonpur											
Road From- SITALPUR PARSA ROAD - RAJAPUR		Date:											
Length of Road: 4.000KM		Position: A.E											
Period : From.....													
Inspector: A.E RWD Sub Division, Daryapur													
S No	Standard Work item Name	Work Units	1	2	3	4	5	6	7	8	9	10	Comments
OM101	OM100 Sealed Pavement												
	Pothole Patching	m2											No. Pothole found
OM102	Surface Depression and Rut Patching	m2											No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm											No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2											No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2											No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2											No Crocodile Cracking found
OM105	Edge Repair	m2											No Edge Repair Required
OM106	Digouts	m2											
OM107	Concrete Pavement	m3											
	Other activities	Lm											
OM200	Shoulder												
	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm											No Edge Drop off Required
OM201	(b) Roughness, Scouring or Potholes	Lm											Not required
	(c) Holding Water	Lm											No Holding water found
OM202	Embankment Repair	No											No Embankment Repair Required
	Other Activities (Raincut)												Defects rectified within stipulated time.
OM 300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm											Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2											Not Required

Sd/-
 09/11/2018
 09/11/2018
 09/11/2018

Name of Contractor: SITALPUR PARSA ROAD - RAJAPUR
Name of Road: JAWAHAR LAL YADAV

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY mm/km ROAD	Latitude	Longitude	Event
26/6/22	11:15:40	85	0.1	150	50.5	1500	1836 G	25.85593	85.18652	Normal
26/6/22	11:16:0	85	0.1	180	40.4	1800	2177 G	25.8551	85.18215	Normal
26/6/22	11:16:0	85	0.1	260	50.5	2600	3086 G	25.8543	85.1771	Normal
26/6/22	11:17:26	85	0.1	160	50.5	1600	1950 G	25.85183	85.16598	Normal
26/6/22	11:18:1	85	0.1	220	10.1	2200	2631 G	25.85087	85.16548	Normal
26/6/22	11:18:1	85	0.1	220	10.1	2200	2631 G	25.84994	85.16632	Normal
26/6/22	11:18:36	85	0.1	180	30.3	1800	2177 G	25.84877	85.1668	Normal
26/6/22	11:19:0	85	0.1	170	60.6	1700	2063 G	25.84783	85.16582	Normal
26/6/22	11:19:11	85	0.1	310	30.3	3100	3654 G	25.84697	85.16312	Normal
26/6/22	11:19:11	85	0.1	310	20.2	3100	3654 G	25.84613	85.15842	Normal
26/6/22	11:20:0	85	0.1	300	30.3	3000	3540 G	25.84522	85.15655	Normal
26/6/22	11:20:22	85	0.1	170	60.6	1700	2063 G	25.84448	85.16143	Normal
26/6/22	11:20:22	85	0.1	140	50.5	1400	1722 G	25.84425	85.17137	Normal
26/6/22	11:20:22	85	0.1	130	50.5	1300	1609 G	25.84343	85.17525	Normal
26/6/22	11:21:0	85	0.1	230	40.4	2300	2745 G	25.84258	85.17137	Normal
26/6/22	11:21:0	85	0.1	180	30.3	1800	2177 G	25.84177	85.1675	Normal
26/6/22	11:22:8	85	0.1	280	30.3	2800	3313 G	25.84101	85.16918	Normal
26/6/22	11:22:43	85	0.1	290	20.2	2900	3426 G	25.84049	85.17693	Normal
26/6/22	11:23:0	85	0.1	210	30.3	2100	2518 G	25.84003	85.18535	Normal
26/6/22	11:23:18	85	0.1	270	30.3	2700	3199 G	25.8393	85.19057	Normal
26/6/22	11:23:18	85	0.1	250	30.3	2500	2972 G	25.83858	85.19595	Normal
26/6/22	11:23:18	85	0.1	230	40.4	2300	2745 G	25.83767	85.1941	Normal
26/6/22	11:23:18	85	0.1	200	40.4	2000	2404 G	25.83668	85.1936	Normal
26/6/22	11:24:0	85	0.1	300	30.3	3000	3540 G	25.83624	85.2008	Normal
26/6/22	11:24:0	85	0.1	270	40.4	2700	3199 G	25.83601	85.21077	Normal
26/6/22	11:24:0	85	0.1	260	40.4	2600	3086 G	25.83588	85.22137	Normal
26/6/22	11:24:0	85	0.1	220	40.4	2200	2631 G	25.83604	85.23097	Normal
26/6/22	11:24:29	85	0.1	260	40.4	2600	3086 G	25.83608	85.24157	Normal
26/6/22	11:24:29	85	0.1	320	20.2	3200	3767 G	25.83588	85.25218	Culvert
26/6/22	11:25:4	85	0.1	240	20.2	2400	2858 G	25.83584	85.26262	Curve
26/6/22	11:25:4	85	0.1	220	10.1	2200	2631 G	25.83634	85.268	Normal
26/6/22	11:25:4	85	0.1	280	30.3	2800	3313 G	25.83633	85.27693	Normal
26/6/22	11:25:40	85	0.1	240	40.4	2400	2858 G	25.83597	85.28535	Normal
26/6/22	11:25:40	85	0.1	230	40.4	2300	2745 G	25.83556	85.29545	Normal
26/6/22	11:26:0	85	0.1	240	30.3	2400	2858 G	25.83486	85.30168	Normal
26/6/22	11:26:15	85	0.1	180	30.3	1800	2177 G	25.83442	85.30975	Normal
26/6/22	11:26:15	85	0.1	270	30.3	2700	3199 G	25.83424	85.31935	Normal
26/6/22	11:26:15	85	0.1	320	30.3	3200	3767 G	25.83397	85.33013	Normal
26/6/22	11:26:40	85	0.1	270	40.4	2700	3199 G	25.83601	85.21078	Normal
26/6/22	11:27:25	85	0.1	260	40.4	2600	3086 G	25.83588	85.22138	Normal

4

112292

Signature
04/11/22
TE

Signature
4/11/22
ATZ

Signature
04/11/22
Executive Engineer
Rural Works Department
Work Division, Sonbhit

Name of Customer : JAWAHAR LAL YADAV
 Name of Work/Road : PUR PARSA ROAD - RAJAPUR
 Lab Job number :
 Date : 26-06-2022
 Section No. : 85

Test Date : 26-04-2022
 Machine No : 372
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : JR PARSA ROAD - RAJAPUR
 Road Type : (R) RURAL ROAD
 Side :
 Interval :
 IIV Range : 609 To 5000 mm/km
 Dist Range : 0 To 41
 Equation : $Y = 0.4X^2 + 1136X + 132.5$

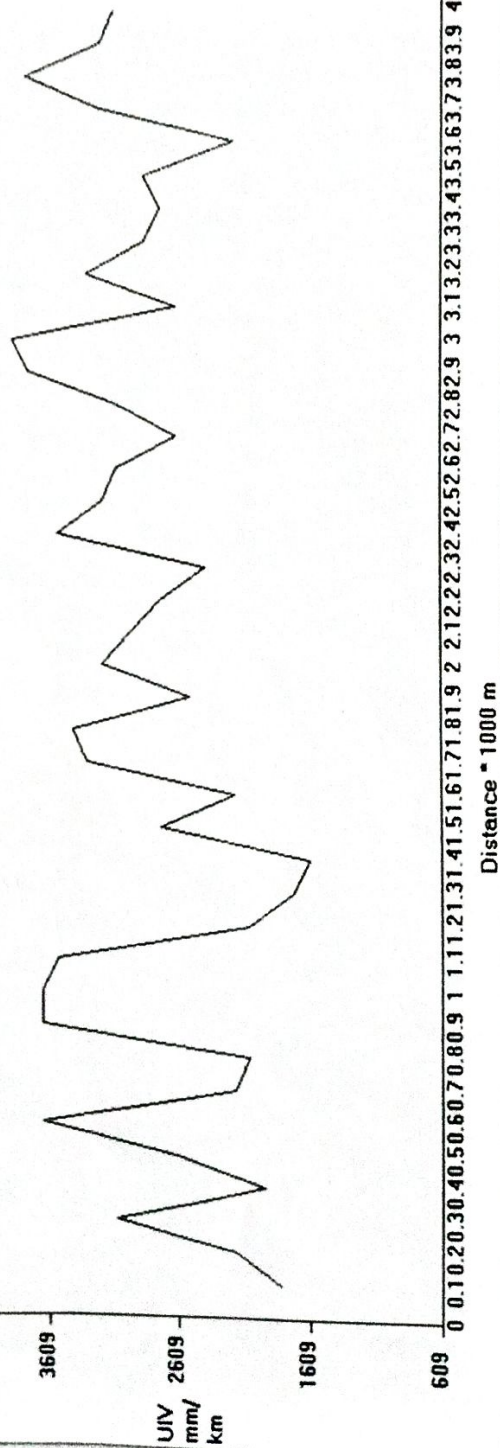
Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BRRDA72\OneDrive\Desktop\Bump Data 25.06.2022\Bump Data\26061323.Xls, Section No. : 85,

Name of Customer : JAWAHAR LAL YADAV, Name of Work/Road : SITALPUR PARSA ROAD - RAJAPUR, Lab Job



[Signature]
 27/7/22

[Signature]
 27/7/22
[Signature]

[Signature]
 Executive Engineer
 Rural Works Department
 Work Division, Sonbhour
