

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा-1।

पत्रांक 15203/नु० छपरा-1/दिनांक 04.11.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-1

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :-


नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-1।


04.11.22

Maintenance Requisition Formate for Scheme Head- MR (3054) Under

Name of Works Division:- Chapra-1

Name of Works Division:- Chapra-1														
Road Details					AA Details									
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Agreement									
					Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
1	DUMARIA - LOHARI	RM/SA/C HA/19/0 009	31306202041	14/03/2021	24.886	10.75459	24.886	0.92895	1.39306	3.2231	1.6588	3.55068	10.75459	1.1
2	JALALPUR NH-19 - DARIYAWGANJ	RM/SA/C HA/19/0 009	31306202049	18/03/2021	25.663	10.317	25.663	0.8426	1.34882	3.30389	1.58822	3.23361	10.31714	1.18
3	MAUNA RLYDHALA - RAMNAGAR	RM/SA/C HA/19/0 009	31306202060	14/03/2021	25.501	10.842	25.501	0.58846	1.28457	3.71865	1.37805	3.87322	10.84295	1.52
Total					76.05	31.91	76.05	2.36	4.03	10.25	4.63	10.66		

Bihar Rural Road Maintenance Policy-2018

Actual Maintenance Expenditure						Current Maintenance Demand										Remarks
1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
0.00000	0.00000	0.00000	0.00000	0.53772	0.53772	1.1	2058	0.53772	0.53772	0.53772	0.53772	1	1	1	2.15088	
0.00000	0.00000	0.00000	0.00000	0.51586	0.51586	1.8	2903	0.51586	0.51586	0.51586	0.51586	1	1	1	2.06343	
0.00000	0.00000	0.00000	0.00000	0.54214	0.54214	1.52	2838	0.54214	0.54214	0.54214	0.54214	1	1	1	2.16856	
0.00	0.00	0.00	0.00	1.60	1.60	4.42		1.60	1.60	1.60	1.60	0.00	0.00	0.00	6.38	


 EXECUTIVE ENGINEER
 R.W.D. MORRIS Division
 Chapter-1
 04.11.22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	MAUNA RLYDHALA - RAMNAGAR		
2	Batch No.	RM/SA/CHA/19/0009		
3	Project ID	31306202060		
4	Total Length of Road (in Km)	1.52		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	1.52		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	10.84295		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.54214		
Compliance Criteria	Standard Job Description	Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	Reduction Payment (6) = (3) / (1) * (2) * (4)
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.54214

Date of inspection by E/1 or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)
Remay
04.11.22

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Chapra-1

Government of Bihar

OM01

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

To: Executive Engineer
RWD Works Division Chapra-1

Date:

Road From- MAUNA RLYDHALA - RAMNAGAR

Length of Road: 1.520 KM

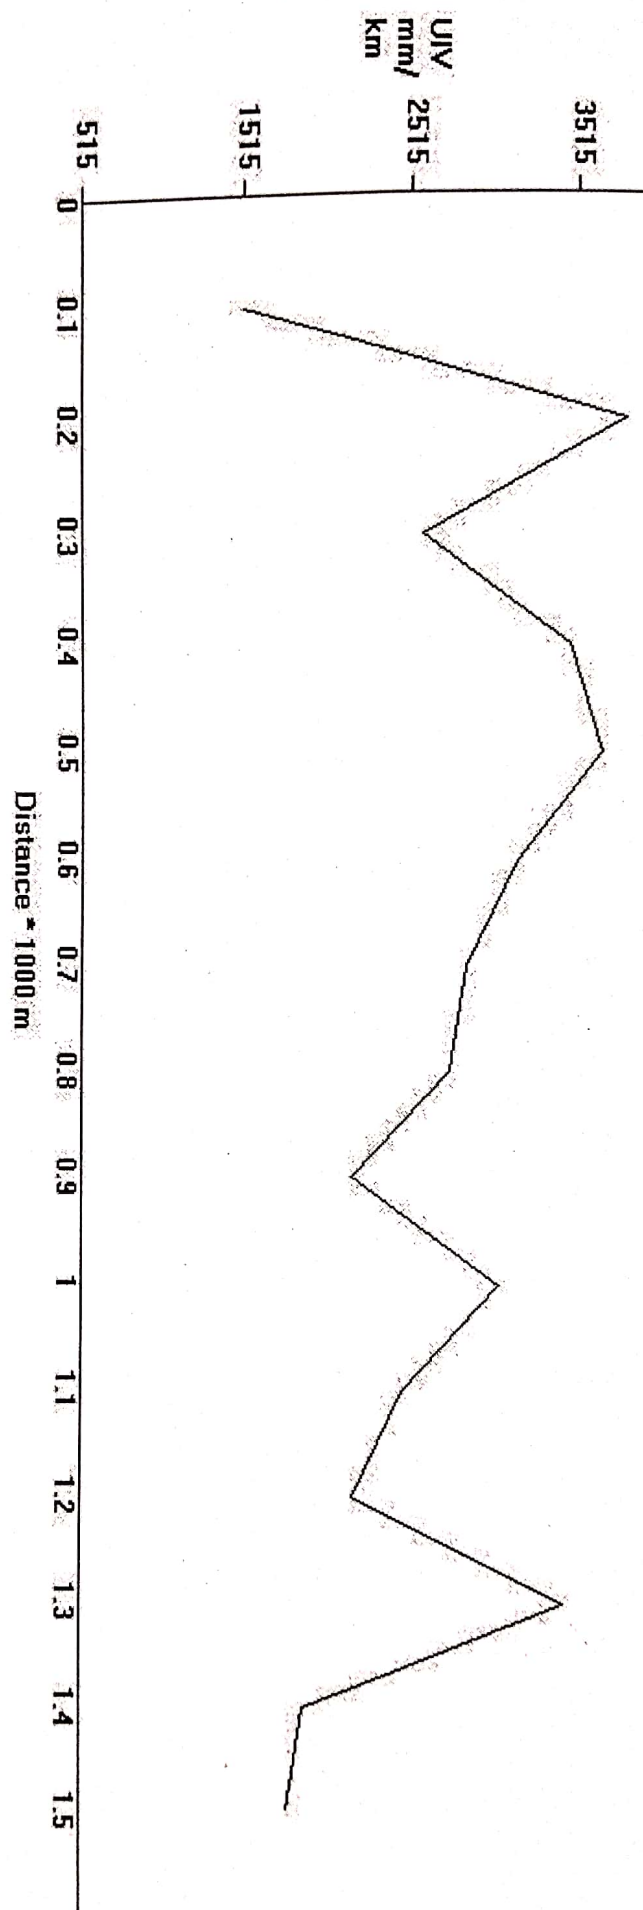
Period : From.....

Position: A.E

Inspector: A.E RWD Sub Division, Sadar

Standard Work item			Work Units	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM100 Sealed Pavement														
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.	
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found	
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found	
Surface Treatment														
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found	
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required	
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found	
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required	
OM106	Digouts	m2	N/A	N/A	N/A	N/A								
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A								
Other activities		Lm												
OM200 Shoulder														
Unsealed Shoulder		No											No Edge Drop off Required	
OM201	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.	
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil								
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found	
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required	
	Other Activite (Raincut)		3%	1%	2%	Nil							Defects rectified within stipulated time.	
OM 300 Drainage including culverts major														
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required	

File :H:\VAISHNAVI CONST\MAUNA RLYDHALA - RAMNAGAR 1.520\16101345.Xls, Section No. :62, Egn : Y = 0 =
Name of Customer :M/S Vaishnav Devi Construction, Name of Work/ Road :MAUNA RLYDHALA - RAMNAGAR.



Scheme - New MR
Road Name- MAUNA RLYDHALA - RAMNAGAR
Contractor Name - M/S Vaishnav Devi Construction

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event	Y = 0 * X ^ 2 + 1.000 * X + 415.2
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				X = 1400
16/ 10/ 21	11: 57: 0	62	0.1	110	0	1100	1515	G	25.79241	84.76145	Normal	Y = 1815
16/ 10/ 21	11: 57: 32	62	0.1	340	20.2	3400	3815	G	25.79278	84.7615	Normal	
16/ 10/ 21	11: 58: 21	62	0.1	220	10.1	2200	2615	G	25.79353	84.76197	Speed Breaker	
16/ 10/ 21	11: 58: 42	62	0.1	310	10.1	3100	3515	G	25.79364	84.76251	Normal	(R) RURAL ROAD
16/ 10/ 21	11: 59: 18	62	0.1	330	20.2	3300	3715	G	25.79414	84.76313	Normal	Good Average Poor
16/ 10/ 21	12: 2: 14	62	0.1	280	10.1	2800	3215	G	25.79494	84.76338	Normal	<4000 4001-5000 >5001
16/ 10/ 21	12: 3: 0	62	0.1	250	10.1	2500	2915	G	25.79489	84.76433	Speed Breaker	
16/ 10/ 21	12: 3: 25	62	0.1	240	10.1	2400	2815	G	25.79563	84.76493	Normal	
16/ 10/ 21	12: 4: 0	62	0.1	180	10.1	1800	2215	G	25.79661	84.76522	Normal	
16/ 10/ 21	12: 5: 10	62	0.1	270	10.1	2700	3115	G	25.79757	84.76544	Normal	
16/ 10/ 21	12: 5: 46	62	0.1	210	10.1	2100	2515	G	25.79861	84.76567	Normal	
16/ 10/ 21	12: 6: 21	62	0.1	180	20.2	1800	2215	G	25.79952	84.76581	Normal	
16/ 10/ 21	12: 6: 21	62	0.1	310	20.2	3100	3515	G	25.80042	84.76586	Normal	
16/ 10/ 21	12: 7: 0	62	0.1	150	30.3	1500	1915	G	25.80157	84.76599	Normal	
16/ 10/ 21	12: 7: 30	62	0.1	140	30.3	1400	1815	G	25.80267	84.76613	Normal	
						TOTAL	41425					
						IRI VALUE	2762					
