

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 1770(3157) बिहारशरीफ, दिनांक 17-11-22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।


विषय :- नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये
अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अध्याचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०-यथोक्त।

विश्वासभाजन


17/11/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ

16/11/22

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Bihar Sharif

1 Year (1st Quarter)

Government Of Bihar OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Rampur-Badhi Ghariyari Road to SH-78
(Package No.RM/NA/BIH/20/0003)
Length of Road :- 0.985 Km
Inspector :- J.E RWD Sub Division : Samera

To:-

Executive Engineer
RWD, Works Division ~~Patna~~ Bihar Sharif

Date:-

Position :- J.E

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	@ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
OM200	Other activities												
	Shoulder												
	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
OM201	(b) Roughness, Scouring or Potholes	l/m	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
OM202	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

Standard Of Work Item		Work	Unit Of Required in each Kilometer										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
OM402	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	Nil											Not Required
OM502	Guard Stones	No	Nil	Nil	Nil	Nil							Not Required
OM503	Distance Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	No	N.A	N.A	N.A	N.A							Not Required
	Other activities	M ²	Nil	Nil	Nil	Nil							Not Required

10/11/22
S.E

10/11/22
AE

Executive Engineer
Rural Work Department
Work Division Bihar Sharif
15/11/22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-	Rampur-Badhi Ghariyari Road to SH-78		
2	Batch No.-	RM/NA/BIH/20/0003		
3	Project ID -	1261034943		
4	Total Length of Road (in Km)	0.985		
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	0.985		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	14.24668		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.71233		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.71233
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				

Date of inspection by E/I or his agent

Date

Signature of person inspecting road

[Signature]
10/11/22
AE

Name and Designation of person inspecting road

Certify by E/I (signature) Date

Scheme-NEW MR
Road Name-Rampur bari gariyari road se SH-78
Contractor-Maa Tara Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event						
1/5/22	8:26:0	76	0.1	240	0	2400	2207	ROAD	25.303508	85.719493	Normal						
1/5/22	8:26:0	76	0.1	330	30.3	3300	2941	G	25.30339	85.720387	Normal						
1/5/22	8:26:0	76	0.1	300	10.1	3000	2696	G	25.303197	85.721447	Normal						
1/5/22	8:26:28	76	0.1	290	10.1	2900	2615	G	25.30282	85.722423	Normal						
1/5/22	8:26:28	76	0.1	230	10.1	2300	2125	G	25.302318	85.723147	Normal						
1/5/22	8:26:28	76	0.1	240	10.1	2400	2207	G	25.301702	85.724057	Normal						
1/5/22	8:27:4	76	0.1	220	10.1	2200	2044	G	25.301407	85.724948	Normal						
1/5/22	8:27:4	76	0.1	310	20.2	3100	2778	G	25.30101	85.725673	Normal						
1/5/22	8:27:39	76	0.1	280	10.1	2800	2533	G	25.300412	85.72616	Normal						
1/5/22	8:28:0	76	0.1	270	10.1	2700	2452	G	25.300113	85.727053	Normal						
						Total	24598										
						IRI Value	2560										


10/11/22

7-E

70/11/22

15/11/22

Name of Customer :Maa Tara Construction, Name of Work/ Road :Rampur-Badhi Ghariyan Road to SH-78, Lab Job

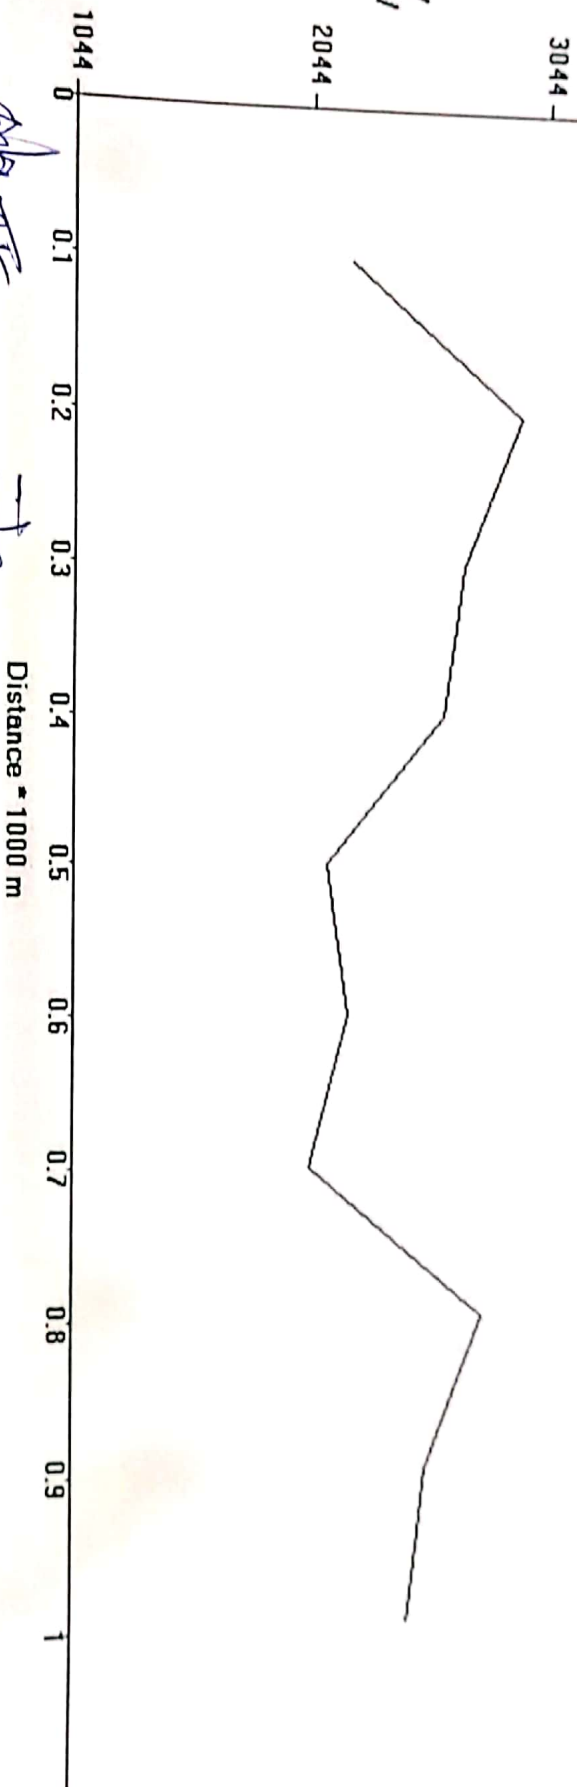

10/11/23

[Signature]

$$\frac{\text{Sample}}{10 \text{ ml}} \quad \text{AE}$$

OK
~~15/11/22~~
