

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सहरसा।

पत्रांक- 1451 अ.३०/सहरसा

दिनांक- 13/10/2022

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल सहरसा।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:-


नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं 2021-22 में व्यय हेतु
अनुरक्षण मद में आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण नीति 2018 शीर्ष अंतर्गत वित्तीय वर्ष 2020-21 एवं
2021-22 में व्यय हेतु अनुरक्षण मद में संलग्न विवरणी के अनुसार रुपये 18,76,206.00 (अठारह लाख
छियत्तर हजार दो सौ छः रुपये) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि किये गये
कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त।

विश्वासभाजून


13-10-2022

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल सहरसा।

Statement of Work: Highway - Saharsa
Maintenance Requirements for Saharsa Road (NH-254) Under Bihar Road Road Maintenance Policy-2018

Sl. No.	Road Name	Route No	Project ID	Actual Date of Completion	A. A. Details										Agreement Details										Actual Maintenance Expenditure										Remarks
					Initial work of Amount	Maintenance Amount	New Work Amount	Maintenance Agreement 1st Year	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Amount	Length in Km	1st Year Maint. Exp.	2nd Year Maint. Exp.	3rd Year Maint. Exp.	4th Year Maint. Exp.	5th Year Maint. Exp.	Total Maint. Exp.	Length in Km	1st Quarter	2nd Quarter	3rd Quarter	4th Quarter	5th Quarter	Total								
1	Bhagpur Bhabhar Road to Chauri	BK/SA/SA/18/100003	2000/10/009	25.03.2020	72.78	27.81	72.84	3.8536	4.4536	10.7633	5.56243	11.50654	16.14031	3.300	0	0	0	0	0	0	3.300		1.80747	1.80747	1.80747	1.80747	1.80747	10.44482							
2	NH- 254	BK/SA/SA/18/100003	2000/02/079	25/03/2020	17.443	8.157	16.993	0.70966	8.10447	2.6889	1.0598	2.34535	8.05867	0.836	0	0	0	0	0	0	0.836		0.40193	0.40193	0.40193	0.40193	0.40193	2.41158							
3	Saharail Bhabhar Jauria Mahabhar	BK/SA/SA/18/100003	2004/04/010	10/01/2021	74.13	18.51	71.089	3.91273	4.39930	10.96457	5.03383	11.78898	16.7944	3.470	0	0	0	0	0	0	3.469		1.83322	1.83322	1.83322			5.50566	18.5206						

Ex-Gratia
3-10-2022
Saharsa

STANDARD FORMAT FOR QUARTERLY STATEMENT

6th Quarter (25.06.2021 to 24.09.2021)

U NAME-

1	Name of the Road	NH - Patuaha
2	Batch No / Package no	MR-N/15-20 - Saharsa/03
3	Project ID	20904302078
4	Total Length of Road (in Km)	0.840 km
5	Length of Road to Meet Required Service Level [Completed Length] (in KM) [1]	0.840 km
6	No of Total Quarter (ie 3 Months as a unit) in 5 years.	20
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	8.03867 Lakh
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.40193

Compliance criteria	Standard job Description	Non- Compliance		Reduction Payment [6] = [3] / [1] * [2] * [4]
		Length Non- Compliance [3]	Weighted Value for Payment Reduction (%) [4]	
1	PAVED ROADS (CARRIAGEWAY)	0.00	60%	0.00
2	SHOULDERS AND EMBANMENTS	0.00	10%	0.00
3	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.00	15%	0.00
4	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00
5	VEGETATION	0.00	5%	0.00
TOTAL PAYMENT REDUCATION FOR THE QUARTER (in Lakh) [5]				0.00
TOTAL PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				0.40193

21/10/22

Date of inspection by E / I his agent prepared by
Contractor's self Control unit

MANOJ SAH
Name and Designation of person inspecting
road

Signature of person inspecting road

VIKRANT RANA

12/10/22
A.E.

Certify by E / I (signature) Date:

13-10-2022
Executive Engineer
Rural Work Department
Works Division, Saharsa

Government of Bihar
OM01
Rural Works Department

Road From: NH- Patna
Length of Road : 0.840KM
Period: 6th Quarter (25.06.2021 to 24.09.2021)
Inspector : J.E., RWD, Sub Division, Kahra

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

To :
EXECUTIVE ENGINEER,
RWD, Works Division, Saharsa
Position : J.E.

Date: 13/10/22

Standard work item			Work	Unit of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM100 Sealed Pavement														
OM101	Pothole Patching	m ²	Nil											
OM102	Surface Depression and Rut Patching	m ²	Nil											
OM103	Crack Sealing	Lm	Nil											
OM104	Surface Treatment													
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil											
	(b) Bleeding/ Flushing	m ²	Nil											
	(c) Crocodile Cracking	m ²	Nil											
OM105	Edge Repair	m ³	Nil											
OM106	Digouts	m ²	N.A.											
OM107	Concrete Pavement	m ³	N.A.											
	Other activities													
OM200 Shoulder														
OM201	Unsealed Shoulder													
	(a) Edge Drop-Off	Lm	Nil											
	(b) Roughness, Scouring or Potholes	Lm	Nil											
	(c) Holding water	Lm	Nil											
OM202	Embankment Repair	m ³	Nil											
	Other activities													
OM300 Drainage including culverts major and minor bridges														
OM301	Surface Drains & Verge	Lm	N.A.											
OM302	Culvert Cleaning	No	Nil											
OM303	Culvert and Pit Repair	m ³	Nil											
	Other activities	m ²	Nil											

21/5/2022

Bidder

Signature
of

12/10/22
A.E.

13/10/2022
Executive Engineer
Rural Works Department
Saharsa

Standard work item		Work	Unit of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Road side - general Tidy	Ha	Nil										Not required.
	(b) clean near safety signs, kilometre posts and roadside furniture	Ha	Nil										Not required.
OM402	Tree and Shrub Management												
	Cutting tree	No.	Nil										Not required.
	Cutting Shrubs	No.	Nil										Not required.
	Other activities												
OMS00	Safety Signage and Road												
OMS01	Signs Maintenance	No.	Nil										Not required.
OMS02	Guard Stones	Lm	N.A										Not required.
OMS03	Distance Stance	No.	N.A										Not required.
OMS04	Road Marking	m2	Nil										Not required.
	Other activities												

(Signature of Contractor/ Authorized representative)

Date 13/10/2022

Place

Executive Engineer
Rural Work Department
Works Division, Saltasa

13-10-2022

13/10/22

12/10/22

A-3

Name of Division:- Saharsa

Name of Block:- Kahra
Length:- 0.836 Km

Name of Agency:- Raj Raman Singh

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 1.137 * X - 181.0$		
15/9/22	12:30:15	45	0.1	290	20.2	2900	3116	G	25.883933	86.63668	Normal	X = 3200		
15/9/22	12:30:36	45	0.1	340	20.2	3400	3684	G	25.883766	86.636508	Normal	Y = 3457		
15/9/22	12:30:55	45	0.1	280	20.2	2800	3002	G	25.883137	86.636493	Normal			
15/9/22	12:31:12	45	0.1	340	20.2	3400	3684	G	25.882647	86.636581	Normal			
15/9/22	12:31:28	45	0.1	300	20.2	3000	3230	G	25.881909	86.636721	Normal	RURAL ROAD		
15/9/22	12:31:47	45	0.1	310	20.2	3100	3343	G	25.880736	86.636574	Normal	Good	Average	Poor
15/9/22	12:32:05	45	0.1	290	20.2	2900	3116	G	25.879289	86.636838	Normal	<4000	4001-5000	>5001
15/9/22	12:32:18	45	0.1	320	30.3	3200	3457	G	25.879455	86.637252	Normal			
15/9/22	12:32:35	45	0.036	320	10.1	3200	3457	G	25.879632	86.637666	Normal			

12/10/22
se

12/10/22
P.E.

12/10/22
Executive Engineer
RWD Works Division
Works Saharsa

Name of Customer : Raj Ramesh Singh
 Name of Work/Road : NH to Pathwa
 Lab Job number :
 Date : 15-09-2022
 Section No. : 45


Test Date : 15-09-2022
 Machine No : 1373
 Road Name : NH to Pathwa
 Road Type : (R) RURAL ROAD
 Side :
 Start S No :
 Start E No :
 Weather :
 Start Location : 0
 End Location : 0.336
 UIV Range : 1991 To 5000 Interval 1000 mm/km
 Dist Range : 0 To 1 0.1 ~ 1000 m
 Equation : $Y = 0.0 \times X^2 + 1.137 \times X - 181.0$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BPRDA135\OneDrive\Desktop\Sentay Kumar Khan\NH to Pathwa.xlsx Section No : 45, Egn Y = 0.0
 Name of Customer : Raj Ramesh Singh, Name of Work/Road : NH to Pathwa, Lab Job number :

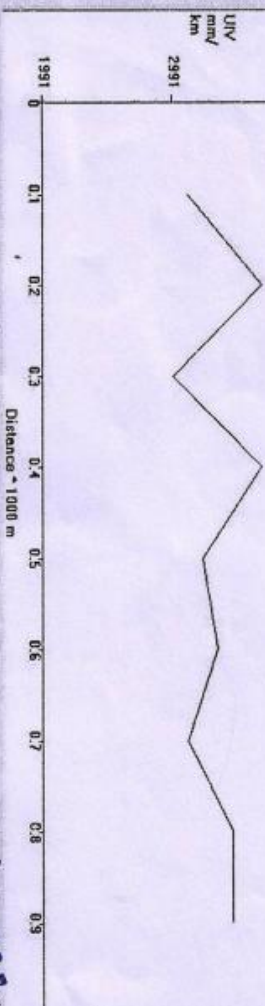

15/09/22
 12/10/22
 A.S.
 15-09-2022
 EXECUTIVE Engineer
 Rural Work Department
 Works Division, Satara
