

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, अरेराज,

पत्रांक- का0अ0-अरेराज-369 / 1344 (130)

/दिनांक 19/10/2022

प्रेषक :- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल अरेराज।

सेवा में,
अपर मुख्य कार्यपालक पदा0-सह0-सचिव,
बिहार पथ विकास अभिकरण, पटना।

विशय:- MR(3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग- अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक- मु0अ0-4(मु0)3054-04-229 / 2021 - 1135 (अनु0) / पटना, दिनांक- 09.03.2022

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः MR(3054) New Maintenance Policy-2018 (1) Package No. MR-N/19-20 Areraj/-23 (2) Package No. MR-N/19-20 Areraj/-28 योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

- अनु0- 1) अधियाचना प्रपत्र।
2) 19 ए प्रपत्र।
3) Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed
4) Standard Formate For Roads Quarterly Statement

विश्वासभाजन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल-अरेराज।

(62/19/10/22)
19/10/22
19/10/22

Form GER 19-A
(See Government of India's Decision(1) below Rule – 150)
Form of utilization certificate up to the month of UP to Oct -2022
New Maintenance policy-2018 (Maintenance) (MR-3054)

Sl No.	Name of Scheme	Sanction No.&Date with Amount (in Rs. Lacks)	Amount Received (in Rs. Lacks)	Particulars
1	New Maintenance policy-2018 (Maintenance) (MR-3054)	Letter No. 51 we Date – 30-04-2022 Rs. 141.45374 Letter No. 14 we Date – 18-07-2022 Rs. 31.14948 Letter No. 27 we Date – 26-08-2022 Rs. 141.89764	314.50086	Certified that of Rs 314.50086 Lakh of grants in said sanctioned upto Apr-2020 in favour of RWD, W.D., Areraj sum of Rs. 197.59666 lakh has been utilized New Maintenance policy-2018 (Maintenance) (MR-3054) Scheme as given sanctioned and that the balance of RS 116.90420 lakh
	Total		314.50086	

2. Certified that I have satisfied myself that the conditions on which the grand's- in-aid was sanctioned have been duly fulfilled/ate being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of checks exercised:-

- a. Works have been supervised by Executive Engineer/ Superintending Engineer.
 - b. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
 - c. Construction material has been tested.
 - d. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
3. Physical Progress achieved:-
- e. Construction of The Road works
 - f. Construction of CD Works :-

EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT,
WORKS DIVISION-ARERAJ.

19/10/22

STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (1st Quarter)

PIU NAME :- Rural Works Departement Works Division Areraj

1	Name Of Road	Amwa Nijamat to Parsauni		
2	Batch No.	RM/EA/ARE/20/0028		
3	Project ID	31708202051		
4	Total Length Of Road(in Km)	2.870		
5	Lenth Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	2.870		
6	N0. of Total Quarter (ie 3 Months as a unit) in 5 year	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	30.08488		
8	Quaterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.50424		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.50424

date of Inpection by E/I Or His Agent
Prepared by Contractor's Self Control Unit

Name and Designation of person inspecting road

date

Signature of person inspecting road

(Signature)

Certify by E/I [Signature] date

Name Of Woks Division:- areraj

Government Of Bihar

OM01

Rural Works Department

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

(1st Quarter)

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Amwa Nijamat to Parsauni
(Package No.MR-N/19-20 Ateraj/-28 (MR-3054)

Length of Road :- 2.870 KM

Period :- From:- 16-03-2021 To 15-06-2021

Inspector :- A.E RWD Sub Division : Paharpur

To:-

Executive Engineer
RWD, Works Division Ateraj

Position :- A.E

Date:-

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometere										Comments
OM100	Sealed payment		1	2	3	4	5	6	7	8	9	10	
OM101	Pothole Patching	m ²	Nil	Nil	Nil								No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil								Not Surface Depression & Rut Patchbg Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil								No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Agregate (Surface Ravelling)	m ²	Nil	Nil	Nil								No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil								No Bleeding/ Flushing Required
	@ Crocodile Cracking	m ²	Nil	Nil	Nil								No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil								No Edge Repair Required
106	Digouts	m ²	Nil	Nil	Nil								
107	Concrete pavement	m ³	Nil	Nil	Nil								
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder	Lm	Nil	Nil	Nil								No Edge Drop-Off Required
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil								Not Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil								No Holding Water Found
	(c) Holding water	M ³	Nil	Nil	Nil								Not Required
OM202	Embankment Repair												Not Required
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major	Lm	Nil	Nil	Nil								Not Required
OM301	Surface Drains & Verge	No	Nil	Nil	Nil								Not Required
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil								Not Required
OM303	Culvert and pit Repair	M ²	Nil	Nil	Nil								Not Required
	Other activities(Whitw washing)												

No	Standard Of Work Item Name	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside - General Tidy												
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil								Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil								Not Required
OM500	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil								Not Required
OM501	Safety Signage and Road												Not Required
OM502	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM503	Guard Stones	Lm	Nil	Nil	Nil								Not Required
OM504	Distance Stones	No	Nil	Nil	Nil								Not Required
	Road Marking	M ²	Nil	Nil	Nil								Not Required
	Other activities												

Bidder

15/6/21

Appendix

Executive Engineer, Works Division, Avera

15/6/21

A.E

Name of Customer : Vinay Kumar
 Name of Work : Amwa Nijamat - Parsauni
 Road :
 Lab Job number : 33
 Date : 10/06/2022
 Section No. : 33


Print Generate Report and Graph

Test Date :	10/06/2022	Road Name :	Amwa Nijamat - Parsauni
Machine No :	378	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UIV Range :	1044 To 5000
Start Location :		Dist Range :	0 To 3
End Location :		Equation :	$Y = 0 \cdot X^2 + 0.816 \cdot X + 249$

Redraw Graph

Map View

File : D:\BUMF\Aarej Div\Aarej\Amwa Nijamat to Parsauni\10061708.Xls. Section No. : 33. Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Vinay Kumar, Name of Work/Road : Amwa Nijamat - Parsauni, Lab Job number : 33

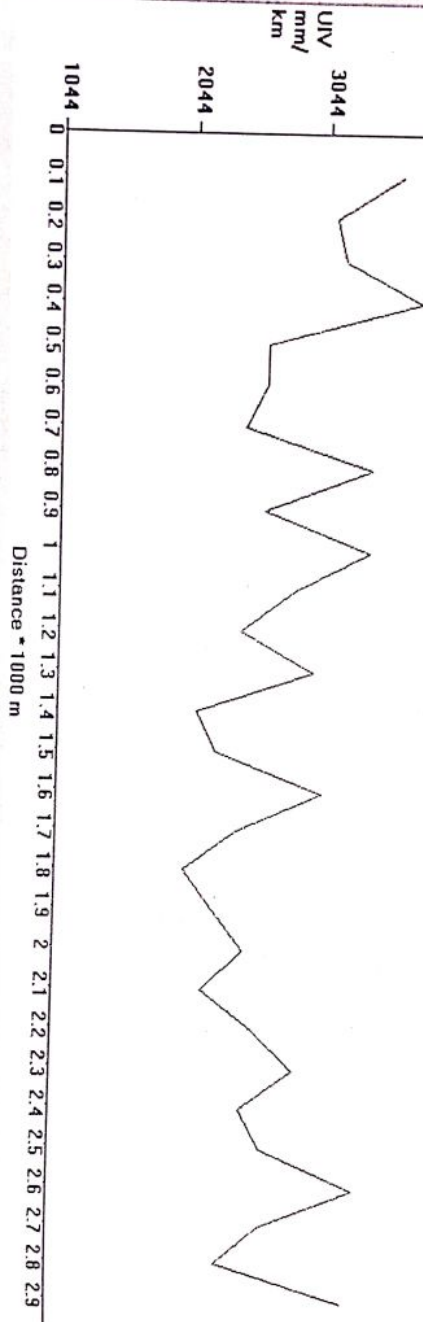

10/6/22
 A-C

10/6/22
 A-C

10/6/22
 A-C

Executive Engineer
 R.W.D. (W.D.)
 Aarej

Name of Work:-Amwa Nijamat to Parsauni
Name of Contractor:-Vinay kumar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	IRI	CATEGORY	Latitude	ongitude	Event
10/6/22	17:1:0	33	0.1	410	0	4100	3594 G		26.62997	84.60451	Normal
10/6/22	17:1:5	33	0.1	350	10.1	3500	3104 G		26.62943	84.60534	Normal
10/6/22	17:1:5	33	0.1	360	20.2	3600	3186 G		26.62906	84.60621	Normal
10/6/22	17:1:40	33	0.1	430	10.1	4300	3757 G		26.62887	84.60759	Normal
10/6/22	17:2:0	33	0.1	290	20.2	2900	2615 G		26.62852	84.60848	Normal
10/6/22	17:2:15	33	0.1	290	20.2	2900	2615 G		26.62805	84.60936	Normal
10/6/22	17:2:15	33	0.1	270	20.2	2700	2452 G		26.62763	84.61015	Normal
10/6/22	17:3:0	33	0.1	390	10.1	3900	3431 G		26.62706	84.61088	Normal
10/6/22	17:3:0	33	0.1	290	20.2	2900	2615 G		26.62636	84.61148	Normal
10/6/22	17:3:26	33	0.1	390	20.2	3900	3431 G		26.62562	84.61121	Normal
10/6/22	17:4:1	33	0.1	320	20.2	3200	2860 G		26.62474	84.61082	Normal
10/6/22	17:4:1	33	0.1	270	20.2	2700	2452 G		26.62433	84.61003	Normal
10/6/22	17:4:37	33	0.1	340	20.2	3400	3023 G		26.62346	84.60983	Normal
10/6/22	17:5:0	33	0.1	230	30.3	2300	2125 G		26.6227	84.60939	Normal
10/6/22	17:5:12	33	0.1	250	30.3	2500	2288 G		26.62193	84.60884	Normal
10/6/22	17:5:12	33	0.1	350	20.2	3500	3104 G		26.62117	84.60827	Normal
10/6/22	17:5:12	33	0.1	270	30.3	2700	2452 G		26.62063	84.60742	Normal
10/6/22	17:5:47	33	0.1	220	30.3	2200	2044 G		26.62025	84.60658	Normal
10/6/22	17:6:0	33	0.1	250	30.3	2500	2288 G		26.61992	84.60571	Normal
10/6/22	17:6:0	33	0.1	280	30.3	2800	2533 G		26.61942	84.60481	Normal
10/6/22	17:6:22	33	0.1	240	30.3	2400	2207 G		26.61887	84.60402	Normal
10/6/22	17:6:22	33	0.1	290	30.3	2900	2615 G		26.61832	84.60328	Normal
10/6/22	17:6:22	33	0.1	330	20.2	3300	2941 G		26.61775	84.60246	Normal
10/6/22	17:7:0	33	0.1	280	20.2	2800	2533 G		26.61736	84.60163	Normal
10/6/22	17:7:0	33	0.1	300	10.1	3000	2696 G		26.6167	84.60133	Normal
10/6/22	17:7:32	33	0.1	390	20.2	3900	3431 G		26.61594	84.60168	Normal
10/6/22	17:7:32	33	0.1	300	20.2	3000	2696 G		26.61507	84.60185	Normal
10/6/22	17:8:7	33	0.1	260	20.2	2600	2370 G		26.61414	84.60199	Normal
10/6/22	17:8:7	33	0.047	180	10.1	3830	3374 G		26.61374	84.60209	Normal

Total IRI	80832
Average IRI Value	2787.31

10/6/22
A

10/6/22
A-E

Executive Engineer
R.W.D. (W.D.)
Aareaj
