

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, अरेराज,

पत्रांक- का0अ0-अरेराज-369 / 1346 (अनु0)

/दिनांक 19/10/2022

प्रेषक :- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल अरेराज।

सेवा में,

अपर मुख्य कार्यपालक पदा0-सह0-सचिव,
बिहार पथ विकास अभिकरण, पटना।

विशय:-

MR(3054) New Maintenance Policy-2018 योजनान्तर्गत अनुरक्षण हेतु राशि की अधियाचना के संबंध में।

प्रसंग-

अभियंता प्रमुख, ग्रामीण कार्य विभाग, बिहार, पटना के पत्रांक- मु0अ0-4(मु0)3054-04-229 / 2021 - 1135 (अनु0) / पटना, दिनांक- 09.03.2022

महाषय,

उपरोक्त विषयक प्रासंगिक पत्र में दिये निर्देश के आलोक में नई अनुरक्षण नीति-2018 अन्तर्गत पथों का अनुरक्षण की राशि के आवंटन हेतु विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः MR(3054) New Maintenance Policy-2018 (Package No. MR-N/19-20 Areraj/-08) योजनान्तर्गत अनुरक्षण हेतु अधियाचना प्रपत्र में दर्शाये गये अधियाचित राशि उपलब्ध कराने की कृपा की जाय। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नहीं है।

अनु0- 1) अधियाचना प्रपत्र।

2) 19 ए प्रपत्र।

3) Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed

4) Standard Formate For Roads Quarterly Statement

विश्वासभाजन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल - अरेराज।

19/10/22
19/10/22

Form GER 19-A
(See Government of India's Decision(1) below Rule – 150)
Form of utilization certificate up to the month of UP to Oct -2022
New Maintenance policy-2018 (Maintenance) (MR-3054)

Sl No.	Name of Scheme	Sanction No.&Date with Amount (in Rs. Lacks)	Amount Received (in Rs. Lacks)	Particulars
1	New Maintenance policy-2018 (Maintenance) (MR-3054)	Letter No. 51 we Date – 30-04-2022 Rs. 141.45374 Letter No. 14 we Date – 18-07-2022 Rs. 31.14948 Letter No. 27 we Date – 26-08-2022 Rs. 141.89764	314.50086	Certified that of Rs 314.50086 Lakh of grants in said sanctioned upto Apr-2020 in favour of RWD, W.D., Areraj sum of Rs. 197.59666 lakh has been utilized New Maintenance policy-2018 (Maintenance) (MR-3054) Scheme as given sanctioned and that the balance of RS 116.90420 lakh
	Total		314.50086	

2. Certified that I have satisfied myself that the conditions on which the grand's- in-aid was sanctioned have been duly fulfilled/ate being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of checks exercised:-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction material has been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.

3. Physical Progress achieved:-

- Construction of The Road works
- Construction of CD Works :-

EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT,
WORKS DIVISION-ARERAJ.

STANDARD FORMATE FOR ROADS QUARTERLY STATEMENT (4th Quarter)

NAME :- Rural Works Department Works Division Arera

1	Name Of Road	parsurampur to Auraliya		
2	Batch No.	RM/EA/ARE/19/0008		
3	Project ID	31708202178		
4	Total Length Of Road(in Km)	4.130		
5	Lenth Of Road To Meet Required Service Level [Completed Length] (in Km) [1]	4.130		
6	N0. of Total Quarter (ie 3 Months as a unit) in 5 year	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount For Maintenance] (in Lakh)	37.96300		
8	Quaterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.89815		
Compliance Criteria	Standard Job Description	Non- Compliance		Reduction Payment [60]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS AND (CARRIAGEWAY)	0	60%	0
II	SHOULDERS AND EMBANMENTS	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGE	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGETATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]				1.89815

date of Inpection by E/I Or His Agent
Prepared by Contractor's Self Control Unit

Name and Designation of person inspecting road

date

Signature of person inspecting road

(Signature)

Certify by E/I [Signature] date

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
(4th Quarter)													
SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT													
Name Of Woks Division:- areaj Government Of Bihar OM01 Rural Works Department				To:- Executive Engineer RWD, Works Division Areaj				Date:-					
Road From:- parsurampur to Auraiya (Package No. MR-N/19-20 Areaj/-08 (MR-3054) Length of Road :- 4.130 KM Period :- From:- 12-06-2021 To 11-09-2021 Inspector :- A.E RWD Sub Division :Harsidhi				Position :- A.E									
No	standard Of Work Item Name	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment	m ²	25.7	28.3	Nil	15.8	1.6						Defects Rectified within stipulated time
OM101	Pothole Patching	m ³	0.09	0.1	Nil	0.02	Nil						Defects Rectified within stipulated time
OM102	Surface Depression and Rut patching	Lm	1000	1000	Nil	1000	130						Defects Rectified within stipulated time
OM103	Crack Sealing												Defects Rectified within stipulated time
OM104	Surface Treatment	m ²	25.7	28.3	Nil	15.8	1.6						No Bleeding/ Flushing Required
	(a) loss of Agregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil	Nil						No Crocodile Cracking Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil						No Edge Repair Required
	@ Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil						
105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil						Not Required
106	Digouts	m ²	Nil	Nil	Nil	Nil	Nil						Not Required
107	Concrete pavement	m ³	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities	m ²											
OM200	Shoulder												Defects Rectified within stipulated time
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	205.18	234.1	Nil	150.3	30.1						Not Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil						No Holding Water Found
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil						Defects Rectified within stipulated time
OM202	Embankment Repair	M ³	40.4	45.8	Nil	25.8	10.5						Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil	Nil						Not Required
OM300	Drainage including culverts major	Lm	Nil	Nil	Nil	Nil	Nil						Not Required
OM301	Surface Drains & Verge	No	2	3	Nil	2	1						Defects Rectified within stipulated time
OM302	Culvert Cleaning	M ³	Nil	Nil	Nil	Nil	Nil						Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities (Whilw washing)	M ²	42	63	Nil	42	21						Defects Rectified within stipulated time

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												Not Required
	Grass Control												Not Required
OM401	(a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil						Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil						Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil	Nil						Defects Rectified within stipulated time
OM402	Cutting Of Branches Of Trees	No	2	3	3	1	Nil						Defects Rectified within stipulated time
	Cutting Of Shrubs From Road Way	No	1000	1000	1000	1000	130						Defects Rectified within stipulated time
	Other activities (Trimming of Grass)	M ²	2250	2250	2250	2250	292.5						Defects Rectified within stipulated time
OM500	Safety Signage and Road												Defects Rectified within stipulated time
OM501	Signs Maintenance	Km	1	1	1	1	0.13						Defects Rectified within stipulated time
OM502	Guard Stones	M ²	4.3	4.5	3.5	3.1	Nil						Defects Rectified within stipulated time
OM503	Distance Stones	Km	1	1	1	1	0.13						Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil	Nil						Not Required
	Other activities												

Bidder

Patel

11/19/12

DE

Appendix

13/19/12
A.C.

Executive Engineer, Works Division (Water)

Signature

Date Time Section Length Bumps Speed OR IRI CATEGORY Latitude Longitude Event
No. in km in mm Rate mm/km mm/km ROAD

ROAD NAME- PARSURAMPUR SE AOIROIYA, CONTRACTOR NAME- M/S SAI ENTERPRISES

$$Y = 0 * X^2 + 0.869 * X + 232.9$$

04/08/22	13:00:21	19	0.1	31	15.0	3100	2927 G	26.362426	84.480989	Normal
04/08/22	13:00:21	19	0.1	30	20.1	3000	2840 G	26.362964	84.480929	Normal
04/08/22	13:01:00	19	0.1	28	23.1	2800	2666 G	26.363471	84.481020	Normal
04/08/22	13:01:32	19	0.1	31	18.2	3100	2927 G	26.363921	84.480999	Normal
04/08/22	13:01:32	19	0.1	28	15.2	2800	2666 G	26.364057	84.480424	Normal
04/08/22	13:01:32	19	0.1	29	16.2	2900	2753 G	26.364246	84.479868	Normal
04/08/22	13:02:07	19	0.1	29	14.3	2900	2753 G	26.364352	84.479313	Normal
04/08/22	13:02:07	19	0.1	30	11.3	3000	2840 G	26.364538	84.478757	Normal
04/08/22	13:02:07	19	0.1	30	15.3	3000	2840 G	26.364586	84.478151	Normal
04/08/22	13:02:42	19	0.1	28	12.3	2800	2666 G	26.364615	84.477595	Normal
04/08/22	13:02:42	19	0.1	30	18.3	3000	2840 G	26.364707	84.476989	Normal
04/08/22	13:03:00	19	0.1	29	23.1	2900	2753 G	26.364918	84.476414	Normal
04/08/22	13:03:17	19	0.1	32	26.1	3200	3014 G	26.365245	84.475969	Normal
04/08/22	13:04:00	19	0.1	28	21.1	2800	2666 G	26.365652	84.475656	Normal
04/08/22	13:04:00	19	0.1	28	16.2	2800	2666 G	26.366024	84.475212	Normal
04/08/22	13:04:28	19	0.1	32	26.2	3200	3014 G	26.366217	84.474676	Normal
04/08/22	13:04:28	19	0.1	28	20.2	2800	2666 G	26.366582	84.474232	Normal
04/08/22	13:05:00	19	0.1	29	15.2	2900	2753 G	26.366998	84.473878	Normal
04/08/22	13:05:03	19	0.1	31	14.3	3100	2927 G	26.367508	84.473898	Normal
04/08/22	13:05:03	19	0.1	31	10.3	3100	2927 G	26.367978	84.474181	Normal
04/08/22	13:05:03	19	0.1	31	15.2	3100	2927 G	26.368185	84.474636	Normal
04/08/22	13:05:39	19	0.1	30	12.3	3000	2840 G	26.368578	84.475050	Normal
04/08/22	13:06:00	19	0.1	31	14.2	3100	2927 G	26.368956	84.475494	Normal
04/08/22	13:06:14	19	0.1	30	12.3	3000	2840 G	26.369336	84.475949	Normal
04/08/22	13:06:14	19	0.1	28	19.2	2800	2666 G	26.369748	84.475989	Normal
04/08/22	13:06:14	19	0.1	31	10.2	3100	2927 G	26.370042	84.476444	Normal
04/08/22	13:06:49	19	0.1	29	15.3	2900	2753 G	26.369747	84.476939	Normal
04/08/22	13:07:00	19	0.1	31	15.2	3100	2927 G	26.369276	84.477141	Normal
04/08/22	13:07:24	19	0.1	28	15.1	2800	2666 G	26.369031	84.477606	Normal
04/08/22	13:07:24	19	0.1	31	16.2	3100	2927 G	26.368782	84.478141	Normal
04/08/22	13:07:24	19	0.1	31	24.2	3100	2927 G	26.368539	84.478646	Normal
04/08/22	13:08:00	19	0.1	28	13.2	2800	2666 G	26.368279	84.479181	Normal
04/08/22	13:08:00	19	0.1	32	15.3	3200	3014 G	26.368054	84.479727	Normal
04/08/22	13:08:35	19	0.1	29	10.2	2900	2753 G	26.367819	84.480262	Normal
04/08/22	13:08:35	19	0.1	28	14.2	2800	2666 G	26.367311	84.480111	Normal
04/08/22	13:09:00	19	0.1	29	11.2	2900	2753 G	26.366782	84.479969	Normal
04/08/22	13:09:10	19	0.1	29	10.3	2900	2753 G	26.366314	84.479787	Normal
04/08/22	13:09:10	19	0.1	28	15.2	2800	2666 G	26.365892	84.479888	Normal
04/08/22	13:09:46	19	0.1	28	15.3	2800	2666 G	26.365701	84.480424	Normal
04/08/22	13:09:46	19	0.1	30	18.2	3000	2840 G	26.365518	84.480989	Normal
04/08/22	13:10:00	19	0.1	32	13.2	3200	3014 G	26.365308	84.481555	Normal
04/08/22	13:10:21	19	0.1	28	15.2	2800	2666 G	26.365055	84.482121	Normal

TOTAL 117888

AVERAGE 2806.86

4/8/22
06

13/9/22
A73

Executive Engineer
R.W.D. (W.D.)
Areraj

Name of Customer : M/S SAI ENTERPRISES

Name of Work/ Road : PARSURAMPUR SE AOIROIYA

Lab Job number :

Date : 04-08-2022

Section No. : 19

Test Date : 04-08-2022

Road Name : PARSURAMPUR SE AOIROIYA

Machine No : 406

Road Type : (R) RURAL ROAD

Start S No :

Start E No :

Side :

Interval :

Weather :

UIV Range : 1666 To 4000 1000 mm/km

Start Location : SURAMPUR

Dist Range : 0 To 4.3 0.1 * 1000 m

End Location : AOIROIYA


Equation : test

Print

Generate Report and Graph

Redraw Graph

Map View

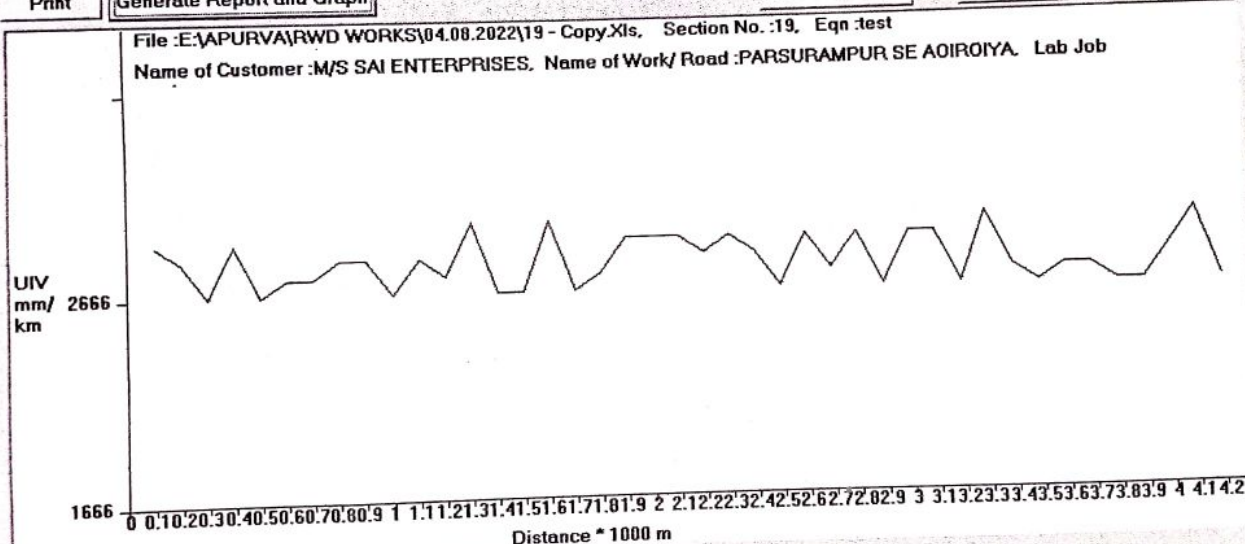

4/8/22
JB

13/9/22
A-8

19/10/22

Executive Engineer
R.W.D. (W.D.)
Areraj
