

पत्रांक...1387(अप्र)/

शेखपुरा, दिनांक...16/08/22 ✓

प्रेषक:--

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, शेखपुरा।

सेवा में,

नोडल पदाधिकारी,
3054 (M.R.) कोषांग,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-- शीर्ष 3054 नई अनुरक्षण नीति-2018 अन्तर्गत पंचवर्षीय Routine Maintenance कराये गए कार्य हेतु अधियाचना के संबंध में।


महाशय,

• उपर्युक्त विषयक कहना है कि विहित प्रपत्र में संलग्न विवरणी के अनुसार शीर्ष 3054 नई अनुरक्षण नीति-2018 अन्तर्गत पंचवर्षीय Routine Maintenance कराये गए कार्य हेतु राशि रुपये 3,12,798/- (तीन लाख बारह हजार सात सौ अठानवे रुपये) मात्र राशि की आवश्यकता है।

अतः कार्यहित में अनुरोध है कि उक्त अधियाचित राशि रुपये 3,12,798/- (तीन लाख बारह हजार सात सौ अठानवे रुपये) मात्र उपलब्ध कराने की कृपा की जाय। ताकि कराये गये कार्य का भुगतान किया जा सके।

अनु०:—यथोक्त।

विश्वासभाजन


कार्यपालक अभियन्ता
ग्रा०का०वि०, कार्य प्रमण्डल,
शेखपुरा

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Unit of Works Division:- Sheikhpura

Road Details				AA Details		Agreement					Actual Maintenance Expenditure						Current Maintenance Demand					Remarks					
No	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in Lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in Km)	1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	ERI As per lump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	Total
1	Barbigha Machur Road To Dumari Road	RM/SH/SH E/19/0001	20803902195	12.05.2021	10.81	6.37	10.24228	119075	119075	119075	119075	119075	595374.0	0.600	Nil	Nil	Nil	Nil	Nil	Nil	3541	0.29769	0.29769	-	-	-	0.59538
2	Kemra Belkhandi Road	RM/SH/SH E/19/0001	20803902039	25.06.2021	25.27	14.73	23.87638	278765	278765	278765	278765	278765	1393826.0	1.396	Nil	Nil	Nil	Nil	Nil	Nil	3643	0.69691	-	-	-	-	0.69691
3	Sheikhpura Sahpur Path To Sabanaura	RM/SH/SH E/19/0003	20803901031	11.06.2021	6.35	3.26	5.90758	61353	61353	61353	61353	61353	306765.0	0.350	Nil	Nil	Nil	Nil	Nil	Nil	3337	0.15338	-	-	-	-	0.15338
4	Chorbar Baruni NAGSY Path To Dharsi	RM/SH/SH E/19/0003	20803901027	09.06.2021	12.75	7.04	12.06417	132790	132790	132790	132790	132790	663952.0	0.700	Nil	Nil	Nil	Nil	Nil	Nil	3950	0.33198	-	-	-	-	0.33198
5	Sheikhpura-Sumka Path To Sasbana Village, Via-Batran Bigha	RM/SH/SH E/19/0003	20803901037	09.06.2021	17.28	10.05	16.30612	188594	188594	188594	188594	188594	942971.0	0.975	Nil	Nil	Nil	Nil	Nil	Nil	3745	0.47149	-	-	-	-	0.47149
6	Manipur Pul To Manipur Mahadati Tola	RM/SH/SH E/19/0003	20803905003	09.06.2021	30.11	18.67	28.48397	351538	351538	351538	351538	351538	1757688.0	1.850	Nil	Nil	Nil	Nil	Nil	Nil	3439	0.87884	-	-	-	-	0.87884
Total =				102.57	60.12	96.8805	1132115	1132115	1132115	1132115	1132115	1132115	5660576	5.8710	0.00	0.000	0.000	0.000	0.000	0.000		2.83029	0.29769	0.00000	0.00000	0.00000	3.12798

Amount in Word :- Three Laacs Twelve Thousand Seven Hundred Ninety Eight Only.

R.W.D. (W) Division,
Sheikhpura

Md. 16/8/22
SR

16.8.22
HE

Executive Engineer
R.W.D. (W) Division,
Sheikhpura

1st Quarter

Government of Bihar
OM01Q

Rural Works Department

Road From :- Kemra Belkhundi Road

Length of Road :- 1.396Km.

Period :- From 25.06.2021 To 24.09.2021

Inspector :- Pankaj Kumar

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

From - OM01

Position :- J.E.

Date

Standard work item			Units of work required in each kilometre										Comments
No.	Name	Work Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM 101	Pothole Pitching	m ²	-										
OM 102	Surface Depression and Rut Patching	m ²	-										
OM 103	Crack Sealing	Lm	-										
OM 104	Surface Treatment												
	(a) Loss of Agreement (Surface Ravelling)	m ²	-										
	(b) Bleeding/Flushing	m ²	-										
	(c) Crocodile Cracking	m ²	-										
OM 105	Edge Repair	m ²	-										
OM 106	Digouts	m ²	-										
OM 107	Concrete Pavement	m ³	-										
	Other activities												
OM200 Sealed Pavement													
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	1										
	(b) Roughness, Scouring or Potholes	Lm	-										
	(c) Holding water	Lm	-										
OM202	Embankment Repair	No.	-										
	Other activities												
BLAY CONSTRUCTION													

BIHAR CONSTRUCTION

Biya Shama prash...

Appendix

[Signature]
J.E.

[Signature]
A.E.

[Signature]
E.E.

Contract PROPRIETOR

RWD (W) Section,
Chewara

RWD (W) Sub Division,
Chewara

RWD (W) Division,
Sheikhpura

Standard work item		Work	Units of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	-										
OM302	Culvert Cleaning	Lm	-										
OM303	Culvert and Pit Repair												
	Other activities												
OM400 Vegetation													
OM401	Grass Control												
	a) Roadside - General Tidy	Ha	-										
	b) Clear near, safety signs, kilometre posts and roadside furniture	Ha	0.1										
OM402	Tree and Shrub Management	Ha	-										
	Other activities												
OM500 Signage and Road Safety													
OM501	Signage and Maintenance	No.	-										
OM502	Guard Stones	Lm	1										
OM503	Distance Stones	No.	1										
OM504	Road Marking	No.	-										
	Other activities												

(Signature of Contractor/Authorized Representative)

Bijay Shannur Prasad

Date

08/12/2018

J.E.

Time

10:00 AM

A.E.

Place

16-8-18

E.E.

Note :- Enclose photographs with the report.

RWD (W) Section,
Chewara

RWD (W) Sub Division,
Chewara

RWD (W) Division,
Sheikhpura

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :-R.W.D. (W) Division, Sheikhpura

Quarter :- 1st

Period :- From- 25.06.2021 To 24.09.2021

1	Name of The Road	Kemra Belkhundi Road		
2	Batch No.	RM/SH/SHE/19/0001		
3	Project ID	20803902039		
4	Total Length of Road (in Km)	1.396		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	1.396		
6	No. of Total Quarter (ie 3 Months as s unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	13.93826		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0.69691		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6] = [3]/[1] * [2] * [4]
		Length Non-Compliant [3]	Weight Value for Payment Reduction (%) [4]	
I	PAVED ROAD (CARRIAGEWAY)	-	60%	-
II	SHOULDERS AND EMBANKMENT	-	10%	-
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	-	15%	-
IV	SIGNAGE AND ROAD SAFETY	-	10%	-
V	VEGATION	-	5%	-
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				-
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [6]				-

Date of inspection by E/I or his agent

Prepared by Contractor's self Control unit

BIJAY CONSTRUCTION
Bijay Shankar Prasad

Date

PROPRIETOR

Asst
16.7.22

Signature of Person inspecting Road

Assistant Engineer

R.W.D.(W) Sub Division,
Chewara

Name and Designatin of person inspecting road

Pankaj Kumar

Junior Engineer

RWD(W) Section, Chewara

Certify by

Executive Engineer

R.W.D.(W) Division,
Sheikhpura

Name of Customer :	Bijay Construction
Name of Work/ Road :	Kemra Belkundi Road
Lab Job number :	40
Date :	08.08.2022
Section No. :	40


Test Date :	08.08.2022	Road Name :	Kemra Belkundi Road
Machine No. :	411	Road Type :	(R) RURAL ROAD
Start S No. :		Side :	
Start E No. :		Interval	
Weather :		U/V Range :	2235 To 5000 mm/km
Start Location :		Dist Range :	0 To 1.4 0.1 * 1000 m
End Location :		Equation :	$Y = 0 * X^2 + 1.021 * X - 31.77$

Print Generate Report and Graph

Redraw Graph

Map View

File : E:\MR New Maintenance Policy\26.09.2021\For Routine Maintenance\08081055.Xls. Section No. : 40, Egn : Y =
 Name of Customer : Bijay Construction, Name of Work/ Road : Kemra Belkundi Road, Lab Job number : 40

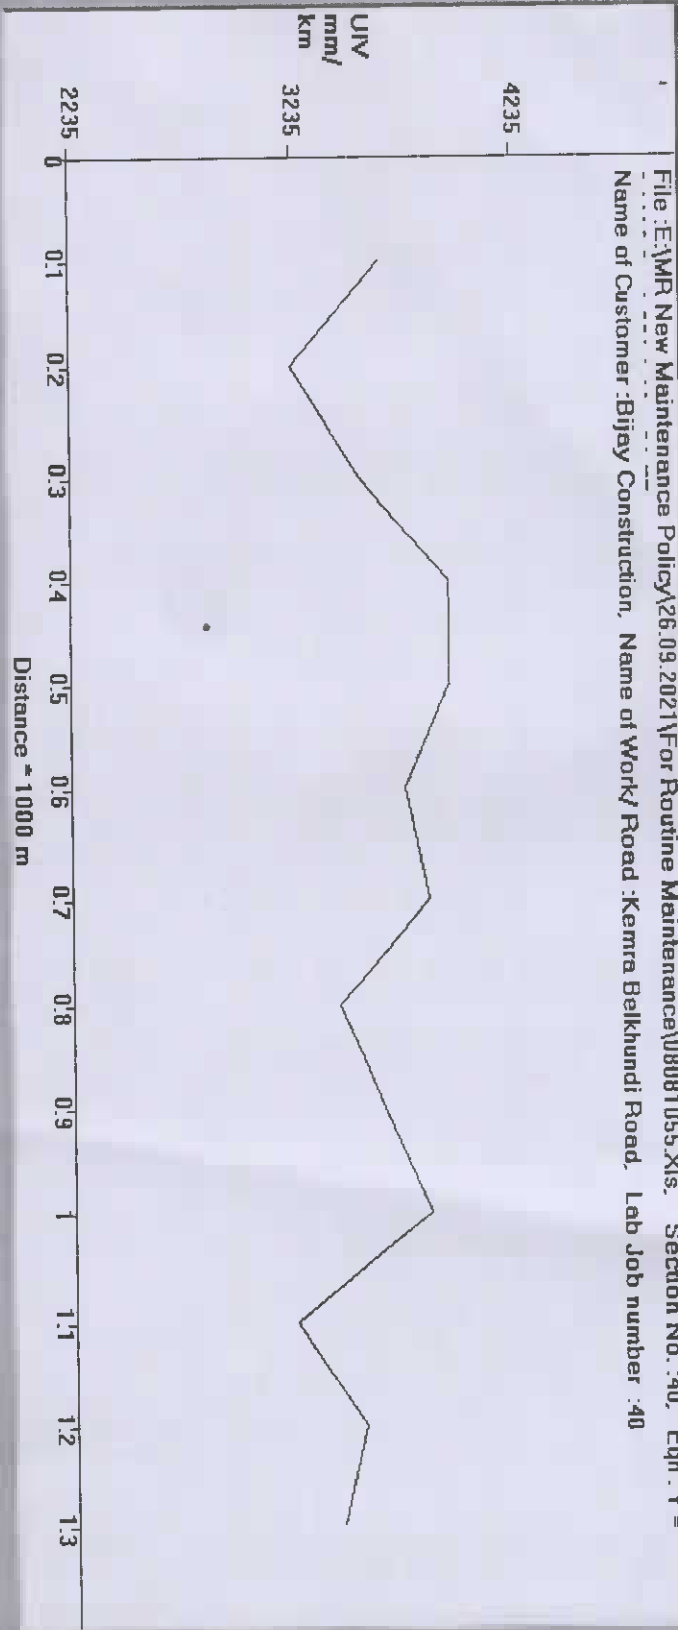

R. Kumar
 16.8.2022
 16.8.22
 16.8.22
 16.8.22
 Executive Engineer
 Rural Works Department
 Works Division, Sheikhpura

Name of Road :- Kemra Belkhundi Road.
Section no.-40

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
8/8/22	10:46:16	40	0.1	360	0	3600	3643	G	25.7074	85.881918	Normal
8/8/22	10:46:52	40	0.1	320	10.1	3200	3235	G	25.69952	85.881497	Normal
8/8/22	10:47:00	40	0.1	350	10.1	3500	3541	G	25.69175	85.881447	Normal
8/8/22	10:47:26	40	0.1	390	10.1	3900	3950	G	25.68268	85.881295	Normal
8/8/22	10:51:5	40	0.1	390	10.1	3900	3950	G	25.6738	85.878585	Normal
8/8/22	10:52:0	40	0.1	370	10.1	3700	3745	G	25.67438	85.877592	Normal
8/8/22	10:52:18	40	0.1	380	10.1	3800	3848	G	25.68322	85.877793	Normal
8/8/22	10:53:0	40	0.1	340	10.1	3400	3439	G	25.68445	85.87682	Normal
8/8/22	10:53:29	40	0.1	360	10.1	3600	3643	G	25.6858	85.875823	Normal
8/8/22	10:54:0	40	0.1	380	10.1	3800	3848	G	25.68658	85.874848	Normal
8/8/22	10:54:4	40	0.1	320	10.1	3200	3235	G	25.68803	85.87382	Normal
8/8/22	10:55:0	40	0.1	350	10.1	3500	3541	G	25.69097	85.87303	Normal
8/8/22	10:55:5	40	0.1	340	10.1	3400	3439	G	25.69097	85.87303	Normal

1.3

16/8/22
SE

16/8/22
AC

Executive Engineer
R.W.D.(W) Division,
Sheikhpura
