

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जहानाबाद।

पत्रांक: 2075 /

जहानाबाद, दिनांक: 26.8.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

सेवा में,

नोडल पदाधिकारी, MR 3054
ग्रामीण कार्य विभाग,
बिहार, पटना।


विषय :- शीर्ष Bihar Rural Road Maintenance Policy -2018 अन्तर्गत कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष Bihar Rural Road Maintenance Policy -2018 अन्तर्गत पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर समर्पित किया जाता है।


अनु० - यथोक्त।

विश्वासभाजन,


26/8/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।
26.8.22 26/8/22

MR 5 year Routine Maint.

Road Details										AA DETAILS		Agreement Details										Previous Maintenance		Length as per Report		(Current Budget for Maintenance Amount)					Remarks
Sl. No.	Road Name	Batch No.	Project ID	Date	Main Work Amount	Maintenance Amount	Main Work Amount	Agreement Mt 1	Agreement 2	Agreement 3	Agreement Mt 4	Agreement Mt 5	Agreement Mt 6	Total Maintenance Amount	Length	alignment	Total	alignment	1st quarter	2nd quarter	3rd quarter	4th quarter	5th quarter	6th quarter	7th quarter						
1	Alua Bigha to Birra	RN/1E/244/19/0005	10603002257	13/12/2020	29.9703	14.1137	28.014	2.65732	2.65732	2.65732	2.65732	2.65732	2.65732	13.2866	1.36	1.32866	1.32866	1.36	0.66433	0.66433	0.66433	0.66433	0.00	1.99299	4.066245	1st, 2nd & 3rd quarter					
2	Ner to Katsasin road.	RN/1E/244/19/0005	10603003028	13/12/2020	84.328	28.618	77.801	5.42166	5.42166	5.42166	5.42166	5.42166	5.42166	27.1063	3.9	2.7108	2.71	3.9	1.35542	1.35542	1.35542	0.00	4.066245	15.2nd & 3rd quarter							
3	REO Road Bishunganj to Jamanganj	RN/1E/244/19/0005	10603002263	12/11/2020	49.49331	18.8857	46.32	3.5686	3.5686	3.5686	3.5686	3.5686	3.5686	17.843	2.2	0.8922	0.8922	2.2	0.89215	0.89215	0.89215	0.89215	0.89215	3.56660	15.2nd, 3rd & 4th quarter						
4	Saguna village to Rampur via Pratapbigha.	RN/1E/244/19/0005	10603001022	14/12/2020	49.44465	18.7524	46.345	3.55502	3.55502	3.55502	3.55502	3.55502	3.55502	17.7751	2.1	0.8888	0.8888	2.1	0.88876	0.88876	0.88876	0.00	2.66627	15.2nd & 3rd quarter							
Total					213.2363	80.36974	198.48	15.2026	15.2026	15.2026	15.2026	15.2026	15.2026	76.013	9.56	5.82040	5.82040	9.56	3.80065	3.80065	3.80065	0.89215	12.29410								


 Executive Engineer
 Road Works Division, Jamnagar

Name of Customer:
 Name of Work/ Road:
 Lab Job number:
 Date:
 Section No.

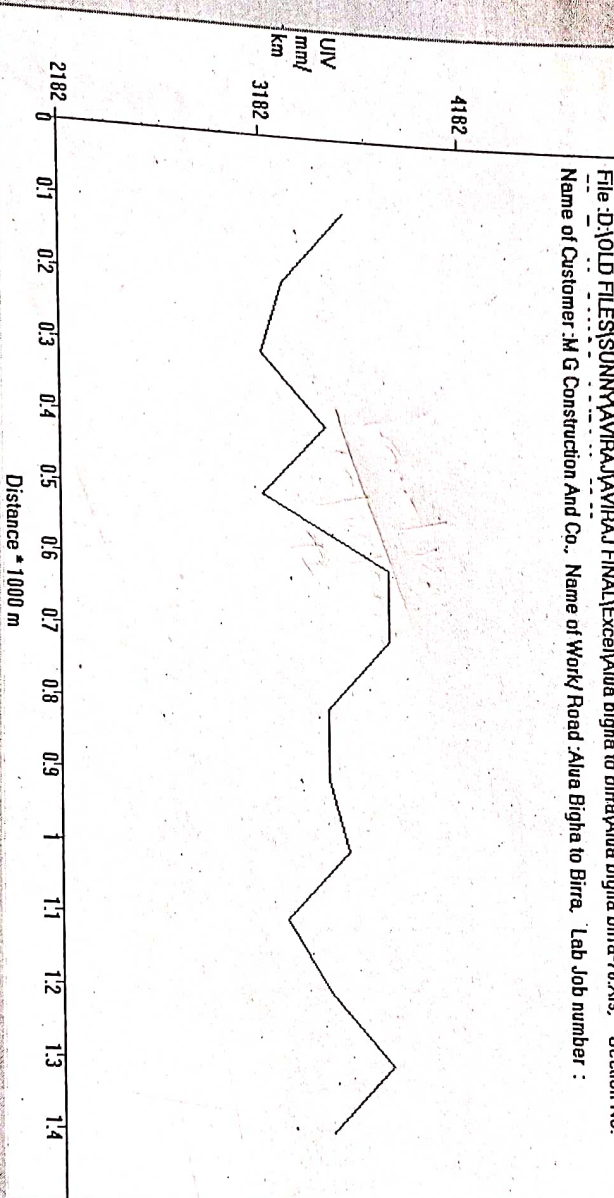
Test Date:
 Machine No:
 Start S No:
 Start E No:
 Weather:
 Start Location:
 End Location:
 Road Name:
 Road Type:
 Side:
 UIV Range: To Interval
 Dist Range: To * 1000 m
 Equation: $Y = 0 * X^2 + 1.047 * X - 63.36$

Print Generate Report and Graph

Redraw Graph

Map View

File: D:\OLD FILES\SUNNYAVIRAJ\AVIRAJ FINAL\Excel\Alua bigha to birra\Alua bigha birra-76.Xls. Section No.
 Name of Customer: M G Construction And Co., Name of Work/ Road: Alua Bigha to Birra. Lab Job number:



Handwritten signature: *Handwritten signature*
 Date: 09/08/2022
 Initials: JE

Handwritten signature: *Handwritten signature*
 Date: 09/08/2022
 Initials: JE

Name of Customer: MG Construction And Co.
Name of Work/ Road: Alua Bigha to Birra

Date	Time	Section No.	Length In km	Bumps In mm	Speed Rate	OR mm/km	IRI/TEGORY ROAD	Latitude	Longitude	Event
9/8/22	8:48:0	76	0.1	320	10.1	3200	3287 G	25.7264	85.32777	Normal
9/8/22	8:48:25	76	0.1	320	10.1	3200	3287 G	25.735	85.32928	Normal
9/8/22	8:49:0	76	0.1	310	20.2	3100	3182 G	25.74452	85.33097	Normal
9/8/22	8:49:0	76	0.1	320	10.1	3200	3287 G	25.7536	85.33215	Normal
9/8/22	8:49:35	76	0.1	310	20.2	3100	3182 G	25.76252	85.3	Normal
9/8/22	8:49:35	76	0.1	320	10.1	3200	3287 G	25.77122	85.3343	Normal
9/8/22	8:50:10	76	0.1	310	20.2	3100	3182 G	25.78038	85.33535	Normal
9/8/22	8:50:10	76	0.1	340	10.1	3400	3496 G	25.78982	85.33635	Speed Breaker
9/8/22	8:50:46	76	0.1	340	10.1	3400	3496 G	25.79863	85.3367	Speed Breaker
9/8/22	8:51:21	76	0.1	320	10.1	3200	3287 G	25.8081	85.3372	Normal
9/8/22	8:51:21	76	0.1	320	10.1	3200	3287 G	25.81678	85.33938	Normal
9/8/22	8:55:0	76	0.1	340	10.1	3400	3496 G	25.81597	85.33938	Normal
9/8/22	8:55:27	76	0.1	310	20.2	3100	3182 G	25.8072	85.3372	Normal
9/8/22	8:56:2	76	0.1	310	20.2	3100	3182 G	25.79787	85.33687	Normal

$$Event: Y = 0 * X^2 + 1.047 * X - 63.36$$

Heart K.
09/08/2022
JE

9/8/22
JE

1st Quarter

Form

Government of Bihar
OM01
Rural Work DepartmentORDINARY MAINTENANCE INSPECTION REPORT
Form OM01To: ... Executive Engineer
RWD, Works Division Jehanabad

Date : ...

Road From : Alua Bigha to Birra
Length of Road : 1.36 Km.

Period:- from 14.12.20 to 13.03.21

Inspector : ... J.E., RWD Sub Division Makhdumpur

Position : ... J.E.

No.	Name	Work	Units	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement													
OM101	Pothole Patching		m ²	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut patching		m ²	Nil	Nil	Nil	Nil							No Surface Depression and Rut patching found.
OM103	Crack Sealing		Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)		m ²	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding / Flushing		m ²	Nil	Nil	Nil	Nil							No Bleeding / Flushing Required
	(c) Crocodile Cracking		m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair		m ²	N.A.	N.A.	N.A.	N.A.							No Edge Repair Required
OM106	Digouts		m ²	N.A.	N.A.	N.A.	N.A.							
OM107	Concrete Pavement		m ³	N.A.	N.A.	N.A.	N.A.							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder		Lm	Nil	Nil	Nil	Nil							No Edge Drop-off Required
	(a) Edge Drop-off		Lm	Nil	Nil	Nil	Nil							No Roughness, Scouring or Potholes Required
OM201	(b) Roughness, Scouring or Potholes		Lm	Nil	Nil	Nil	Nil							No Holding water Found
	(c) Holding water		M ³	Nil	Nil	Nil	Nil							No Embankment Repair Required
OM202	Embankment Repair		M ³	N.A.	N.A.	N.A.	N.A.							
	Other activities													
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge		Lm	N.A.	N.A.	N.A.	N.A.							Not Required
OM302	Culvert Cleaning		No.	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair		M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Waste Washing)		M ²	Nil	Nil	Nil	Nil							Not Required

Appendix

Executive Engineer, Works Division

Executive Engineer,
R. W. D. (W) DivisionDate: 12/03/2021
Signature

Standard work item No.	Name	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400 Vegetation	Grass Control												
	a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM401													
OM402	Tree and Shrub Management (Cutting Trees)	No.	Nil	Nil	Nil	Nil							Not Required
	(Cutting shrubs)	No.	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No.	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM503	Distance Stones	No.	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM504	Road marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

(Signature of Contractor/Authorized representative)

Date

Time

Place

Note:- Enclose photographs with this report.

Handwritten signature
22/04/2022
fe

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	Alua Bigha to Birra		
2	Batch No.	RM/JE/JAH/19/005		
3	Project ID	10603002257		
4	Total Length of Road (In km.)	1.400		
5	Length of Road to Meet Required Service Level {Completed Length} (In km) [1]	1.400		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	1st		
7	Ordinary Maintenance Cost as per Shedule [Agreement Amount for Maintenance) in lakh	14.1137		
8	Quarterly Payment:1/20 of Ordinary Maintenance Cost as per shedule (in Lakh) [2]	0.66433		
Compliance Criteria	Standard job Decription	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.66433

Date of inpection by E/I or his agent
Prepared by contractor's self control unit

PRANET KUMAR JE / MOKS / mps

Name and Designation of person inspecting road

Pranet K. S.
24/04/2022
Signature

Date
Signature of person inspecting road
