

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, टिकारी।

पत्रांक: 1839 3-ख/9

टिकारी, दिनांक: 3.9.22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, टिकारी।

सेवा में,

नोडल पदाधिकारी, MR 3054
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनु० - यथोक्त।

विश्वासभाजन,

8/9/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, टिकारी।

Division: Tekant

Maintenance Requestion Formate for Scheme Head- MR (0654) under Bihar Rural Road Maintenance Policy - 2018 (Initial Identification and Surface Renewal)

Road Details					AA Details																				Remarks							
S. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Agreement (in lakh)										Actual Maintenance Expenditure (in Lakh)											Current Maintenance Demand						
					Main Work Amount (in lakh)	Agreement m-1	Agreement m-2	Agreement m-3	Agreement m-4	Agreement m-5	Total Agreement	Length (in Km)	1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length (in Km)	Corrected Length (in Km)	1st QTR Maintenance (in lakh)	2nd QTR Maintenance (in lakh)	3rd QTR Maintenance (in lakh)	4th QTR Maintenance (in lakh)		Total						
1	Repair and Maintenance of Road from 20/000 Bela Barabar Road to Bhagwanpur	3	15221033208	09-02-2021	27.1	13	26.82200	1.1126	1.6514	4.1089	2.0039	4.295	13.17217	1.30	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.000	35.49	0.65861	0.65861	0.65861	0.00000	1.97583	Dhirenendra Kumar Singh
2	Repair and Maintenance of Road from 20/000 Rauna shripur to Bithaur	3	15221033209	04-02-2021	6.03	3.1	6.33500	0.2582	0.384	0.9206	0.4637	0.978	3.00429	0.30	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.30000	34.37	0.15021	0.15021	0.15021	0.00000	0.45064	Dhirenendra Kumar Singh	
3	Repair and Maintenance of Road from 20/000 Rauna shripur to Diba	3	15221033210	10-02-2021	17.7	9.8	17.50800	0.8218	1.2215	3.0054	1.4718	3.122	9.64254	0.95	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.95000	32.10	0.48213	0.48213	0.48213	0.00000	1.44638	Dhirenendra Kumar Singh		
4	Repair and Maintenance of Road from 20/000 Rauna shritut to Dail Bigha	3	15221033211	09-03-2021	31.9	14	31.80400	1.199	1.7828	4.4143	2.1533	4.636	14.1881	1.40	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.60000	31.81	0.70924	0.70924	0.00000	0.00000	1.41848	Dhirenendra Kumar Singh		
5	Repair and Maintenance of Road from NH-83 Neunti to Bataspur	3	15221033212	13-02-2021	42.3	20	41.90300	1.7334	2.5877	6.471	3.1389	5.613	19.54435	2.05	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.60000	33.48	0.97722	0.97722	0.97722	0.00000	2.93165	Dhirenendra Kumar Singh		



Name of work : Repair and Maintenance of Road from Rauna shripur to Bithraura
Name of customer : Dharendra Kumar Singh


(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitud e	Direction1	Remarks
16-08-22	18:01:21	65	100	100	30.0 cm	12.7 Km/Hr	3000.0 mm/Km	3127	4.18	Good	24 9205294	N	85 0336924	E	Normal
16-08-22	18:01:41	65	100	200	38.0 cm	18.0 Km/Hr	3800.0 mm/Km	3871	5.06	Good	24 9207774	N	85 0326014	E	Normal
16-08-22	18:02:01	65	100	300	32.0 cm	18.1 Km/Hr	3200.0 mm/Km	3313	4.4	Good	24 9209891	N	85 0318842	E	Normal
Total Length			300					3437							

11/9/22
173

11/9/22

Name of Customer: Dharendra Kumar Singh, Machine no: 19211, Road: Repair and Maintenance of Road from Ramra shripur to Bithaura, Date: 24/08/22, Section No: 65, Equation: $Y = -0.931X + 233.6$

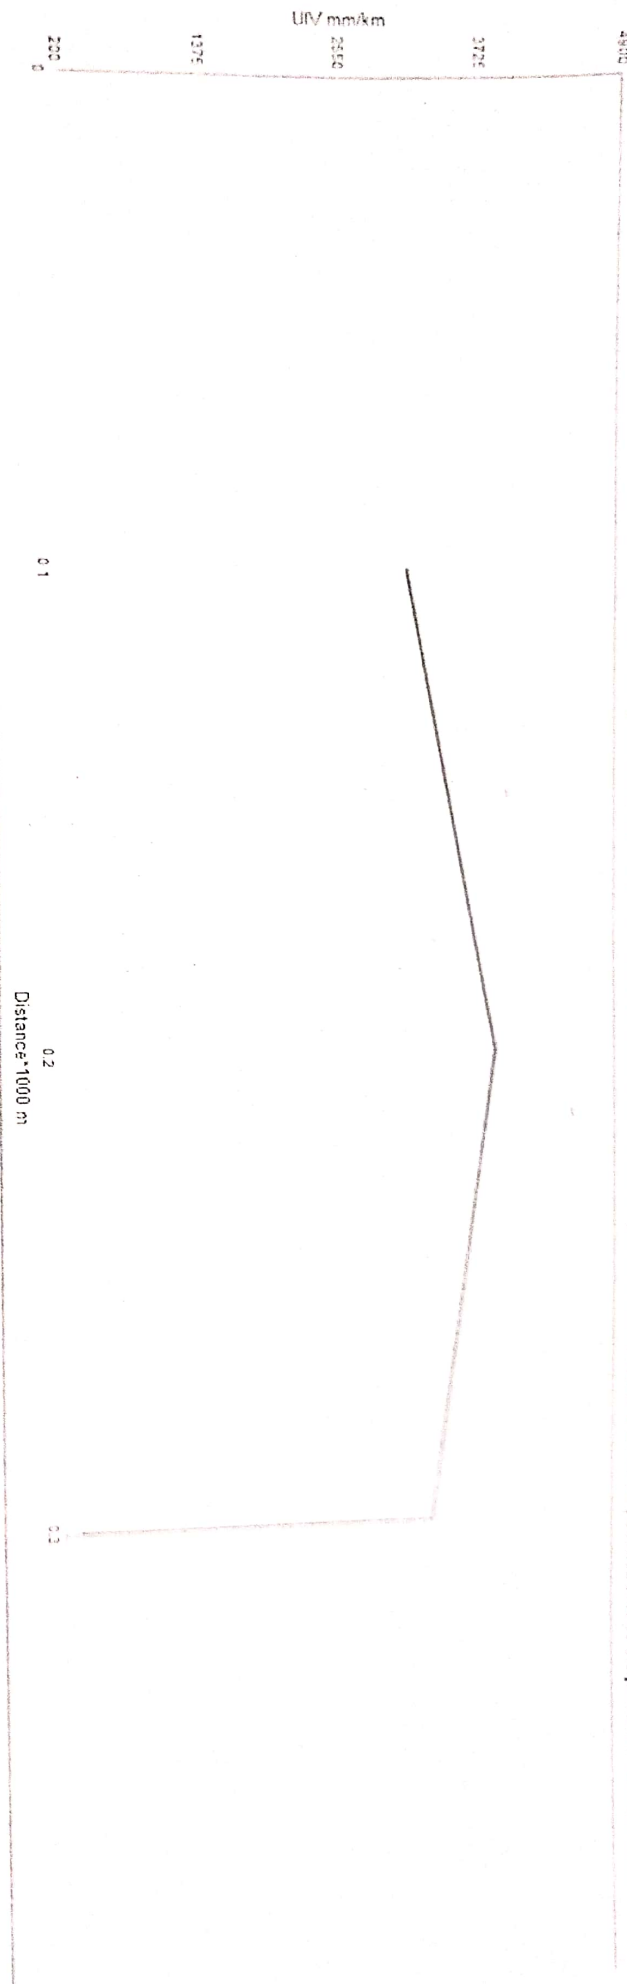

19/12/22

20/10/22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	Repair and Maintenance of Road from Rauna shripur to Bithraura		
2	Batch No.	RM/GA/TIK/20/0003		
3	Project ID	15221033209		
4	Total Length of Road (in km.)	0.300 km		
5	Length of Road to Meet Required Service Level {Completed Length} (in km) [1]	0.300 km		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	2nd		
7	Ordinary Maintenance Cost as per Shedule [Agreement Amount for Maintenance) in lakh	3.00429		
8	Quarterly Payment: 1/20 of Ordinary Maintenanace Cost as per shedule (in Lakh) [2]	0.15021		
Compliance Criteria	Standard job Decription	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
I	Paved Roads (CARRIAGEWAY)	Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	0.00
II	SHOULDERS AND EMANMENTS	0%	60%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	10%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	15%	0.00
V	VEGATAION	0%	10%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]		0%		5%
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.00
				0.15021

Date of inspection by E/I or his agent
Prepared by contractor's self control unit

Name and Designation of person inspecting road

Date
Signature of person inspecting road



Government of Bihar
OM01
Rural Work Department

ORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Form

Road Repair and Maintenance of Road from Rauna
From :- shripur to Bithraura

Length of Road : 0.300 Km.

Period:- from 05.05.2021 to 04.08.2021

Inspector :J.E., RWD Sub Division Belaganj

To : ... Executive Engineer

RWD, Works Division Tekari

Date : ...

Position : J.E


Standard work Item		Work	Unit of work required in each kilometre										Comments
No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m ²	Nil										No. Pothole found.
OM102	Surface Depression and Rut patching	m ²	Nil										No Surface Depression and Rut patching found.
OM103	Crack Sealing	Lm	Nil										No Crack Sealing found
OM104	Surface Treatment												No Loss of Agreagate (Surface Ravelling) found
	(a) Loss of Agreagate (Surface Ravelling)	m ²	Nil										No Bleeding / Flushing Required
	(b) Bleeding / Flushing	m ²	Nil										No Crocodile Cracking found
	(c) Crocodile Cracking	m ²	Nil										No Edge Repair Required
OM105	Edge Repair	m ²	Nil										
OM106	Digouts	m ²	N.A.										
OM107	Concrete Pavement	m ³	N.A.										
	Other activities												
OM200 Shoulder													
OM201	Unsealed Shoulder												No Edge Drop-off Required
	(a) Edge Drop-off	Lm	Nil										No Roughness, Scouring or Potholes Required
	(b) Roughness, Scouring or Potholes	Lm	Nil										No Holding water Found
	(c) Holding water	Lm	Nil										No Embankment Repair Required
OM202	Embankment Repair	M ³	Nil										
	Other activities		N.A.										
OM300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A.										Not Required
OM302	Culvert Cleaning	No.	Nil										Not Required
OM303	Culvrt and pit Repair	M ³	Nil										Not Required
	Other activities (White Washing)	M ²	Nil										

Executive Engineer, Works Division Tekari

Appendix

Bidder

Standard work Item		Work	Unit of work required in each kilometre										Comments	
No.	Name	Units	1	2	3	4	5	6	7	8	9	10		
OM400 Vegetation														
OM401	Grass Control													
	a) Roadside- General Tidy	Ha	Nil										Not Required	
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil										Not Required	
OM402		No.	Nil										Not Required	
	Tree and Shrub Management	No.	Nil										Not Required	
	(Cutting Trees)	No.	Nil										Not Required	
	(Cutting shrubs)	No.	Nil										Not Required	
	Other activities (Trimming of Grass)	M ²	Nil										Not Required	
OM500	Safety Signage and Road												Not Required	
OM501	Signs Maintenance	No.	Nil										Not Applicable	
OM502	Guard Stones	Lm	N.A.										Not Applicable	
OM503	Distance Stones	No.	N.A.										Not Required	
OM504	Road marking	M ²	Nil											
	Other activities													


 (Signature of Contractor/Authorized representative)

Date

Time

Place

Note:- Enclose photographs with this report.

