

कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमण्डल, औरंगाबाद

पत्रांक 1938 अनु0

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, औरंगाबाद।

सेवा में,

नोडल पदाधिकारी, (MR304

ग्रामीण कार्य विभाग, पटना, बिहार।

औरंगाबाद, दिनांक 09-09-2022

विषय:-


नई अनुरक्षण नीति-2018 MR(3054) योजना के अन्तर्गत पाँच वर्षीय रख-रखाव पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR(3054) योजना के अन्तर्गत पाँच वर्षीय रख-रखाव पथ में कराये गये कार्य के लिए सम्वेदक को भुगतान करने हेतु अधिचाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु0:-आवंटन माँग पत्र की प्रति संलग्न।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, औरंगाबाद।


21/9/22

Name of Works Division:- Aurangabad

RYD, Works Division
Murangabad (Bihar)

Executive Engineer
RWD, Works Division
Aurangabad (Bihar)

Name of Customer :	Priye Ranjan kr singh
Name of Work/Road :	Risip Maharaigamj rd to Haneya
Lab Job number :	
Date :	03-09-2022
Section No.	63

Test Date :	03-09-2022	Road Name :	
Machine No :		Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		U/V Range :	1044 To 4000 1000 mm/km
Start Location :		Dist Range :	0 To 2.9 0.1 * 1000 m
End Location :		Equation :	$Y = 0 * X^2 + 0.816 * X + 249$

Print

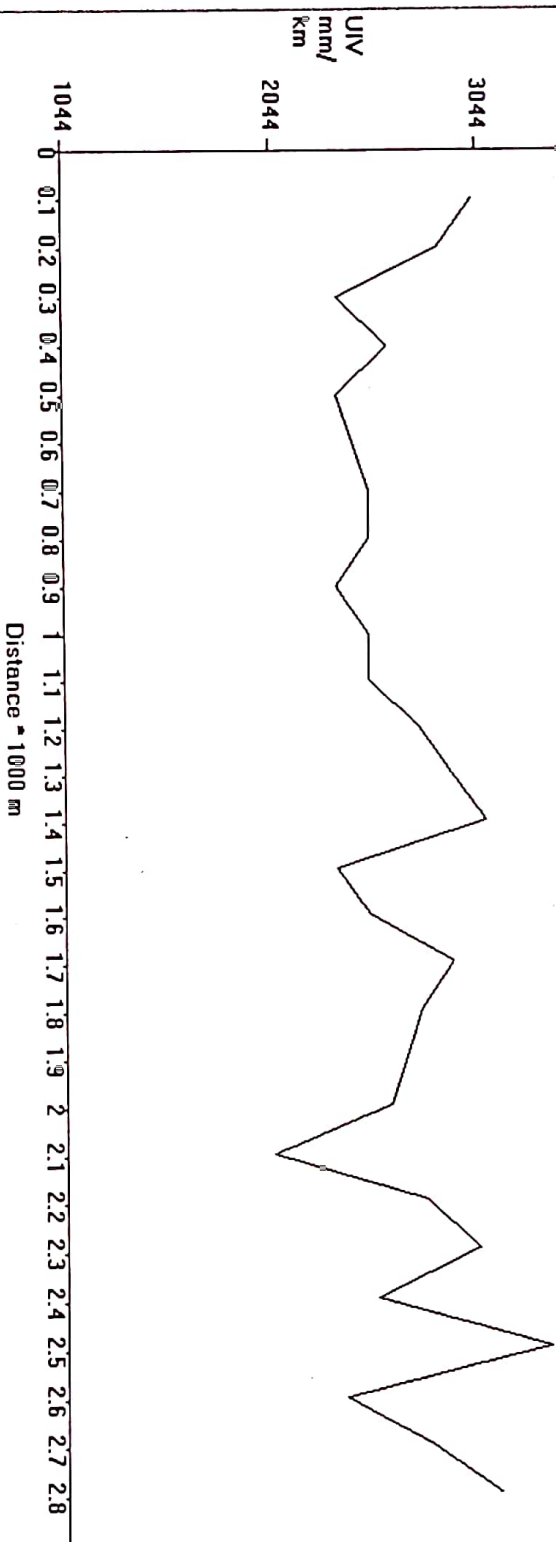
Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\HP\Desktop\Bump Indicator 28.05.2022\Priyeranjan\63.xlsx Section No. : 63. Eqn : $Y = 0 * X^2 +$

Name of Customer : Priye Ranjan kr singh. Name of Work/Road : Risip Maharaigamj rd to Haneya. Lab Job



JE

AE

EE

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	ongitude	Event
03/9/22	14:55:21	63	0.1	340	0	3400	3023	G	24.55198	84.24746	Normal
03/9/22	14:56:0	63	0.1	320	10.1	3200	2860	G	24.55115	84.24781	Normal
03/9/22	14:56:0	63	0.1	260	20.2	2600	2370	G	24.55025	84.2481	Normal
03/9/22	14:56:31	63	0.1	290	20.2	2900	2615	G	24.54941	84.24835	Normal
03/9/22	14:56:31	63	0.1	260	20.2	2600	2370	G	24.54854	84.24862	Normal
03/9/22	14:57:0	63	0.1	270	20.2	2700	2452	G	24.5477	84.24859	Normal
03/9/22	14:57:6	63	0.1	280	20.2	2800	2533	G	24.54679	84.24854	Normal
03/9/22	14:57:42	63	0.1	280	10.1	2800	2533	G	24.54595	84.24828	Normal
03/9/22	14:58:17	63	0.1	260	10.1	2600	2370	G	24.54526	84.2487	Normal
03/9/22	14:58:17	63	0.1	280	20.2	2800	2533	G	24.54448	84.24906	Normal
03/9/22	14:58:17	63	0.1	280	20.2	2800	2533	G	24.54358	84.24926	Normal
03/9/22	14:58:17	63	0.1	310	10.1	3100	2778	G	24.54274	84.24929	Normal
03/9/22	14:59:0	63	0.1	330	10.1	3300	2941	G	24.5418	84.24934	Normal
03/9/22	14:59:28	63	0.1	350	10.1	3500	3104	G	24.54104	84.2496	Normal
03/9/22	15:0:3	63	0.1	260	20.2	2600	2370	G	24.54029	84.25013	Normal
03/9/22	15:0:3	63	0.1	280	10.1	2800	2533	G	24.53958	84.25057	Normal
03/9/22	15:1:0	63	0.1	330	10.1	3300	2941	G	24.53867	84.25089	Normal
03/9/22	15:1:13	63	0.1	310	20.2	3100	2778	G	24.53786	84.2512	Normal
03/9/22	15:1:49	63	0.1	300	10.1	3000	2696	G	24.53697	84.25126	Normal
03/9/22	15:2:0	63	0.1	290	10.1	2900	2615	G	24.5361	84.25116	Normal
03/9/22	15:2:24	63	0.1	220	20.2	2200	2044	G	24.53523	84.25096	Normal
03/9/22	15:3:0	63	0.1	340	10.1	3400	3023	G	24.5344	84.25138	Normal
03/9/22	15:3:35	63	0.1	280	10.1	2800	2533	G	24.53365	84.25184	Normal
03/9/22	15:4:10	63	0.1	380	10.1	3800	3349	G	24.53284	84.25224	Normal
03/9/22	15:4:45	63	0.1	260	10.1	2600	2370	G	24.53201	84.25259	Normal
03/9/22	15:5:20	63	0.1	310	10.1	3100	2778	G	24.53118	84.25291	Normal
03/9/22	15:5:56	63	0.1	350	10.1	3500	3104	G	24.53027	84.25301	Normal
03/9/22	15:6:0	63	0.1	350	10.1	3500	3104	G	24.52936	84.25315	Normal

Rishup Maharajganj road to Haneya

Shreyansh
22/09/22
S.E.

Shreyansh
22/09/22
S.E.

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

Sl. No.

3rd Quarter 08.07.2021 to 07.10.2021

1	Name of the Road	XXX	Risipal Mahabirganga to Hanaya
2	Batch No	XXX	MR-N/15-20 Awarded/25
3	Project ID	XXX	NEA 22000 176
4	Total Length of Road (in Km)	0.00	2.80 KM
5	Length of Road to Meet Required Service Level [Completed length] (in Km) [1]	0	2.80 KM
6	No. of Total Quarter (ie 3 Months as a unit) in 2 years	20	
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	0	24,95,135.00
8	Quarterly Payment 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	0	1,24,756.20
Compliance Criteria	Standard Job Description	Non- Compliance	
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]
I	PAVED ROADS (CARRIAGEWAY)		60%
II	SHOULDERS AND EMBANKMENTS		10%
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES		15%
IV	SEWAGE AND ROAD SAFETY		10%
V	VEGETATION		5%
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]			0.00 0.00
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) [6]			0.00 1,24,756.20

Inspected by E/I or his agent
Inspected by Contractor's self Control unit

Signature of person inspecting road
06/09/2022
EE

(Signature)

Signature of person inspecting road

Certify by E/I [signature] Date:-

Signature
06/09/22
EE
