

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जहानाबाद।

पत्रांक: 2098 /

जहानाबाद, दिनांक: 10/9/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

सेवा में,

नोडल पदाधिकारी, MR 3054
ग्रामीण कार्य विभाग,
बिहार, पटना।


विषय :- शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत कराये जा रहे अनुरक्षण
कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष Bihar Rural Road Maintenance Policy - 2018
अन्तर्गत पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर
समर्पित किया जाता है।

अनु० - यथोक्त।

विश्वासभाजन,


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।
10.9.22

Road Details										Agreement Details										Revenue			1st year 2nd year 3rd year 4th year 5th year					Remarks
Sl No	Road Name	Batch No.	Project ID	Date	Main Work Amount	Maintenance Amount	Main Work Amount	Agreement 1	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maintenance	Length	1st year	2nd year	3rd year	4th year	5th year	Total	1st year	2nd year	3rd year	4th year	5th year	Total	Remarks	
1	MOKEPUR TO MIRJAPUR BIKHUPUR ROAD	RN/2E/JAN/19/0006	15301036000	15/02/2021	48 628	17 331	47 851	3 33347	3 33347	3 33347	3 33347	3 33347	15 66735	1.9	0.00	0.00	0.00	0.00	0.00	1.9	2911	0.85417	0.85417	0.85417	0.85417	0.85417	2 50010	1st. 2nd. 3rd. 4th. 5th. year
2	Ghozi Nulaganj road to Raqunahapur road.	RN/2E/JAN/19/0006	10603001049	29/11/2020	50 337	17 333	49 391	3 45666	3 45666	3 45666	3 45666	3 45666	12 2832	1.9	0.00	0.00	0.00	0.00	0.00	1.9	2762	0.85417	0.85417	0.85417	0.85417	0.85417	3 45666	1st. 2nd. 3rd. 4th. 5th. year
3	Kake Main road to Domtoli Kasturba School)	RN/2E/JAN/19/0006	10603001052	2/2/2021	12 45	5 288	12 256	1 0751	1 07509	1 07509	1 07509	1 07509	5 37545	0.5	0.00	0.00	0.00	0.00	0.5	315	0.28878	0.28877	0.28877	0.28877	0.00000	0 80632	1st. 2nd. 3rd. 4th. 5th. year	
4	Katavul Barampur Road	RN/2E/JAN/19/0006	10603002274	28/11/2020	55 378	17 337	53 969	3 40525	3 40525	3 40525	3 40525	3 40525	12 07525	2	0.00	0.00	0.00	0.00	0.00	2	315	0.85131	0.85131	0.85131	0.85131	0.00000	2 53394	1st. 2nd. 3rd. 4th. 5th. year
5	Jehanabad Arwal road N.110 to Tadubdha.	RN/2E/JAN/19/0006	10603004031	30/12/2020	19 592	11.71	19 145	1.74066	1.74065	1.74065	1.74065	1.74065	8 70327	0.85	0.00	0.00	0.00	0.00	0.86	2814	0.43517	0.43516	0.43516	0.43516	0.43516	1 74065	1st. 2nd. 3rd. 4th. 5th. year	
6	Ghozi Islampur road to Betauri road	RN/2E/JAN/19/0006	12903003009	18/02/2021	28 146	10 57391	31 9285	2 14476	2 14476	2 14476	2 14476	2 14476	10 57318	1.00	0.00	0.00	0.00	0.00	1.0	3128	0.52899	0.52899	0.52899	0.52899	0.52899	2 14476	1st. 2nd. 3rd. 4th. 5th. year	
Total					186 428	69 084	182 812	13 0111	13 01112	13 01112	13 01112	13 01112	65 05863	7.16	0	0	0	0	7.16		2 25179	2 25228	2 25278	1 29933	13 17243			

10/09/22
DAD E

18/19/22
16.9.19/22

ENGINEER
RMD

Steco Analyzer

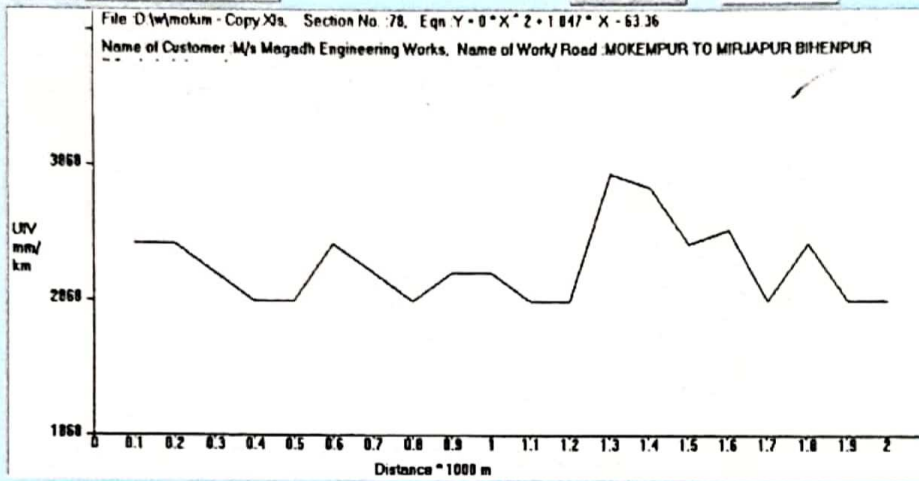
Name of Customer: M/s Maqadh Engineering Works
Name of Work/Road: TO MIRJAPUR BIHENPUR RD
Lab Job number:
Date: 8/9/2022
Section No: 78

Test Date: 8/9/2022 Road Name: MOKEMPUR TO MIRJAPUR B
Machine No: 398 Road Type: (R) RURAL ROAD
Start S No:
Start E No:
Weather:
Ultraviolet Range: 1668 To 5000 1000 mm/km
Start Location: Mokempur Dist Range: 0 To 21 01 * 1000 m
End Location: Mirapur Equation: $Y = 0 * X^2 + 1.047 * X - 63.36$

Print Generate Report and Graph

Redraw Graph

Map View



Ⓞ
09/08/22

J-E

A
9/8/22

AO

J
9/8/22

Executive Engineer
B. W. D. (W) Division
Jhansabad

Name of Customer :M/s Magadh Engineering Works

Name of Work/ Road :MOKENPUR TO MIRJAPUR BIHENPUR Road

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	Longitude	Event
9/8/22	9:52:0	78	0.1	320	20.2	3200	3287	G	25.10162	85.132037	Normal
9/8/22	9:52:19	78	0.1	320	20.2	3200	3287	G	25.10253	85.131952	Normal
9/8/22	9:53:0	78	0.1	300	20.2	3000	3077	G	25.10343	85.131835	Normal
9/8/22	9:53:29	78	0.1	280	20.2	2800	2868	G	25.1043	85.13172	Normal
9/8/22	9:54:4	78	0.1	280	20.2	2800	2868	G	25.10512	85.1317	Normal
9/8/22	9:54:4	78	0.1	320	20.2	3200	3287	G	25.10606	85.13172	Normal
9/8/22	9:54:4	78	0.1	300	20.2	3000	3077	G	25.10695	85.13173	Normal
9/8/22	9:54:40	78	0.1	280	20.2	2800	2868	G	25.10789	85.13168	Normal
9/8/22	9:55:0	78	0.1	300	20.2	3000	3077	G	25.1088	85.13175	Normal
9/8/22	9:55:15	78	0.1	300	20.2	3000	3077	G	25.10974	85.13182	Normal
9/8/22	9:56:26	78	0.1	280	20.2	2800	2868	G	25.11055	85.13185	Normal
9/8/22	10:0:0	78	0.1	280	20.2	2800	2868	G	25.10999	85.131902	Normal
9/8/22	10:0:0	78	0.1	370	10.1	3700	3810	G	25.10916	85.1318	Normal
9/8/22	10:0:31	78	0.1	360	20.2	3600	3705	G	25.10821	85.13168	Curve
9/8/22	10:0:31	78	0.1	320	20.2	3200	3287	G	25.10734	85.13173	Normal
9/8/22	10:1:7	78	0.1	330	20.2	3300	3391	G	25.10643	85.13173	Normal
9/8/22	10:1:7	78	0.1	280	20.2	2800	2868	G	25.10548	85.13173	Normal
9/8/22	10:1:42	78	0.1	320	20.2	3200	3287	G	25.10455	85.13172	Normal
9/8/22	10:2:17	78	0.1	280	20.2	2800	2868	G	25.10366	85.131868	Normal
9/8/22	10:3:0	78	0.1	280	20.2	2800	2868	G	25.10279	85.131952	Normal
3129											

09/08/22


[Signature]

[Signature]
 Executive Engineer
 R. V. D. (W) Division
 Jabalpur

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	MOKEMPUR TO MIRJAPUR BIHENPUR ROAD		
2	Batch No.	RM/JE/JAH/19/0006		
3	Project ID	16301036090		
4	Total Length of Road (in km.)	1.900		
5	Length of Road to Meet Required Service Level (Completed Length) (in km) [1]	1.900		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	1st quater		
7	Ordinary Maintenance Cost as per Shedule (Agreement Amount for Maintenance) In lakh	0.83337		
8	Quarterly Payment:1/20 of Ordinary Mainten ance Cost as per shedule (in Lakh) [2]	0.83337		
Compliance Criteria	Standard job Description	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.83337

Date of Inpection by E/I or his agent
Prepared by contractor's self control unit


 09/08/22
 Name and Designation of person inspecting road

Signature

Date
Signature of person inspecting road

1st Quarter

Government of Bihar

OM01

Rural Work Department

Road From : MOKEMPUR TO MIRJAPUR BIHENPUR ROAD

Length of Road : 1.900 Km.

Periode:- from 16.02.21 to 15.05.21

Inspector :J.E., RWD Sub Division

ORDINARY MAINTENANCE INSPECTION REPORT

Form OM01

To: ... Executive Engineer
RWD, Works Division Jehanabad

RWD, Works Division Jehanabad

Form

Date : ...

Position : ..J.E

No.	Name	Work Units	Unit of work required in each kilometre										Comments					
			1	2	3	4	5	6	7	8	9	10						
OM100	Sealed Pavement																	
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil											No. Pothole found.
OM102	Surface Depression and Rut patching	m ²	Nil	Nil	Nil	Nil	Nil											No Surface Depression and Rut patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil											No Crack Sealing found
	Surface Treatment																	
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil											No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil											No Bleeding / Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil											No Crocodile Cracking found
OM105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil											No Edge Repair Required
OM106	Digouts	m ²	N.A.	N.A.	N.A.	N.A.	N.A.											
OM107	Concrete Pavement	m ³	N.A.	N.A.	N.A.	N.A.	N.A.											
	Other activities																	
OM200	Shoulder																	
	Unsealed Shoulder																	
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil											No Edge Drop-off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil											No Roughness, Scouring or Potholes Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil											No Holding water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil											No Embankment Repair Required
	Other activities		N.A.	N.A.	N.A.	N.A.	N.A.											
OM300	Drainage including culverts major																	
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.	N.A.											Not Required
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil	Nil											Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil	Nil											Not Required
	Other activities (Whale Washing)	M ²	Nil	Nil	Nil	Nil	Nil											Not Required

Appendix

Executive Engineer, Works Division

Bidder

No.	Standard work item	Work Units	Unit of work required in each kilometre										Comments	
			1	2	3	4	5	6	7	8	9	10		
OM400 Vegetation														
Grass Control														
OM401	a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM402	Tree and Shrub Management (Cutting Trees)	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	(Cutting shrubs)	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM500	Safety Signage and Road													
OM501	Signs Maintenance	No.	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	Not Applicable
OM503	Distance Stones	No.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.	Not Applicable
OM504	Road marking	M ²	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Nil	Not Required
Other activities														

(Signature of Contractor/Authorized representative) *[Signature]* Date *9/18/19* Time *9:15 AM* Place *800*

2107 *9/18/19*

Note:- Enclose photographs with this report.
