

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जहानाबाद।**

पत्रांक: 2098 /

जहानाबाद, दिनांक: 10/9/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

सेवा में,

नोडल पदाधिकारी, MR 3054
ग्रामीण कार्य विभाग,
बिहार, पटना।


विषय :- शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनु० - यथोक्त।

विश्वासभाजन,


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।
10.9.22

Road Details				AA DETAILS				Agreement Details							Previous Maintenance Exp				Current Demand for Maintenance Amount					Remarks
Sl No.	Road Name	Batch No.	Project ID	Date	Main Work Amount	Maintenace Amount	Main Work Amount	Agreement nt 1	Agreement nt 2	Agreement nt 3	Agreement nt 4	Agreement nt 5	Total Maintenance amount	Length	1st quarter	2nd quarter	3rd quarter	4th quarter	Total					
1	MOKEMPUR TO MIRJAPUR RINENPUR ROAD	RM/DE/JAH/19/ 0006	16301036090	15/02/2021	48.628	17.333	47.851	3.33347	3.33347	3.33347	3.33347	3.33347	16.66735	1.9	0.00	0.00	0.00	0.00	0.00	2.50010	1st, 2nd, 3rd quarter			
2	Ghosi Hulasganj road to Rachunathpur road.	RM/DE/JAH/19/ 0006	10601001049	29/11/2020	50.33	17.333	49.391	3.45666	3.45666	3.45666	3.45666	3.45666	17.7833	1.9	0.00	0.00	0.00	0.00	0.00	3.45666	1st, 2nd, 3rd, 4th quarter			
3	Kako Main road to Domteil Kasturba School)	RM/DE/JAH/19/ 0006	10603001052	7/2/2021	12.45	5.388	12.256	1.07509	1.07509	1.07509	1.07509	1.07509	5.37546	0.5	0.00	0.00	0.00	0.00	0.00	0.00332	1st, 2nd, 3rd quarter			
4	Katauli Rustampur Road	RM/DE/JAH/19/ 0006	10601002274	29/11/2020	55.378	17.33	53.969	3.40525	3.40525	3.40525	3.40525	3.40525	17.07625	2	0.00	0.00	0.00	0.00	0.00	2.53384	1st, 2nd, 3rd, 4th quarter			
5	Jehansbad Arwal road N.H.110 to Yadubigha.	RM/DE/JAH/19/ 0006	10601004031	30/12/2020	19.592	11.71	19.145	1.74066	1.74065	1.74065	1.74065	1.74066	8.70327	0.86	0.00	0.00	0.00	0.00	0.00	1.71005	1st, 2nd, 3rd quarter			
6	Ghoshi Islampur road to Belaulli road	RM/DE/JAH/19/ 0006	10603003009	15/02/2021	28.1849	10.57391	31.92885	2.11476	2.11476	2.11476	2.11476	2.11476	10.5739	1.00	0.00	0.00	0.00	0.00	0.00	2.11478	1st, 2nd, 3rd, 4th quarter			
Total					186.428	69.094	182.612	13.0111	13.0112	13.0112	13.0112	13.0111	65.09563	7.16	0	0	0	0	0	13.87243	1.29932			

11/12/22
Executive Engineer
RWD Ghosi, Jehansabad

10/09/22
DAO

Stats Analyzer


Name of Customer : M/S Magadh Engineering
 Name of Work/ Road : Katali Rustampur Road
 Lab Job number :
 Date : 8/8/2022
 Section No. : 73

Test Date : 8/8/2022 Road Name : Katali Rustampur Road
 Machine No : 398 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UV Range : 1554 To 5000 1000 mm/km
 Start Location : Katali Dist Range : 0 To 2.1 0.1 * 1000 m
 End Location : Rustampur Rc Equation : $Y = 0 * X^2 + 1.047 * X - 63.36$

Print Generate Report and Graph

Redraw Graph

Map View

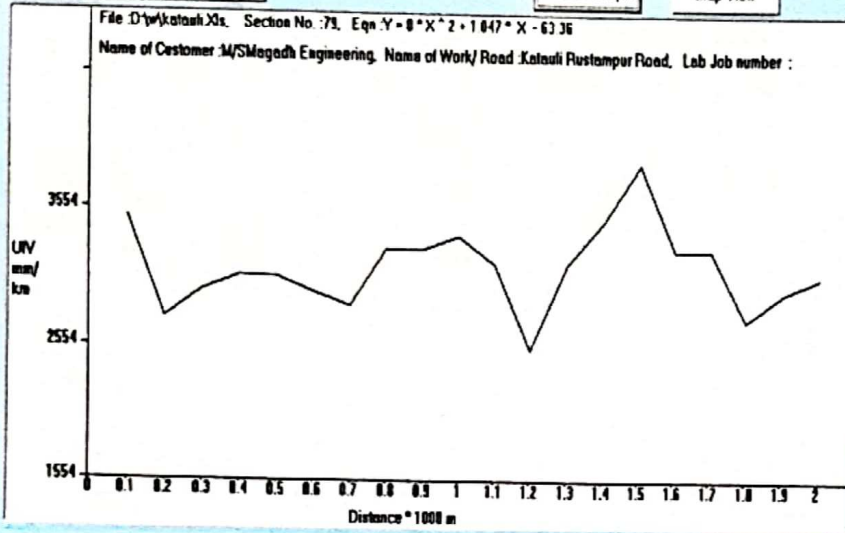

09/08/22

25

9/8/22

25

Executive Engineer
 B. W. D. (W) Division
 Jehanabad

Name of Customer :M/s Magadh Engineering Works

Name of Work/ Road :Katauli Rustampur Road

Y = 0° X + 2 + 1.047° X - 63.36

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	Longitude	Event
9/8/22	10:33:0	79	0.1	340	0	3400	3496 G		25.13488	85.157357	Normal
9/8/22	10:33:26	79	0.1	270	20.2	2700	2763 G		25.13575	85.157743	Normal
9/8/22	10:33:26	79	0.1	290	20.2	2900	2972 G		25.13662	85.157945	Normal
9/8/22	10:34:0	79	0.1	300	20.2	3000	3077 G		25.1375	85.158163	Normal
9/8/22	10:34:0	79	0.1	300	20.2	3000	3077 G		25.13841	85.15842	Normal
9/8/22	10:34:0	79	0.1	290	20.2	2900	2972 G		25.13928	85.158803	Normal
9/8/22	10:34:35	79	0.1	280	20.2	2800	2868 G		25.13999	85.15936	Normal
9/8/22	10:35:0	79	0.1	320	20.2	3200	3287 G		25.14087	85.159662	Normal
9/8/22	10:35:10	79	0.1	320	20.2	3200	3287 G		25.14178	85.15983	Normal
9/8/22	10:35:10	79	0.1	330	20.2	3300	3391 G		25.14266	85.15998	Normal
9/8/22	10:35:46	79	0.1	310	20.2	3100	3182 G		25.14356	85.16015	Normal
9/8/22	10:36:0	79	0.1	250	20.2	2500	2554 G		25.14443	85.16007	Normal
9/8/22	10:36:21	79	0.1	310	20.2	3100	3182 G		25.1453	85.15968	Normal
9/8/22	10:36:21	79	0.1	340	20.2	3400	3496 G		25.14614	85.159308	Normal
9/8/22	10:36:56	79	0.1	380	10.1	3800	3915 G		25.14703	85.158938	Normal
9/8/22	10:37:0	79	0.1	320	20.2	3200	3287 G		25.14787	85.158635	Normal
9/8/22	10:37:32	79	0.1	270	20.2	2700	2763 G		25.14964	85.157995	Normal
9/8/22	10:38:7	79	0.1	290	20.2	2900	2972 G		25.1505	85.157777	Normal
9/8/22	10:39:0	79	0.1	300	20.2	3000	3077 G		25.15096	85.158298	Normal
										3145	

09/08/22

9/8/22

9/8/22

P. V. D. (W) Division
Jalanshad

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	Katauli to Rustampur Road		
2	Batch No.	RM/JE/JAH/19/0006		
3	Project ID	10603002274		
4	Total Length of Road (in km.)	2.000		
5	Length of Road to Meet Required Service Level (Completed Length) (in km) [1]	2.000		
6	No. of Total Quarter (ie 3 Months as a unit) In 5 Years	3rd quarter		
7	Ordinary Maintenance Cost as per Shedule (Agreement Amount for Maintenance) in lakh	0.85131		
8	Quarterly Payment:1/20 of Ordinary Mainten ance Cost as per shedule (in Lakh) [2]	0.85131		
Compliance Criteria	Standard job Decription	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.85131

Date of inpection by E/1 or his agent
Prepared by contractor's self control unit

Name and Designation of persion inspecting road

Signature

Date
Signature of person inspecting road

09/08/22
35

9/8/22
AG

3rd Quarter

Government of Bihar
OM01
Rural Work DepartmentORDINARY MAINTENANCE INSPECTION REPORT
Form OM01

Form

To: ... Executive Engineer

RWD, Works Division Jehanabad

Date : ...

Road From : Katauli to Rustampur Road

Length of Road : 2.000 Km.

Period:- from 29-05-2021 to 28-08-2021

Inspector :J.E., RWD Sub Division

Position : ...J.E

No.	Standard work item	Work	Units	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed Pavement													
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut patching	m ²	Nil	Nil	Nil	Nil	Nil							No Surface Depression and Rut patching found.
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil	Nil							No Crack Sealing found
	Surface Treatment													
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil	Nil							No Bleeding / Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m ²	Nil	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m ²	N.A.	N.A.	N.A.	N.A.	N.A.							
OM107	Concrete Pavement	m ³	N.A.	N.A.	N.A.	N.A.	N.A.							
	Other activities													
OM200	Shoulder													
	Unsealed Shoulder													
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil	Nil							No Edge Drop-off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil	Nil							No Roughness, Scouring or Potholes Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil	Nil							No Holding water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other activities		N.A.	N.A.	N.A.	N.A.	N.A.							
OM300	Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.	N.A.							Not Required
OM302	Culvert Cleaning	No.	Nil	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil	Nil							Not Required
	Other activities (White Washing)	M ²	Nil	Nil	Nil	Nil	Nil							Not Required

Bidder

Appendix

Executive Engineer, Works Division

Standard work item	Work Units	Unit of work required in each kilometre										Comments
		1	2	3	4	5	6	7	8	9	10	
No. Name												
OM400 Vegetation												
Grass Control												
a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM401												
Tree and Shrub Management	No.	Nil	Nil	Nil	Nil							Not Required
(Cutting Trees)	No.	Nil	Nil	Nil	Nil							Not Required
(Cutting shrubs)	No.	Nil	Nil	Nil	Nil							Not Required
Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500 Safety Signage and Road												Not Required
OM501 Signs Maintenance	No.	Nil	Nil	Nil	Nil							Not Required
OM502 Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM503 Distance Stones	No.	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM504 Road marking	M ²	Nil	Nil	Nil	Nil							Not Required
Other activities												

31/8/12 2107

(Signature of Contractor/Authorized representative)

Date

Time

Place

31/8/12
2107

31/8/12
2107

31/8/12
2107

Note:- Enclose photographs with this report.
