

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- cerwdwd2bettiah@gmail.com

पत्रांक- 1914-386/ नरकटियागंज, दिनांक- 29/9/2022

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह— सचिव नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:-

MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर इस पत्र में संलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु०:- 1. उपयोगिता प्रमाण-पत्र From GFR 19A

2. अधियाचना पत्र।

विश्वासभाजन,

कार्यपालक अभियन्ता,

ग्रा०का०वि०, का०प्र०, नरकटियागंज।

Divya
28/09/2022

FORM GFR 19-A

(See Government of India's decision (I) below rule- 150)
Form of Utilization certificate up to the month of SEP.-2022
PIU:- E.E RWD(W)DIV-NARKATIAGANJ

SL.NO.	Name of Schemes	Sanction No.& Date with Amount (In Lacs)	Amount received (In Lacs)	Particulars
1	2	3	4	5
1	Maintenance Fund of MR(3054) New Maintenance Policy- 2018	Letter No:-27 Date:-26.08.2022	23.79597	Certified that out of Rs. 23.79597 Lacs of grants-in-aid sanctioned during the years 2022-23 in favour of Executive Engineer R. W. D. Works Division, Narkatiaganj a sum of Rs. 23.79597 Lacs has been utilized for the purpose of Maintenance Fund of MR(3054) New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL Lac remaining unutilized at the end of the period under report.
		TOTAL	23.79597	

2. Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled, are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of checks exercised:-

- Works has been supervised by Executive Engineer / Superintending Engineer.
- Periodic as inspection has been conducted by Executive Engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D. Works Division, Narkatiaganj

Requisition Form for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl. No.	Package No.	Name of Road	Project ID as per MHS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lacs)				Remarks.	
					Length (in km)	Amount of (in Lakh)					1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
	RM, JTE NAR 20/0002	JHAJHARI - GHORPAKRI	31808902051	1224 24-04-2020	3.325	104.734	104.734	31.94645	91/20-21 20.08.2020	19-08-2021	14-08-2021	1.59732	0.00000	0.00000	0.00000	

[Signature]
28/09/22
JCE

[Signature]
28/09/22
JCE

Executive Engineer
Rural Works Department
Works Division Narkatiaganj
[Signature]
28/09/2022

RWD, Works Division, Narkataganj

1st Quarter

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- JHAJHARI - GHORPAKRI

Length of Road :3.325 KM

Inspector :- A.E. RWD WORKS SUB DIVISION, MAINATAND

To:-

Executive Engineer
RWD, Works Division Narkataganj

Date:-

Position :- A.E.

No	standard OF Work Item Name	Work Unit	Unit OF Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	NIL	NIL	NIL								No pothole found
OM102	Surface Depression and Rut patching	m ³	NIL	NIL	NIL								No Surface Depression and Rut patching found
OM103	Crack Sealing	Lm	NIL	NIL	NIL								No crack found
	Surface Treatment		NIL	NIL	NIL								Not required
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	NIL	NIL	NIL								No Loss of Aggregate (Surface ravelling) found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL								No bleeding / furnishing found
	© Crocodile Cracking	m ²	NIL	NIL	NIL								No Crocodile cracking found
OM105	Edge Repair	m ²	NIL	NIL	NIL								Notified & repaired
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.								
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	NIL	NIL	NIL								No Edge Drop off found
	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL								No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	NIL	NIL	NIL								No Holding Water Found
OM202	Embankment Repair	M ³	NIL	NIL	NIL								Notified & repaired
	Other activities (Rain Cuts)		N.A.	N.A.	N.A.								
OM300	Drainage Including culverts major												
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.								NA
OM302	Culvert Cleaning	No	NIL	NIL	NIL								DONE
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL								DONE
	Other activities (Whitewashing)	M ²	NIL	NIL	NIL								Not required

Contractor

28.09.20

28.09.20

E.E

Standard Of Work Item			Work		Unit Of Required In each Kilometer										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10			
OM400	Vegetation												Done		
	Grass Control												Done		
OM401	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL								Done		
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	NIL	NIL	NIL								Done		
OM402	Tree and Shrub Management	No	NIL	NIL	NIL								Done		
	Cutting Of Branches Of Trees	No	NIL	NIL	NIL								Done		
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL								Done		
	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL								Done		
OM400	Safety Signage and Road												Not Required		
OM401	Signs Maintenance	No	NIL	NIL	NIL								Not Required		
OM402	Guard Stones	Lm	NA	NA	NA								N.A.		
OM403	Distance Stones	No	NA	NA	NA								N.A.		
OM404	Road Marking	M ²	NIL	NIL	NIL								Not Required		
	Other activities														

Arav Kumar
Contractor

Arav Kumar
J.E.
28/09/22

Arav Kumar
A.E.
28/09/22

Arav Kumar
Executive Engineer
Rural works Department
Works Division, Narkatigangaj



STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Narkatiaganj

1st Quarter

1	Name of the Road	JHAJHARI - GHORPAKRI		
2	Batch No.	RM/WE/NAR/20/0002		
3	Project ID	31808902051		
4	Total Lenth of Road (in KM)	3.325		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	3.325		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	31.94645		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.5973225		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				1.5973225

Date of inspection by E/I or his agent

Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date

(Signature)

Signature of person inspecting road

Certify by E/I [signature] Date:-

Executive Engineer

Rural Works Department

Works Division, Narkatiaganj



Name of Road - JHAJHARI - GHORPAKRI [Sec-18]

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
3/7/22	11:13:29	18	0.1	230	10.1	2300	2391	G	27.15831	84.65535	Normal
3/7/22	11:14:4	18	0.1	200	20.2	2000	2030	G	27.15904	84.65497	Normal
3/7/22	11:14:4	18	0.1	290	20.3	2900	2915	G	27.15992	84.6549	Normal
3/7/22	11:14:39	18	0.1	270	20.3	2700	2763	G	27.16078	84.65475	Normal
3/7/22	11:15:0	18	0.1	260	20.2	2600	2658	G	27.16166	84.65498	Normal
3/7/22	11:15:15	18	0.1	220	20.1	2200	2248	G	27.16273	84.65522	Normal
3/7/22	11:15:15	18	0.1	260	20.1	2600	2658	G	27.16329	84.65453	Normal
3/7/22	11:15:15	18	0.1	200	20.1	2000	2030	G	27.16286	84.65367	Normal
3/7/22	11:15:17	18	0.1	220	20.1	2200	2240	G	27.16218	84.653	Normal
3/7/22	11:15:17	18	0.1	220	20.3	2200	2240	G	27.16151	84.65242	Normal
3/7/22	11:15:18	18	0.1	250	21.3	2500	2554	G	27.16057	84.65227	Normal
3/7/22	11:15:18	18	0.1	240	21.3	2400	2449	G	27.15984	84.652	Normal
3/7/22	11:15:18	18	0.1	280	25.3	2800	2868	G	27.15941	84.65096	Normal
3/7/22	11:15:19	18	0.1	260	23.2	2600	2611	G	27.15906	84.6501	Normal
3/7/22	11:15:19	18	0.1	210	21.2	2100	2135	G	27.15828	84.64958	Normal
3/7/22	11:15:19	18	0.1	230	20.3	2300	2344	G	27.1578	84.64867	Normal
3/7/22	11:15:20	18	0.1	210	20.2	2100	2193	G	27.15724	84.64796	Normal
3/7/22	11:15:20	18	0.1	230	20.2	2300	2345	G	27.15663	84.64715	Normal
3/7/22	11:15:20	18	0.1	230	22.3	2300	2365	G	27.15602	84.64634	Normal
3/7/22	11:15:22	18	0.1	280	21.3	2800	2821	G	27.1556	84.64464	Normal
3/7/22	11:15:23	18	0.1	270	21.3	2700	2763	G	27.15577	84.64449	Normal
3/7/22	11:15:23	18	0.1	220	20.3	2200	2235	G	27.15651	84.64402	Normal
3/7/22	11:15:24	18	0.1	220	20.2	2200	2235	G	27.1567	84.64305	Normal
3/7/22	11:15:24	18	0.1	270	20.2	2700	2715	G	27.15587	84.64274	Normal

Name of Road - JHAJHARI - GHORPAKRI [Sec-18]

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
3/7/22	11:15:24	18	0.1	240	20.2	2400	2435	G	27.15495	84.64246	Normal
3/7/22	11:15:25	18	0.1	240	20.2	2400	2402	G	27.15417	84.6421	Normal
3/7/22	11:15:25	18	0.1	260	20.2	2600	2611	G	27.1533	84.6418	Normal
3/7/22	11:15:27	18	0.1	230	21.5	2300	2311	G	27.15244	84.64152	Normal
3/7/22	11:15:27	18	0.1	260	23.4	2600	2643	G	27.15158	84.64124	Normal
3/7/22	11:15:27	18	0.1	300	23.1	3000	3031	G	27.15113	84.6399	Normal
3/7/22	11:15:28	18	0.1	270	23.1	2700	2746	G	27.15055	84.63919	Normal
3/7/22	11:15:28	18	0.1	280	20.2	2800	2896	G	27.15038	84.6383	Normal
3/7/22	11:15:29	18	0.025	240	20.2	2400	2460	G	27.15004	84.63758	Normal
Average IRI Value							2491				

Munir
28/9/22


[Signature]
Executive Engineer
Rural Works Department
Works Division, Narkatiyaganj

Name of Customer : Ms Nazari Nirman
Name of Work/ Road : JHAJHARI - GHORPAKRI
Lab Job number :
Date : 03 Jul '22
Section No. : 18

Test Date : 03-Jul-'22
Machine No : 402
Start S No :
Start E No :
Weather :
Start Location :
End Location :
Road Name : JHAJHARI - GHORPAKRI
Road Type : (R) RURAL ROAD
Side :
Interval :
UVI Range : 1030 To 4000 mm/km
Dist Range : 0 To 35 0.1 1000 m
Equation : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Print Generate Report and Graph

Redraw Graph Map View

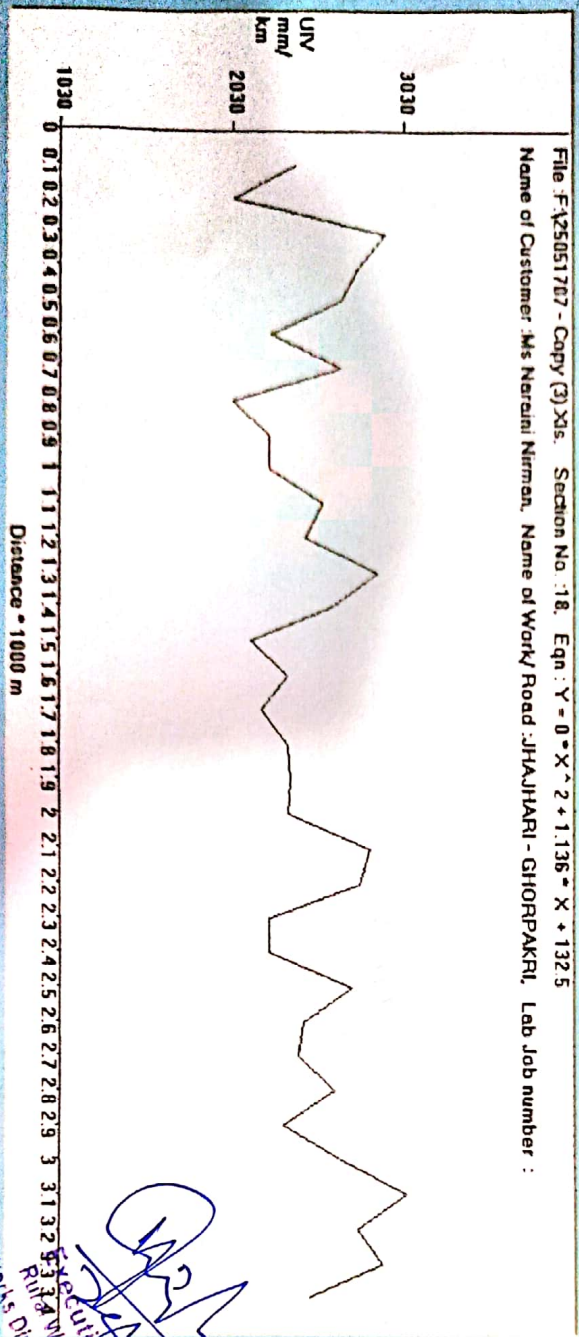

[Signature]
Executive Engineer
Public Works Department
Works Division, N. Malindi, Gail

Handwritten signature and date
28/9/22
