

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक...481(305)...../ बिहारशरीफ, दिनांक...18-4-23.

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये
अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि नई अनुरक्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०-यथोक्त।

विश्वासभाजन


18/4/23


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
18/04/23

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

1 Year (2nd Quarter)

RWD, Works Division Bihar Sharif

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Badhiya Kajichak More To SH-78
(Package No.RM/NA/BIH/20/0003)
Length of Road :- 1.50 Km
Inspector :- J.E RWD Sub Division : Samnera

To:-

Executive Engineer
RWD, Works Division Hathua

Date:-

Position :- J.E

No	standard Of Work Item	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Raveling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												Not Required
	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
OM402	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

30/11/21
J.E

30/11/21
J.E

18/04/23
18/04/23

Executive Engineer
Rural Work Department
Work Division Bihar Sharif
18/04/23

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-			
2	Batch No.-	Badhiya Kajichak More To SH-78		
3	Project ID -	RM/NA/BIII/20/0003		
4	Total Length of Road (in Km)	1261034951		
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	1.5		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	1.5		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	20		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	20.54026		
		1.02701		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.00000
				1.02701

Date of inspection by E/I or his agent

Date

Name and Designation of person inspecting road


Signature of person inspecting road

Certify by E/I (signature) Date

[Signature]
30/11/21
S.E

[Signature]
30/11/21
R

File : E:\Bump Machine\Bump Reading\Maa Tara Construction\01051720.Xls, Section No. :80, Eqn : $Y = 0.0000X^2 + 0.0000X + 0.0000$
 Name of Customer : Maa Tara Construction, Name of Work/ Road : Badhiya Kajichak More To SH-78, Lab Job

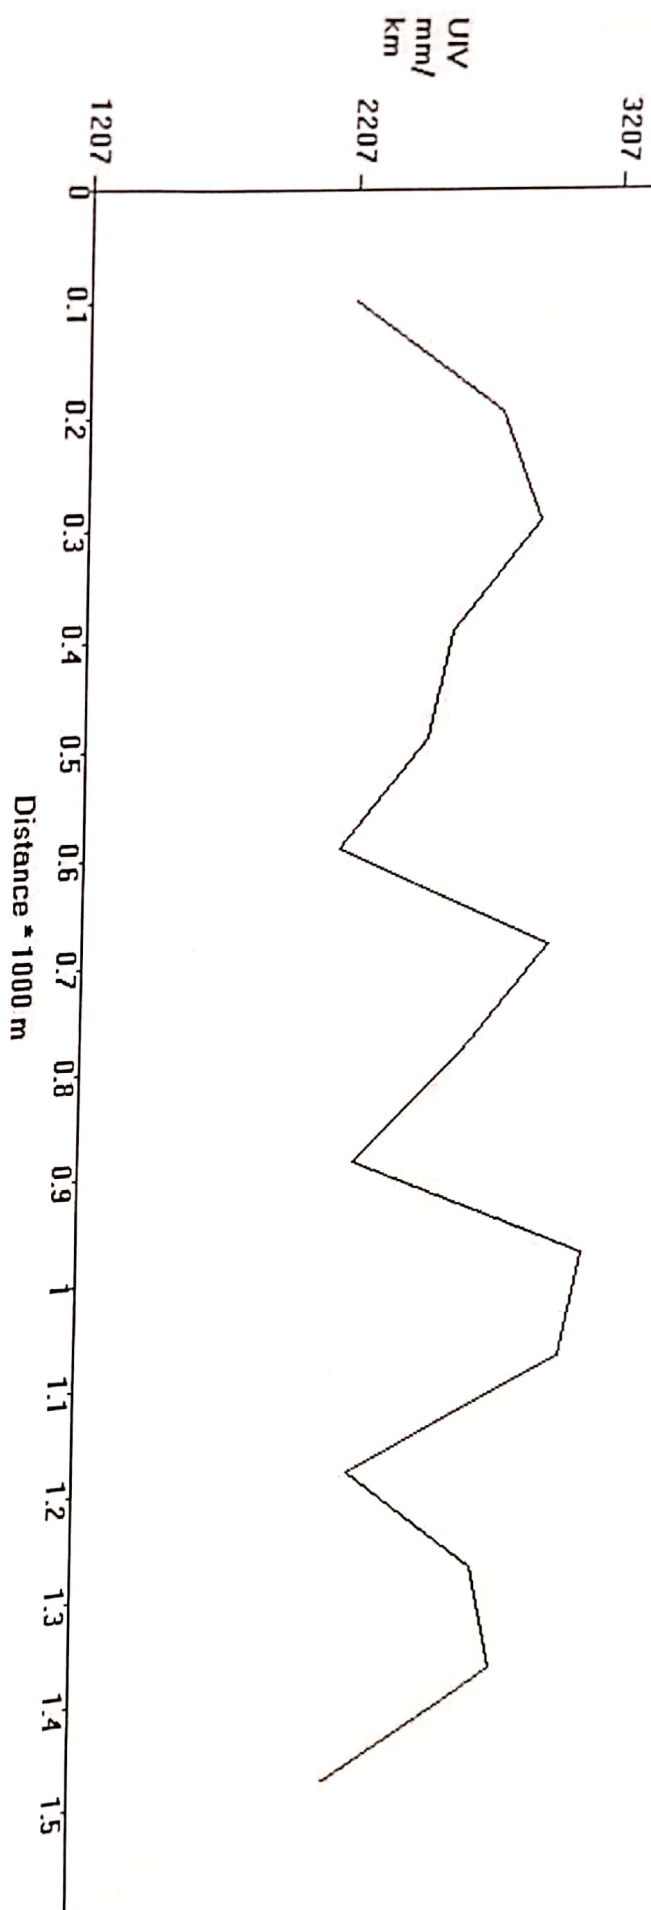

Handwritten signature
 30/11/21
 J.E

Handwritten signature
 30/11/22
 ME

Scheme-NEW MR
Road Name-Badhiya Kajlichak more se SH-78
Contractor-Maa Tara Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$y = 0 \cdot x^2 + 0.816 \cdot x + 249$			(R) RURAL ROAD		
1/5/22	8:56:31	80	0.1	240	0	2400	2207	G	25.26808	85.779965	Normal				Good	Average	Poor
1/5/22	8:57:0	80	0.1	310	20.2	3100	2778	G	25.267657	85.780958	Speed Breaker				<4000	4001-5000	>5001
1/5/22	8:57:6	80	0.1	330	20.2	3300	2941	G	25.267318	85.781852	Normal						
1/5/22	8:57:6	80	0.1	290	10.1	2900	2615	G	25.266953	85.78281	Speed Breaker						
1/5/22	8:57:41	80	0.1	280	20.2	2800	2533	G	25.266578	85.78372	Normal						
1/5/22	8:58:0	80	0.1	240	20.2	2400	2207	G	25.266188	85.784645	Normal						
1/5/22	8:58:16	80	0.1	340	30.3	3400	3023	G	25.265745	85.785555	Normal						
1/5/22	8:58:16	80	0.1	300	10.1	3000	2696	G	25.265335	85.786463	Normal						
1/5/22	8:58:52	80	0.1	250	20.2	2500	2288	G	25.264905	85.787272	Normal						
1/5/22	8:59:0	80	0.1	360	30.3	3600	3186	G	25.26448	85.78813	Normal						
1/5/22	8:59:0	80	0.1	350	30.3	3500	3104	G	25.264018	85.789107	Normal						
1/5/22	8:59:26	80	0.1	250	20.2	2500	2288	G	25.263575	85.79	Normal						
1/5/22	8:59:26	80	0.1	310	30.3	3100	2778	G	25.263138	85.790908	Normal						
1/5/22	8:59:26	80	0.1	320	20.2	3200	2860	G	25.26267	85.79178	Normal						
1/5/22	9:00:0	80	0.1	350	30.3	3500	3104	G	25.262172	85.792575	Normal						
						Total-	40608										
						IRI Value	2707										

Handwritten signature and date 11/1/21

Handwritten signature and date 11/1/21
