

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 18163195 / बिहारशरीफ, दिनांक 18-4-23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- नई अनुस्क्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये
अनुस्क्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।


महोदय,

उपर्युक्त विषयक के संबंध में कहना है कि नई अनुस्क्षण नीति-2018 (MR-3054) योजनान्तर्गत पथ में कराये गये अनुस्क्षण कार्य के लिए संवेदक को भुगतान करने हेतु अभियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०-यथोक्त।

विश्वासभाजन


18/4/23


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
18/04/23

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Bihar Sharif

1 Year (2nd Quarter)

Government Of Bihar

OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- NH-82 Husaina Road to Bari Missian Village
(Package No.RM/NA/BIH/19/0002)
Length of Road :- 0.74 Km
Inspector :- J.E RWD Sub Division : Sarmera

To:-

Executive Engineer
RWD, Works Division Hathua

Date:-

Position :- J.E

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												Comments
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	Nil	Nil	Nil	Nil							
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							No Holding Water Found
	Other activities (Rain Cuts)												Not Required
OM300	Drainage including culverts major												Not Required
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whilw washing)	M ²	Nil	Nil	Nil	Nil							Not Required

No	Standard Of Work Item	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road		Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

30.11.21
E

30.11.21
N

18/4/23

Executive Engineer
Rural Work Department
Work Division Bihar Sharif
18/4/23

18/4/23

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-	NH-82 Husaina Road to Bari Missian Village		
2	Batch No.-	RM/NA/BIH/19/0002		
3	Project ID -	10200701012		
4	Total Length of Road (in Km)	0.74		
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	0.74		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	5.61919		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.28096		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.28096

Date of inspection by E/I or his agent

Date

Name and Designation of person inspecting road


Signature of person inspecting road

Certify by E/I (signature) Date

[Signature]
30.11.21
C-E

[Signature]
30/11/21
R

File : E:\Bump Machine\Bump Reading\Maa Tara Construction\01051720.Xls, Section No. : 82, Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Maa Tara Construction, Name of Work/ Road : NH-82 Husaina Road to Bari Missian Village.

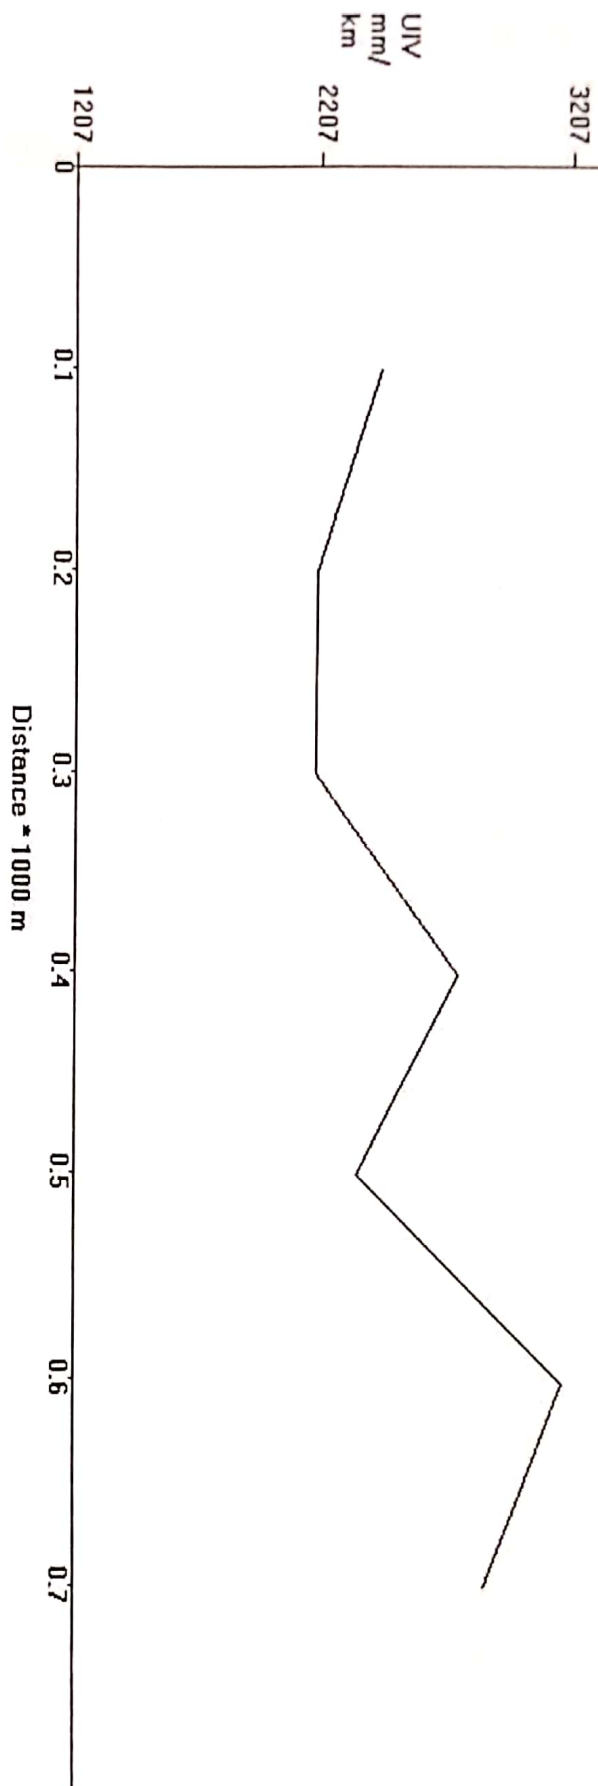

08/11/22
 J.C

08/11/22
 W

Scheme-NEW MR

Road Name-14H-82 Husena road se barimisiya

Contractor-Maa Tara Construction

Contractor-Maa Tara Construction																
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event					
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD								
1/5/22	9:52:26	82	0.1	270	0	2700	2452	G	25.274098	85.81483	Normal	$Y = 0 \cdot X^2 + 0.816 \cdot X + 249$				
1/5/22	9:52:26	82	0.1	240	10.1	2400	2207	G	25.274927	85.814982	Normal	$X = 3100$				
1/5/22	9:52:26	82	0.1	240	10.1	2400	2207	G	25.275892	85.81505	Normal	$Y = 2778$				
1/5/22	9:53:1	82	0.1	310	10.1	3100	2778	G	25.276775	85.81507	Normal	(R) RURAL ROAD				
1/5/22	9:53:36	82	0.1	260	10.1	2600	2370	G	25.277623	85.814965	Normal	Good	Average		Poor	
1/5/22	9:54:11	82	0.1	360	10.1	3600	3186	G	25.277585	85.815202	Normal	<4000	4001-5000		>5001	
1/5/22	9:54:47	82	0.1	320	10.1	3200	2860	G	25.276705	85.81508	Normal					
						Total-	18060									
						IRI Value	2580									

1/5/22
9:54:47
J.C

1/5/22
9:54:47
J.C
