

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

पत्रांक :- 536 (अ.प्र.)

पटना/दिनांक :- 12/3/23

श्रेष्ठ,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना ।

सेवा में,

नोजल पदाधिकारी-3054,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-3054 (एम.आर.) बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 योजना अन्तर्गत अनुस्क्षण भद् में आवंटन का अधिसावना के संबंध में ।

महोदय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-3054 (एम.आर.) बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 योजना अन्तर्गत अनुस्क्षण भद् में निम्नांकित पथों का आवंटन का अधिसावना का भाग (Yearly Quarter wise) तैयार कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है, जो निम्न प्रकार है :-

Sl. No.	Name of Road	Yearly Quarter wise	Amount (in Lakh)
1.	PIPERA MORE PMGSY ROAD-CHATNA VIA CHATNA MAHADALIT TOI.A (Package No.- RM/PA/PAT/19/0012)	1 st Year-1 st Quarter	0.51196

अतः अनुरोध है कि उक्त योजना अन्तर्गत अनुस्क्षण भद् में आवंटन उपलब्ध कराने की कृपा की जाय, ताकि संवेदक का भुगतान किया जा सके ।

अनु०:- यथोक्त ।

विश्वासभाजन

 12/3/23

कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road -	PIPRA MORE PMGSY ROAD - CHATNA VIA CHATNA MAHADALIT TOLA		
2	Batch No. -	RM/PA/PAT/19/0012		
3	Project ID -	1261036164		
4	Total Length of Road (in Km)	1.01		
5	Length of Road to Meet Required Service Level [Completed length] (in Km)	1.01		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	10.23913		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.51196		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANKMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND SIGNAGE AND ROAD SAFETY	0	15%	0.00000
IV		0	10%	0.00000
V	VEGETATION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.51196

Date of inspection by E/I or his agent

Date

Signature of person inspecting road

Name and Designation of person inspecting road

Certify by E/I (signature) Date

Sanjay
4/5/23
dr

Subayy
04/05/23

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Patna

1 Year (1st Quarter)

Government Of Bihar

OM101

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Pipra More PMGSY Road Chhatra Via Chhatra Mahadalit Toia
(Package No.-MR-N/2019-2020/PATNA/12)
Length of Road :- 1.010 Km
Inspector :- J.E RWD Sub Division : Sampat Chak

To:-

Executive Engineer
RWD, Works Division Patna

Date:-

Position :- J.E

No	standard Of Work Item Name	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment	m ²											No Pot Hole Found.
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patching Found
OM102	Surface Depression and Rut patching	m ³	Nil	Nil	Nil	Nil							No Crack sealing Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	Surface Treatment												No Bleeding/ Flushing Required
OM104	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
	© Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
105	Edge Repair	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m ²	N.A	N.A	N.A	N.A							N/A
107	Concrete pavement	m ³	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												No Edge Drop-Off Required
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							Not Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							Not Required
OM202	Embankment Repair	m ³	Nil	Nil	Nil	Nil							N/A
	Other activities (Rain Cuts)												
OM300	Drainage including culverts major												N/A
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Whitewashing)	M ²	Nil	Nil	Nil	Nil							

done by 14/12/20

15/12/20

15/12/20

No	Standard Of Work Item	Work	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation													
	Grass Control													
	(a) Roadside- General Tidy													
OM401	(b) Clear near Safety signs, kilometer posts and roadside furniture													
OM402	Tree and Shrub Management													
	Cutting Of Branches Of Trees													
	Cutting Of Shrubs From Road Way													
	Other activities (Trimming of Grass)													
OM500	Safety Signage and Road													
OM501	Signs Maintenance													
OM502	Guard Stones													
OM503	Distance Stones													
OM504	Road Marking													
	Other activities													

4/12/23

5/12/23

Executive Engineer
Rural Work Department
Work Division Patna

15/03/23



Name of The Road : Pipra More PMGSY Road Chhatna Via Chhatna Mahadalit Tola
Division : Patna

Block : Sampachak

Contractor Name : SHRAWAN TECHBUILD PRIVATE LIMITED

Length : 1.01 Km

Package No. : MR-N/2019-2020/PATNA/12

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.936 * X + 278.4$		
10/02/2023	11: 23: 45	89	0.1	340	0	3400	3460	G	25.538118	85.126598	Normal	X = 2600		
10/02/2023	11: 24: 0	89	0.1	380	30.3	3500	3554	G	25.537137	85.126565	Normal	Y = 2712		
10/02/2023	11:24:20	89	0.1	350	20.2	3500	3554	G	25.5356	85.126665	Speed Breaker			
10/02/2023	11: 24: 40	89	0.1	360	30.3	3600	3648	G	25.535523	85.12616	Normal	(R)RURAL ROAD		
10/02/2023	11: 24: 58	89	0.1	350	20.2	3500	3554	G	25.534635	85.125875	Speed Breaker	Good	Average	Poor
10/02/2023	11: 25: 15	89	0.1	250	20.2	2500	2618	G	25.53379	85.126027	Curve	<4000	4001-5000	>5001
10/02/2023	11: 25: 32	89	0.1	350	20.2	3500	3554	G	25.533405	85.126952	Curve			
10/02/2023	11: 25: 55	89	0.1	270	30.3	2700	2805	G	25.53264	85.126615	Normal			
10/02/2023	11: 26: 10	89	0.1	340	30.3	3400	3460	G	25.531978	85.126328	Normal			
10/02/2023	11: 26: 30	89	0.1	250	30.3	2500	2618	G	25.532622	85.125942	Normal			
10/02/2023	11: 26: 50	89	0.01	260	30.3	2600	2712	G	25.53272	85.125622	Normal			
Total			1.01	3500	262.6	34700	35537		280.878168	85.127466				
Average							3181.818	3256.181						

Shrawan
4/5/23

Shrawan
04/08/23

Shrawan
15/09/23



Name of Customer :	TECHBUILD PRIVATE LIMITED
Name of Work/	Pipra More PMGSY Road Chit
Road :	
Lab Job number	
Date :	10/02/2023
Section No.	89


Test Date :	10/02/2023
Road Name :	Pipra More PMGSY Road Chit
Machine No :	374
Road Type :	(R) RURAL ROAD
Start S No :	
Start E No :	
Side :	
Interval :	
Weather :	
UV Range :	1618 To 5000 mm/km
Start Location :	
Dist Range :	0 To 1.2 0.1 - 1000 m
Equation :	$Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BRRDA23\OneDrive\Desktop\Steco.Xls, Section No. :89, Eqn : $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$
Name of Customer : SHARWAN TECHBUILD PRIVATE LIMITED, Name of Work/ Road : Pipra More PMGSY Road

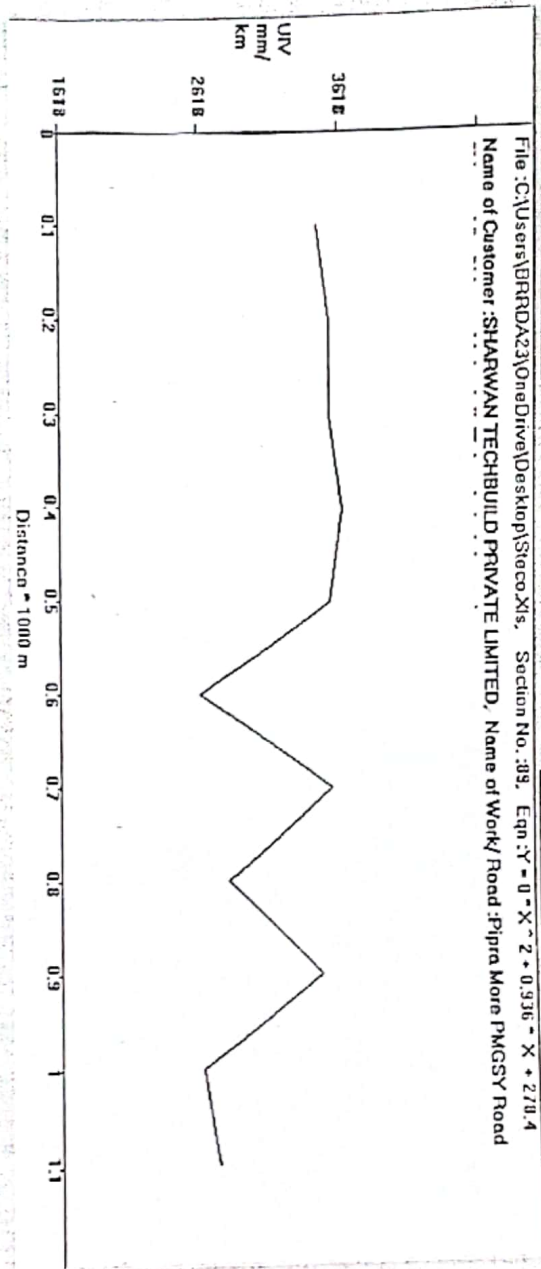

Good Road
10/3/23

Impd
04/02/23

15/01/23
