


Name of Customer :
Name of Work/ Road :
Lab Job number
Date :
Section No.

Test Date : **Road Name :**
Machine No : **Road Type :**
Start S No : **Side :**
Start E No : **Interval**
Weather : **UIV Range :** **To** **mm/km**
Start Location : **Dist Range :** **To** *** 1000 m**
End Location : **Equation :**

Print **Generate Report and Graph**

Redraw Graph

Map View

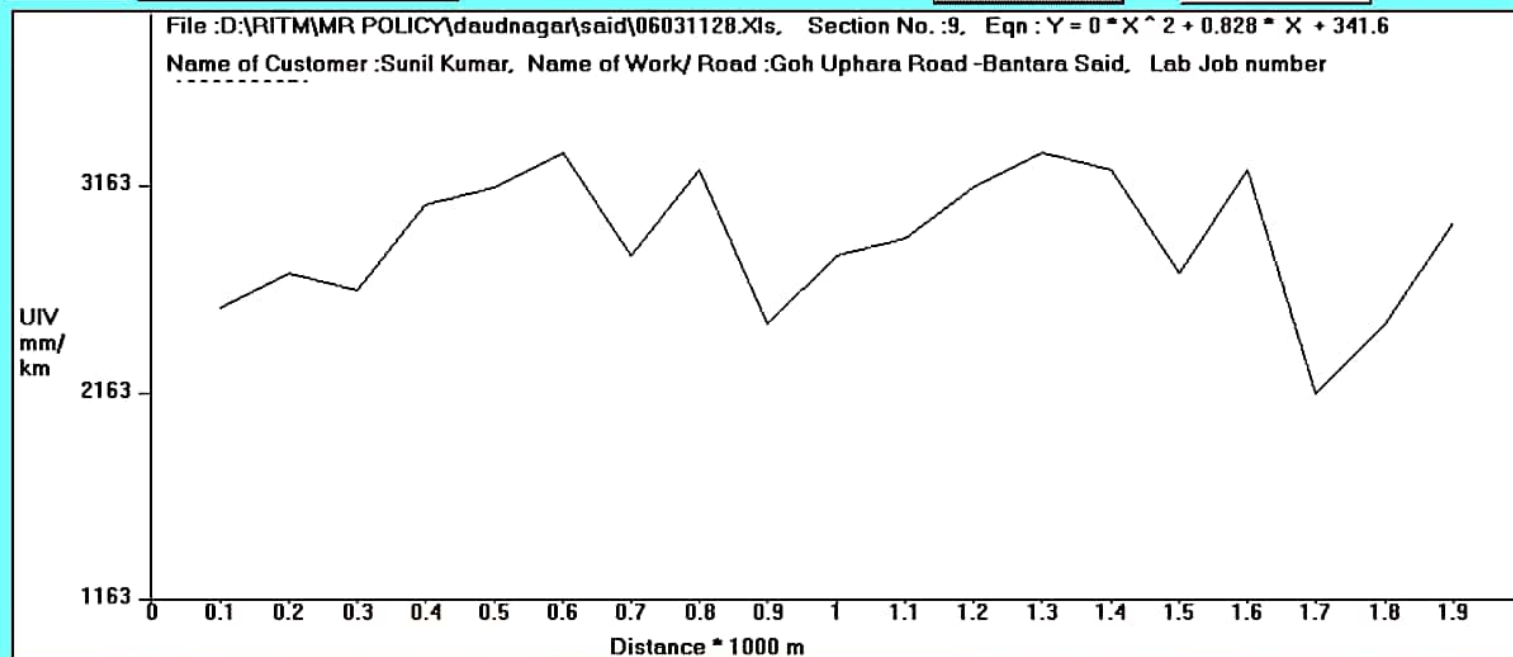

Name of Road -Goh Uphara Road -Bantara Said

Name of Contractor- Sunil Kumar

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
28/12/22	7:28:3	9	0.1	270	0	2700	2577	G	25.7986	84.663687	Normal
28/12/22	7:28:38	9	0.1	290	10.1	2900	2742	G	25.7893	84.663552	Normal
28/12/22	7:29:13	9	0.1	280	10.1	2800	2659	G	25.78077	84.663	Normal
28/12/22	7:29:48	9	0.1	330	10.1	3300	3073	G	25.77495	84.662845	Normal
28/12/22	7:30:0	9	0.1	340	10.1	3400	3156	G	25.77668	84.661885	Normal
28/12/22	7:30:23	9	0.1	360	20.2	3600	3322	G	25.7678	84.661598	Normal
28/12/22	7:30:23	9	0.1	300	20.2	3000	2825	G	25.7591	84.661363	Normal
28/12/22	7:31:0	9	0.1	350	10.1	3500	3239	G	25.75378	84.660942	Normal
28/12/22	7:31:34	9	0.1	260	10.1	2600	2494	G	25.75697	84.659965	Normal
28/12/22	7:32:9	9	0.1	300	10.1	3000	2825	G	25.76425	84.659982	Normal
28/12/22	7:33:0	9	0.1	310	20.2	3100	2908	G	25.77102	84.659882	Normal
28/12/22	7:36:0	9	0.1	340	20.2	3400	3156	G	25.77105	84.659898	Normal
28/12/22	7:36:51	9	0.1	360	10.1	3600	3322	G	25.7639	84.659965	Normal
28/12/22	7:37:0	9	0.1	350	10.1	3500	3239	G	25.75695	84.659998	Normal
28/12/22	7:37:27	9	0.1	290	10.1	2900	2742	G	25.75403	84.660942	Normal
28/12/22	7:38:2	9	0.1	350	10.1	3500	3239	G	25.75925	84.661363	Normal
28/12/22	7:38:2	9	0.1	220	10.1	2200	2163	G	25.76745	84.661565	Normal
28/12/22	7:38:37	9	0.1	260	10.1	2600	2494	G	25.77663	84.661868	Normal
28/12/22	7:39:12	9	0.1	320	20.2	3200	2991	G	25.77532	84.662793	Normal
Length			1.9		Total IRI		2903				

$$Y = 0 * X^2 + 0.828 * X + 341.6$$

$$X = 3094$$

$$Y = 2903$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

Poores
 02/10/2023

Sunil
 02/10/23
 A.E

E'E

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दाउदनगर ।

पत्रांक: 229/313

दाउदनगर, दिनांक: 20.01.2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दाउदनगर।

सेवा में,

नोडल पदाधिकारी, MR 3054
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- शीर्ष Bihar Rural Road Maintenance Policy - 2018 अन्तर्गत कराये जा रहे अनुरक्षण
कार्य के भुगतान हेतु राशि अधियाचना के संबंध में।

महाराज,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष Bihar Rural Road Maintenance Policy - 2018
अन्तर्गत पथ में कराये जा रहे अनुरक्षण कार्य के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में संलग्न कर
समर्पित किया जाता है।

अनु० - यथोक्त।

विश्वासभाजन,

20.01.23
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दाउदनगर।
20.01.23

Maintenance Requisition Formate for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
 ie of works Division- Daudnagar

Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)																								
Road Details					A & A Details			Agreement Details							Previous Maintenance Exp		Current Demand for Maintenance Amount							
Sl No	Road Name	Batch No	Project ID	Actual Date of Completion	Maint work amount	Maintenance amount	Main Work Amount	Agreement 1	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maintenance amount	Length	1st quarter	Total Maintenance EXP	Length as per Report in Year	1st quarter	2nd quarter	3rd quarter	4th quarter	Total	Remarks	
1	Deshkara Goh Road Savna	RMA/UDA U/190013	10602802049	09-01-2021	28.299	10.635	25.228	0.69948	1.04466	3.00564	1.36991	3.43067	9.55026	1.25	0.0	0.0	28.12.22	28.25	0.47792	0.47792	0.47792		1.43376	
2	Goh Gaya Road - Daulpur	RMA/UDA U/190013	10602802042	09-01-2021	40.444	15.84	36.197	1.08478	1.56718	4.4954	2.02115	5.08356	14.25207	1.87	0.0	0.0	28.12.22	29.42	0.71260	0.71260	0.71260		2.13780	
3	Goh Hamid Nagar Road - Ankeni	RMA/UDA U/190013	10602802044	29-08-2021	37.054	12.955	33.067	0.80647	1.26265	3.71232	1.64067	4.19605	11.81816	1.57	0.0	0.0	28.12.22	30.94	0.58091	0.58091	0.58091		1.74273	
4	Goh Rafiqganj Road - Rakunda	RMA/UDA U/190013	10602802045	09-01-2021	14.128	5.563	12.6	0.34534	0.53201	1.6087	0.68967	1.8034	4.97832	0.69	0.0	0.0	28.12.22	33.22	0.24891	0.24891	0.24891		0.74673	
5	Goh Uphaara Road - Santara Said	RMA/UDA U/190013	10602802051	29-08-2021	43.495	18.498	38.911	1.02835	2.16293	5.18998	2.49923	5.78594	16.636	1.994	0.0	0.0	28.12.22	29.03	0.8308				0.8308	
Total																								

Handwritten: 20.1.2023
 Divisional Accounts Officer
 Rural Works Department,
 works Division,

Handwritten: 20.1.23
 Executive Officer
 Rural Works Department,
 Works Division, Daudnagar

3rd Quarter

Government of Bihar OM01 Rural Work Department		ORDINARY MAINTENANCE INSPECTION REPORT Form OM01										Form	
Road From: <u>Chahypham to SP Bahrn</u>		To: ... Executive Engineer RWD, Works Division Daudnagar										Date: ... <u>28/11/22</u>	
Length of Road: ... <u>1.95 km</u>		Position: J E											
Period: from <u>29.08.20</u> to <u>29.11.20</u>		Inspector: J E, RWD Sub Division <u>Uday</u>											
No.	Standard work item Name	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed Pavement												No Pothole found
OM101	Pothole Patching	m ²	Nil	Nil	Nil	Nil							No Surface Depression and Rut patching found
OM102	Surface Depression and Rut patching	m ²	Nil	Nil	Nil	Nil							No Crack Sealing found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							
OM104	Surface Treatment												No Loss of Aggregate (Surface Raveling) found
	(a) Loss of Aggregate (Surface Raveling)	m ²	Nil	Nil	Nil	Nil							No Bleeding / Flushing Required
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil	Nil							No Crocodile Cracking found
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil	Nil							No Edge Repair Required
OM105	Edge Repair	m ²	Nil	Nil	Nil	Nil							
OM106	Digouts	m ²	N.A.	N.A.	N.A.	N.A.							
OM107	Concrete Pavement	m ³	N.A.	N.A.	N.A.	N.A.							
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												No Edge Drop-off Required
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time
	(b) Roughness, Scouring or Potholes /	Lm / m ²	2%	Nil	Nil	2%							No Holding water Found
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Embankment Repair Required
OM202	Embankment Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (Raincut)		Nil	Nil	Nil	Nil							
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A.	N.A.	N.A.	N.A.							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M ³	Nil	Nil	Nil	Nil							Not Required
	Other activities (White Washing)	M ²	100%	100%	100%	100%							white washing within stipulated time.

Bidder

Appendix

Executive Engineer, Works Division

No.	Standard work item Name	Work Units	Unit of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
OM401	Grass Control												
	a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	(Cutting Trees)	No	100%	100%	100%	Nil							Cutting of Trees & shrub within time period
	(Cutting shrubs)	No	100%	100%	100%	Nil							Trimming of Grass within time period
	Other activities (Trimming of Grass)	M ²	100%	100%	100%	100%							
OM500	Safety Signage and Road												
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM503	Distance Stones	No	N.A.	N.A.	N.A.	N.A.							Not Applicable
OM504	Road marking	M ²	Nil	Nil	Nil	Nil							Not Required
	Other activities												

(Signature of Contractor/Authorized representative)

Date

Time

Place

Anil Kumar
28/12/22

Praveen
02/01/2023

Uday

Note:- Enclose photographs with this report.

T.C.

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of Road	Goh Uphara Road - Bantara Said		
2	Batch No.	RM/AU/DAU/19/0013		
3	Project ID	10602802051		
4	Total Length of Road (in km.)	1.994		
5	Length of Road to Meet Required Service Level {Completed Length} (in km) [1]	1.994		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 Years	1st		
7	Ordinary Maintenance Cost as per Shedule {Agreement Amount for Maintenance} in lakh	16.616		
8	Quarterly Payment: 1/20 of Ordinary Maintenance Cost as per shedule (in Lakh) [2]	0.83080		
Compliance Criteria	Standard job Description	Non Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (CARRIAGEWAY)	0%	60%	0.00
II	SHOULDERS AND EMANMENTS	0%	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0%	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0%	10%	0.00
V	VEGATAION	0%	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00
TO BE PAIF FOR THE QUARTER / DEMAND (in Lakh) [6]				0.8308 0.83080

Date of inspection by E/I or his agent
Prepared by contractor's self control unit

Name and Designation of person inspecting road

Pamoo
02/01/2023

Vinay
02/01/23
Signature AE

Date
Signature of person inspecting road
