

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, मोहनियाँ।

Email ID:- ee.rwdworkmohania@gmail.com

Mob:- 8986915825

पत्रांक.....20.....

मोहनियाँ / दिनांक.....07/01/2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मोहनियाँ।

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार


विषय :- नई अनुरक्षण नीति-2018MR (3054)योजना के अंतर्गत पथ में कराये गये
त्रैमासिक अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054)योजना के अंतर्गत पथ में कराये गये त्रैमासिक अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मोहनिया।

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to 16 July 2022

Sl.No	Name of Scheme	Sanction No.&Date With Amount (In lace Rs.)	Amount Received (In lace Rs.)	Particulars
1	Maintenance of Rural roads Under MR (New Maintenance Policy-2018 MR (3054) BRRDA PATNA)	New Maintenance Policy-2018 MR (3054) BRRDA PATNA	205.01908	Certified that out of Rs.205.01908 lakh of grants-in-aid sanctioned during the years 2022-23 In favor of EE,RWD works division Mohania a sum of Rs. 155.41143 lakh has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs.49.60765 lakh remaining unutilized at the end of the period under report.
	Total:		205.01908	

2. Certified that I have satisfied my self that the cosnditions on which the grant-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was utilized for the purpose for which it was sanctioned.-

Kind of Checks exercised:-

- i. Works have been supervised by Executive Engineer/ Superintending Engineer.
- ii. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- iii. Construction materials have been tested.
- iv. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- v. All other caudal formalities have been observed.

3. Physical Progress achieved:-

- i. Construction of Road Works.
- ii. Construction of CD works.


07/01/2023
Divisional Accounts Officer
R.W.D, works Division
Mohania.


Executive Engineer
R.W.D, works Division
Mohania.

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Mohania

Quarter:- 1 Period:- 12-06-2021
10-09-2021

1	Name of the Road	Lahurbari Kariram Canal Road - Seni Sarai				
2	Batch No./Package No.	RM/KA/MOH/20/0006				
3	Project ID	NEA220002315				
4	Total Length of Road (in KM)	1.230				
5	Length of Road to Meet Required Service Level [Completed length](in Km)	1.230				
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20				
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	8.91973				
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh)	0.44599				
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]		
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%) [4]			
		I	PAVED ROADS (CARRIAGEWAY)	-	60%	0.00000
		II	SHOULDERS AND EMBANKMENTS	-	10%	0.00000
		III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	-	15%	0.00000
		IV	SIGNAGE AND ROAD SAFETY	-	10%	0.00000
V	VEGATION	-	5%	0.00000		
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]						0.00000
TOTAL TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]						0.44599

Date of inspection by E/I or his agent

Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

(Signature)
(Signature)

Date

Certify by E/I [signature] Date:-

Signature of person inspecting road

(Signature)
5/12/2021

(Signature)
Executive Engineer
Rural Works Department
Works Division, Mohania

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division:- Mohania

Quarter:- 1

Government Of Bihar OM01

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:-Lahurbari Kariram Canal Road - Seni Sarai
(Package No.-RM/KA/MOH/20/0006)
length of Road:-1.230 KM

To,

Executive Engineer
RWD (w) Div. Mohania

Date:-02.12.2022

Inspector :- **JE RWD Sub Division Ramgarh**

Position :-J.E.

No	standard Of Work Item	Work Unit	Unit OF Required in each Kilometere												Comments
	Name		1	2	3	4	5	6	7	8	9	10	11	12	
OM100	Sealed payment														
OM101	Pothole Patching	m ²	Nil	Nil											No Pot Hole found.
OM102	Surface Depression and Rut patching	m ³	Nil	Nil											Not Surface Depression & Rut Patching found.
OM103	Crack Sealing	Lm	Nil	Nil											No Crack Sealling found
OM104	Surface Treatment														
	(a) Loss of Agreegate (SurfacebRavelling)	m ²	Nil	Nil											No Loss of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil											No Loss of Aggregates (Surface Ravelling) Found
	© Crocodile Cracking	m ²	Nil	Nil											No Bleeding / Flushing found.
105	Edge Repair	m ²	Nil	Nil											No Crocodile Cracking Found
106	Digouts	m ²	NA	NA											No Edge Repair Required
107	Concreate pavement	m ³	NA	NA											
	Other activities														
OM200	Shoulder														
OM201	Unsealed Shoulder														
	(a) Edge Drop-off	Lm	Nil	Nil											No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil											Not Required
	(c) Holding water	Lm	Nil	Nil											No Holding water Found.
OM202	Embankment Repair	m ³	Nil	Nil											Not Required
	Other activities (Rain Cuts)														
OM300	Drainage including culverts major														Not Required
OM301	Surface Drains & Verge	Lm	NA	NA											Not Required
OM302	Culvert Cleaning	No	Nil	Nil											Not Required
OM303	Culvert and pit Repair	m ³	Nil	Nil											Not Required
	Other activities(Whilw washing)	m ²	Nil	Nil											

No	standard Of Work Item	Work	Unit OF Required in each Kilometere												
	Name	Unit	1	2	3	4	5	6	7	8	9	10	11	12	Comments
OM400	Vegetation														
	Grass Control														
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil											
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil											Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil											Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil											Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil											Not Required
	Other activities (Trimming of Grass)	m ²	Nil	Nil											Not Required
OM500	Safety Signage and Road														Not Required
OM501	Signs Maintanence	No	NIL	NIL											
OM502	Guard Stones	Lm	NA	NA											Not Required
OM503	Distance Stones	No	NA	NA											Not Required
OM504	Road Marking	No	Nil	Nil											Not Required
	Other activities														Not Required

Bidder

Appendix


 Executive Engineer
 Rural works Department
 Works Division, Mohania


 5/12/2022
 G.E.

Z. Balon
 05/12/2022
 A.E.

Name of Road-Lahurbari Kariram Canal Road - Seni Sarai

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
09/12/22	17:56:9	78	0.1	240	10.1	2400	2286	G	25.307573	83.707357	Normal
09/12/22	17:56:44	78	0.1	340	10.1	3400	3163	G	25.307763	83.708232	Normal
09/12/22	17:57:0	78	0.1	310	20.2	3100	2900	G	25.308087	83.70914	Normal
09/12/22	17:57:19	78	0.1	320	20.2	3200	2987	G	25.30858	83.709713	Normal
09/12/22	17:57:19	78	0.1	230	20.2	2300	2198	G	25.309235	83.71003	Normal
09/12/22	17:58:0	78	0.1	300	20.2	3000	2812	G	25.309707	83.711043	Normal
09/12/22	17:58:0	78	0.1	210	20.2	2100	2023	G	25.30968	83.711497	Normal
09/12/22	17:58:30	78	0.1	290	10.1	2900	2724	G	25.309772	83.71281	Speed Breaker
09/12/22	17:59:5	78	0.1	310	10.1	3100	2900	G	25.309578	83.713602	Normal
09/12/22	17:59:41	78	0.1	270	10.1	2700	2549	G	25.309393	83.71409	Normal
09/12/22	18:0:0	78	0.1	240	10.1	2400	2286	G	25.30884	83.715285	Normal
09/12/22	18:0:16	78	0.1	260	10.1	2600	2461	G	25.308408	83.716195	Normal
			1.2								

[Signature]
12/12/2022
J.E.

B. Gaba.
12/12/2022
A.E.

[Signature]
7/1/23

Name of Customer : Jai Maa Sherewali Construction

Name of Work/ Road : Lahurbari Kariram Canal Road -

Lab Job number

Date : 09-12-2022

Section No. 78

Test Date : 09-12-2022

Machine No : 405

Start S No : 78

Start E No :

Weather :

Start Location :

End Location :

Road Name : ariram Canal Road - Seni Sarai

Road Type : (R) RURAL ROAD

Side :

Interval

UIV Range : 1023 To 4000 1000 mm/km

Dist Range : 0 To 1.3 0.1 * 1000 m

Equation : $Y = 0 * X^2 + 0.877 * X + 181.3$


Print

Generate Report and Graph

Redraw Graph

Map View

File : E:\Mohania\New Maintenance policy 2018\Maintenance Req 18\Bump\Jai ma sherawali\22041937- seni sarai.
Name of Customer : M/S Jai Maa Sherewali Construction, Name of Work/ Road : Lahurbari Kariram Canal Road - Seni

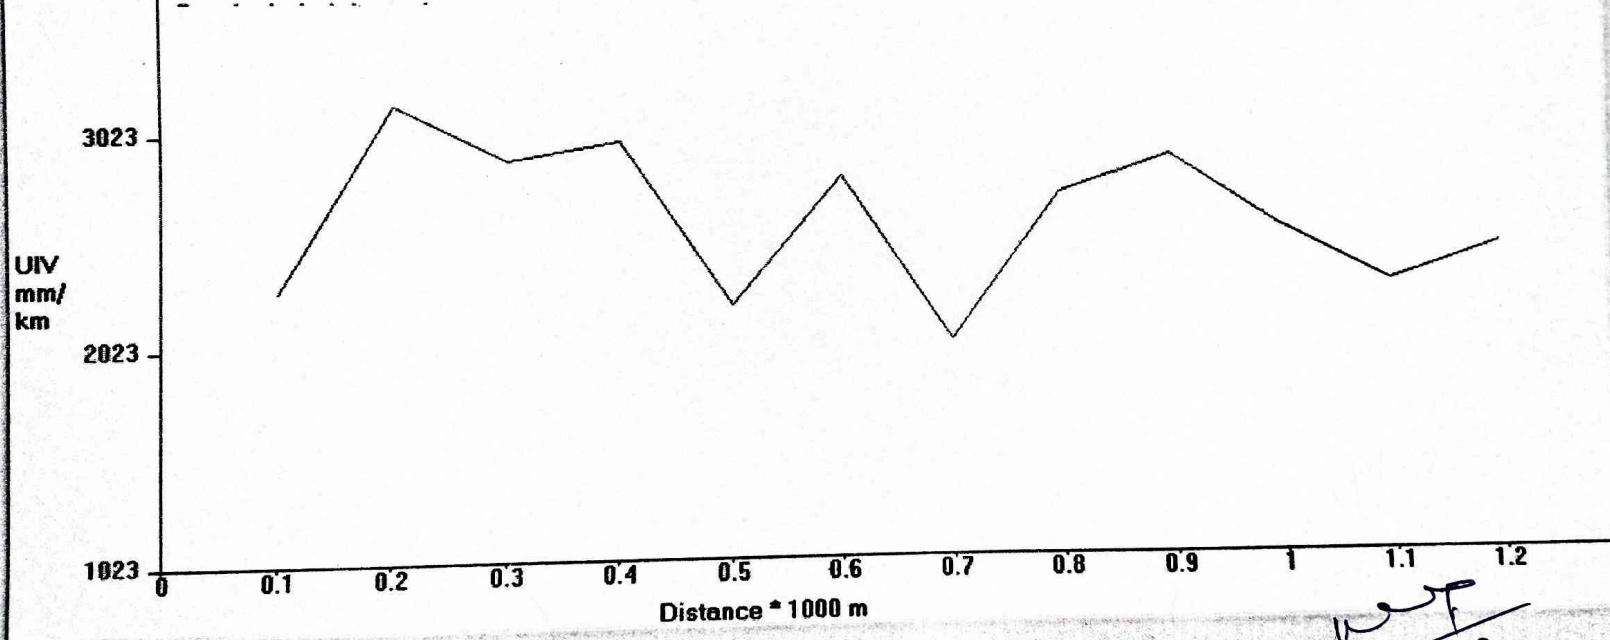

S. Balu.
12/12/2022
R.E

Executive Engineer
R.W.D. Work Division
Mohania
