

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिकहरना, ढाका।

पत्रांक - १२० / सिकहरना, ढाका, दिनांक- ३०.०६.२०२२

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिकहरना, ढाका।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग,
विश्वसरैया भवन, पाच्चा तल्ला, बिहार, पटना।

विषय :-

M/R (3054) New Maintenance Police 2018 योजना हेतु आवंटन अधियाचना
के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि इस प्रमंडलान्तर्गत M/R (3054)
New Maintenance Police 2018 योजना के अधीन कराये गये कार्य के विरुद्ध भुगतान हेतु
आवंटन अधियाचना विहित-प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनुलग्नक :- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिकहरना, ढाका।
30/6/22

FORM GFR 19-A

(See Government of Indian's Decision (1) below Rule-150)
Form of Utilisation Certificate Upto the Month of upto.....

MR 3054 New Maintenance Policy-2018**PIU :- EE RWD (W) DIVISION DHAKA**

Sl.	Name of the Scheme	Sanction No. & Date with Amount (Rs. In Lakh)	Amount Received (Rs. In Lakh)	Particulars
1	Construction of Rural Roads Under MR-3054 New Maintenance Policy-2018			Certified that out of Rs. Nil Lacs received the year 2022-23 in favor of Executive Engineer, R.W.D. (W), Division Dhaka a sum of Rs. Nil lacks has been utilized for the purpose of MR 3054 New Maintenance Policy-2018 Schemes as given in the margin for which it was sanctioned of Rs. Nil Remaining unutilized at the end of the period under.
Total :-				

Certified that I have satisfied my self that the condition on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

[Signature]
Divisional Account Officer
R.W.D. (W) Div., Dhaka

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conduct by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal Formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.

[Signature]
Executive Engineer
R.W.D.(W) Div., Dhaka
[Signature]
23/6/22

Standard Format For Roads Quarterly Statement

3rd Quarter

PIU Name :- R.W.D., Works Div. Dhaka

1	Name of Road	Dhaka Belwa ghat road to Daudnagar		
2	Batch No.	31708602076		
3	Project ID	RM/EA/SIK/20/0004		
4	Total Length of road (in K.M)	1.805		
5	Length of road to Meet Required Service Level (Completed Length) (In K.M.)	1.805		
6	No. of Total Quarter (ie 3 months as a unit) in 5 Year	20		
7	Ordinary Maintenance Cost as per Schedule {Agreement Amount For maintenance (In Lakh)}	19.26693		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (In Lakh)	0.96305		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment (6) = (3)/(1)*(2)*(4)
		Length Non Compliant	Weighted Value for Payment Reduction (%)	
	Paved Roads (Carriage Way)	0	60%	0
	Shoulders and Embankments	0	10%	0
	Cross Drainage Including Culverts and Bridges	0	15%	0
	Signage and Road Safety	0	10%	0
	Vegetation	0	5%	0
Quarterly Payment as per Agreement				0.96305
Total Payment Reduction for the Quarter (in Lakh) (As per work done length)				0.00000
Agreement Below 0.05%				0.00048
To be paid for the Quarter/Demand (In Lakh)				0.96257

Date of Inspection by E/I or his agent
Prepared by Contractor's self Control unit

Name of Designation of Person inspecting

(Signature)

Subendrakr
23/6/22

Date :- 21.06.22
Signature of Person inspecting road


Certified by E/I (Signature) Date

Requisition Formate for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
RWD, Works Division, Dhaka **(2nd Quarter)**

Government of Bihar OM01 Rural Works Department			Summary of Ordinary Maintenance Inspection Report											
Road From :- Dhaka Belwa ghat road to Daudnagar (Package No.- MR-N/19-20 Dhaka/22)								To Executive Engineer RWD, Works Division, Dhaka					Date :-	
Length of Road :- 1.805 Km Period From :- 25.11.2021 to 24.02.2022 Inspector :- AE, RWD, Sub Division, Dhaka								Position :- A.E						
No.	Standard of Works Item	Work	Unit of Required in each Kilometer										Comments	
	Name	Unit	1	2	3	4	5	6	7	8	9	10		
OM100	Seesla Payment													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No Pot Hole Found	
OM102	Surface Depression and Rut Patching	m3	Nil	Nil	Nil	Nil								
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing area Found	
OM104	Surface Treatment													
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregates not found	
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil								
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil								
105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required	
106	Digouts	m2	Nil	Nil	Nil	Nil							Not Required	
107	Concrete pavement	m3	Nil	Nil	Nil	Nil								
OM200	Other Activities		Nil	Nil	Nil	Nil								
	Shoulder		Nil	Nil	Nil	Nil								
OM201	Unsealed Shoulder		Nil	Nil	Nil	Nil								
	(a) Edge Drop-off		Nil	Nil	Nil	Nil								
	(b) Roughness Scouring or potholes	Lm	Nil	Nil	Nil	Nil							Not Required	
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil								
OM202	Embankment Repair	Lm	Nil	Nil	Nil	Nil								
	Other activities (Rain Cuts)	M3	Nil	Nil	Nil	Nil								
OM300	Drainage including culverts major		Nil	Nil	Nil	Nil								
OM301	Surface Drains & Verge	Lm	Nil	Nil	Nil	Nil								
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil								
OM303	Culvert and Pit Repair	M3	Nil	Nil	Nil	Nil							Not Required	
	Other activities (Whilw Washing)	M2	Nil	Nil	Nil	Nil							Not Required	
No.	Standard of Work Item	Work	1	2	3	4	5	6	7	8	9	10	Comments	
OM400	Vegetation		Nil	Nil	Nil	Nil								
	Gross Control		Nil	Nil	Nil	Nil								
OM401	(a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil								
	(b) Clear near Safety signs, Kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil								
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required	
	Cutting of Branches of Trees	No	Nil	Nil	Nil	Nil								
	Cutting of Shrubs From Road Way	No	Nil	Nil	Nil	Nil								
	Other Activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required	
OM500	Safety Signage and Road		Nil	Nil	Nil	Nil								
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required	
OM502	Guard Stones	Lm	Nil	Nil	Nil	Nil								
OM503	Distance Stones	No	Nil	Nil	Nil	Nil							Not Required	
OM504	Road Marking	M2	Nil	Nil	Nil	Nil							Not Required	
	Other activities													

Bidder

Subendrakr
 21.06.22
 Appendix


 23/6/22
 Executive Engineer
 RWD, Works Division, Dhaka

Name of Customer: SHANDALIYA ENTERPRISES

Name of Work/ Road: DHAKA BELWA GHAT SE DAWD NAGER

Lab Job number:

Date: 18-11-2021

Section No. 6

Test Date: 18-11-2021

Machine No: 406

Start S No:

Start E No:

Weather:

Start Location: DHAKA BELWA

End Location: DAWD NAGER

Road Name: WA GHAT SE DAWD NAGER

Road Type: (A) ASPHALTIC

Side:

Interval

UIV Range: 449 To 4000 1000 mm/km

Dist Range: 0 To 1.9 0.1 * 1000 m


Equation: test

Print

Generate Report and Graph

Redraw Graph

Map View

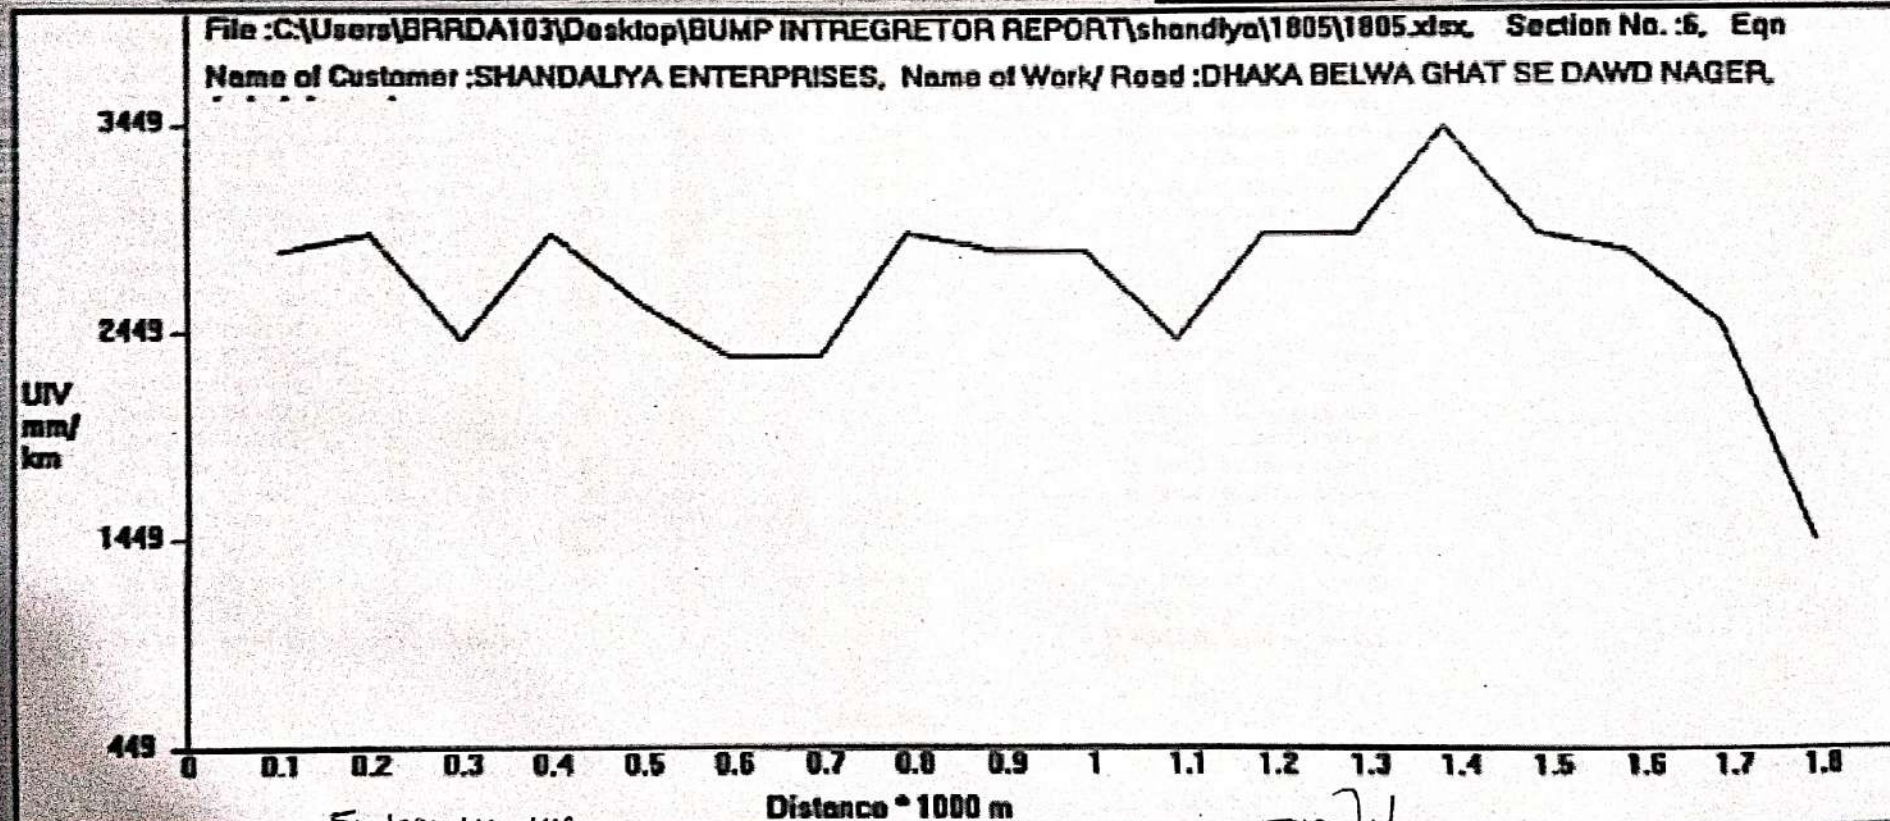

Subendra K.

21.06.22

Shandhya
23/6/22

Date	Time	Section No.	Length in km	Bumps in mm	Speed km/hr	OR km/hr	IRI CATEGORY ROAD
ROAD NAME- Chaka Behwa Ghat To Dandi Nagar							
18/11/21	15:30:9	59	0.1	330	20.2	3300	3300 G
18/11/21	15:30:44	59	0.1	340	30.3	2400	2338 G
18/11/21	15:31:0	59	0.1	230	30.3	2300	2231 G
18/11/21	15:31:0	59	0.1	340	20.2	2400	2338 G
18/11/21	15:31:21	59	0.1	240	30.3	2400	2338 G
18/11/21	15:31:23	59	0.1	280	20.2	2800	2666 G
18/11/21	15:31:23	59	0.1	210	30.3	2300	2057 G
18/11/21	15:32:0	59	0.1	260	30.3	2600	2492 G
18/11/21	15:32:0	59	0.1	210	30.3	2300	2057 G
18/11/21	15:32:0	59	0.1	340	20.2	3400	3387 G
18/11/21	15:32:33	59	0.1	240	30.3	2400	2338 G
18/11/21	15:33:0	59	0.1	250	30.3	2500	2405 G
18/11/21	15:33:7	59	0.1	300	20.2	3000	2839 G
18/11/21	15:33:7	59	0.1	290	20.2	2900	2752 G
18/11/21	15:33:7	59	0.1	300	20.2	3000	2839 G
18/11/21	15:33:42	59	0.1	300	30.3	3000	2839 G
18/11/21	15:34:0	59	0.1	290	30.3	2900	2752 G
18/11/21	15:34:0	59	0.1	250	30.3	2500	2405 G
18/11/21	15:34:17	59	0.1	300	30.3	3000	2839 G
18/11/21	15:34:17	59	0.1	330	20.2	3300	3300 G
18/11/21	15:34:17	59	0.1	240	30.3	2400	2338 G
18/11/21	15:35:0	59	0.1	230	30.3	2300	2231 G
18/11/21	15:35:0	59	0.1	240	20.2	2400	2338 G
18/11/21	15:35:0	59	0.1	240	30.3	2400	2338 G
18/11/21	15:35:28	59	0.1	280	20.2	2800	2666 G
18/11/21	15:35:28	59	0.1	210	30.3	2300	2057 G
18/11/21	15:36:3	59	0.1	260	30.3	2600	2492 G
18/11/21	15:36:3	59	0.1	210	30.3	2300	2057 G
18/11/21	15:36:38	59	0.1	330	20.2	3300	3300 G
18/11/21	15:36:38	59	0.1	270	20.2	2700	2579 G
18/11/21	15:37:13	59	0.1	330	20.2	3300	3300 G
18/11/21	15:37:13	59	0.011	170	30.3	3036	2871 G
TOTAL						11765	
AVERAGE						2555.15	

Latitude	Longitude	Event
$Y = 0^\circ X^2 + 0.869^\circ X + 232.9$		
26.76764	85.11545	Normal
26.76777	85.11552	Normal
26.76855	85.11611	Normal
26.76932	85.1167	Normal
26.77009	85.11724	Normal
26.77081	85.11774	Normal
26.77163	85.11832	Normal
26.77238	85.11886	Normal
26.77311	85.11938	Normal
26.77374	85.12008	Normal
26.77447	85.12077	Normal
26.77527	85.12114	Normal
26.77596	85.12173	Normal
26.77678	85.12226	Normal
26.77759	85.12274	Normal
26.77841	85.12323	Normal
26.77923	85.12365	Normal
26.78001	85.12409	Normal
26.7805	85.12483	Normal
26.78096	85.12571	Normal
26.78177	85.12604	Normal
26.7827	85.12628	Normal
26.78353	85.12653	Normal
26.78443	85.1268	Normal
26.78533	85.12695	Normal
26.78613	85.12678	Normal
26.78696	85.12676	Normal
26.7878	85.12613	Normal
26.78862	85.12646	Normal
26.78954	85.12657	Normal
26.79044	85.12658	Normal
26.79133	85.12667	Normal

(5) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5000

Subendrak
21.06.22

Samal
23/6/22
