

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

पत्रांक—...493(2023)

दिनांक—...04/03/2023...

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति 2018” (3054-MR)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण नीति 2018” योजनान्तर्गत पथ:-

1. BETTIAH NARKATIAGANJ ROAD – RAMPURWA

का कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाषन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नरकटियागंज

**Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj**

Requisition Format for Scheme Head - MIR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative Length (in Km)	Administrative Amount	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	RM/WE/NAR/22/0003	BETTIH NARKATIAGANJ ROAD - RAMPURWA	31808802066	1585 30.03.2022	2.9	78.22000	84.41211 (in Lakh)	47/22-23 11.10.2022	10.10.2023	2968	SDBC-25mm	5%	0.00000	0.00000	84.40000	Surface Complete



Divisional Account Officer
Rural Works Department
Works Division Narkatiaganj


Executive Engineer
Rural Works Department
Works Division Narkatiaganj

Office of the Executive Engineer RWD Works Division, Narkatiaganj


Name of Road :- BETTIAH NARKATIAGANJ ROAD - RAMPURWA
Name of Scheme :- MR 3054 New Maintenance Policy 2018
Name of Contractor :- Arvind Kumar Singh
Length of Road :- 2.900 Km
Project ID :- 31808802066
Package No :- RM/WE/NAR/22/0003
Name of Block :- Chanpatia

Certified that all item wise 100% measurement has been taken by me



03.03.2023

Certified that all item wise 50% measurement has been Verified by me



03/03/23

Certified that all item wise 10% measurement has been taken by me



03/03/23

Name of Road - BETTIAH NARKATIAGANJ ROAD - RAMPURWA (Sec-68)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
3/3/23	12:53:29	68	0.1	280	0	2800	2772	G	26.875388	84.516548	Normal
3/3/23	12:54:4	68	0.1	270	21.3	2700	2714	G	26.875025	84.517423	Normal
3/3/23	12:54:4	68	0.1	280	21.3	2800	2788	G	26.874685	84.518315	Normal
3/3/23	12:54:39	68	0.1	320	31.4	3200	3188	G	26.874398	84.519242	Normal
3/3/23	12:55:14	68	0.1	290	21.3	2900	2853	G	26.87403	84.52013	Normal
3/3/23	12:55:50	68	0.1	280	21.3	2800	2841	G	26.873258	84.520638	Normal
3/3/23	12:56:25	68	0.1	270	21.3	2700	2749	G	26.872575	84.521295	Normal
3/3/23	12:57:0	68	0.1	340	11.2	3400	3377	G	26.871988	84.521985	Normal
3/3/23	12:57:0	68	0.1	300	21.3	3000	2958	G	26.87143	84.52276	Normal
3/3/23	12:57:36	68	0.1	290	21.3	2900	2853	G	26.87103	84.523635	Normal
3/3/23	12:58:10	68	0.1	350	21.3	3500	3482	G	26.87057	84.524443	Normal
3/3/23	12:58:45	68	0.1	340	11.2	3400	3377	G	26.86981	84.524292	Normal
3/3/23	12:59:0	68	0.1	300	21.3	3000	2958	G	26.869078	84.524325	Normal
3/3/23	12:59:20	68	0.1	290	21.3	2900	2853	G	26.868772	84.525202	Normal
3/3/23	13:0:0	68	0.1	260	24.3	2600	2586	G	26.868782	84.526212	Normal
3/3/23	13:0:0	68	0.1	330	26.2	3300	3272	G	26.869035	84.527103	Normal
3/3/23	13:0:31	68	0.1	260	24.5	2600	2579	G	26.86882	84.528097	Normal
3/3/23	13:1:6	68	0.1	300	24.7	3000	2951	G	26.868563	84.52904	Normal
3/3/23	13:1:42	68	0.1	270	24.2	2700	2684	G	26.86831	84.529982	Normal
3/3/23	13:2:0	68	0.1	330	24.2	3300	3272	G	26.868053	84.530875	Normal
3/3/23	13:2:17	68	0.09	320	31.4	3200	3228	G	26.867758	84.531852	Normal
Average IRI Value=							2968				

[Handwritten Signature]

[Handwritten Signature]
03/03/2023

[Handwritten Signature]
03.03.2023

Name of Customer : ARVIND KUMAR SINGH

Name of Work/Road : BETTIAH NARKATAGANJ ROAD

Lab Job number : _____

Date : 03-03-2023

Section No. : 68

Test Date : 03-03-2023

Road Name : BETTIAH NARKATAGANJ ROAD

Machine No : 402

Road Type : (R) RURAL ROAD

Start S No : _____

Side : _____

Start E No : _____

Interval : _____

Weather : _____

U/V Range : 1579 To 4000 mm/km

Dist Range : 0 To 22

Equation : $Y = 0 \cdot X^2 + 1136 \cdot X + 132.5$


Print Generate Report and Graph

Redraw Graph

Map View

File : F:\03031455.Xls, Section No. : 68, Eqn : $Y = 0 \cdot X^2 + 1136 \cdot X + 132.5$

Name of Customer : ARVIND KUMAR SINGH, Name of Work/Road : BETTIAH NARKATAGANJ ROAD -

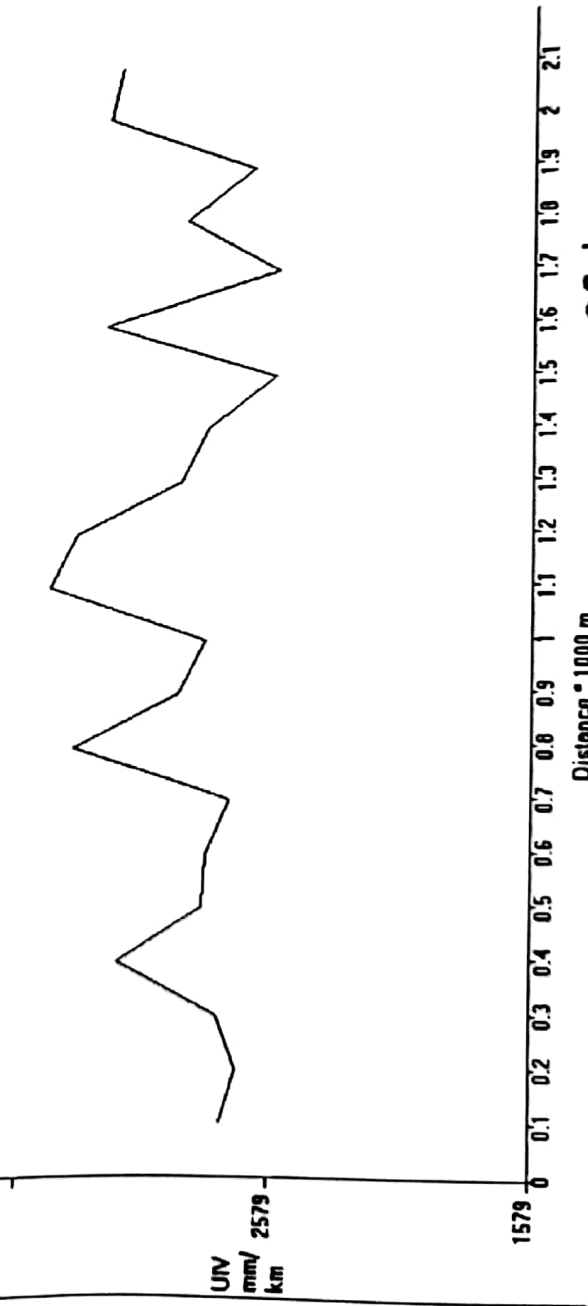

[Signature]
03.03.2023

[Signature]
03.03.2023

[Signature]
03.03.2023
