

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दानापुर।

पत्रांक:- 368 अड्ड

दानापुर/दिनांक:-21/03/23

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल दानापुर।

सेवा में,

सचिव ब्राडा (बी.आर.आर.डी.ए.)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-शीर्ष-3054 (एम.आर.) बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 योजना
अंतर्गत अनुरक्षण मद में आवंटन के अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-3054 (एम.आर.) बिहार
ग्रामीण पथ नई अनुरक्षण नीति-2018 योजना अंतर्गत अनुरक्षण मद में निम्नांकित पथों का
आवंटन के अधियाचना का मांग (Yearly Quarter Wise) तैयार कर आवश्यक
कार्रवाई हेतु समर्पित की जा रही है जो निम्न प्रकार है।

अतः अनुरोध है कि उक्त योजना
अन्तर्गत अनुरक्षण मद में आवंटन उपलब्ध कराने की कृपा की जाये ताकि संवेदक का
भुगतान किया जा सके।

(यथोक्त)

विश्वासभाजन


21/03/23
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल दानापुर।

21/3/23

Sl.No	Name of The Road	Yearly Quarter Wise	Amount (In Lakh)
1.	Phulwari Mission Road- Ganjpar (Pkg.No-RM/PA/DAN/20/0013)	1 st Year- 1 st Quarter	1.69770
		1 st Year- 2nd Quarter	1.69770
2.	Janipur-Mohanchak Sorangpur High School Road Chak Manjhi) (Pkg.No-RM/PA/DAN/20/0013)	1 st Year- 1 st Quarter	0.47565

Ali
14/12/23
AG

20
21/12/23

21/12/23
सर्वप्रकार के सर्वेक्षण
समीक्षा कार्य विभाग
कर्मचारी, बिलासपुर
21/12/23

Requisition Format for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and Surface Renewal)

RWD, Works Division, Danapur
Government Of Bihar

1st Year (1st Quarter)

Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Janipur - Mohanbhak Sorangpur High School Road (Chak Manjh)
(Package No:- RM/PA/DAN/20/0013)
Length of Road :- 1.400 Km
Inspector :- JE RWD Sub Division :- Phulwari Sharif

To:-
Executive Engineer
RWD, Works Division, Danapur

Position :- JE

No	Standard of Work Item Name	Work Unit	Unit Required in each Kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m ²	Nil	Nil									No Pot Hole found.
OM102	Surface Depression and Rut Patching	m ³	Nil	Nil									Not Surface Depression & Rut Patching Found
OM103	Crack sealing	Lm	Nil	Nil									No Crack found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil									No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil									No Bleeding/ Flushing Required
	© Crocodile Cracking	m ²	Nil	Nil									No Crocodile Cracking Found
105	Edge Repair	m ²	Nil	Nil									No Edge Repair Required
106	Digouts	m ²	N/A	N/A									Not Required
107	Concrete pavement	m ³	N/A	N/A									N/A
OM200	Other activities												
	Shoulder												
	Unsealed shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil									No Edge Drop Off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil									No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	Nil	Nil									No Holding Water found
	Other activities (Rain Cuts)	m ³	Nil	Nil									Repaired as required
OM202	Embankment Repair												N/A
OM300	Drainage including Culverts major	Lm	N/A	N/A									N/A
OM301	Surface Drains & Verges	No	Nil	Nil									Cleaned
OM302	Culvert Cleaning	m ³	Nil	Nil									Not Required
OM303	Culvert and Pot Repair	m ²	Nil	Nil									Not Required
	Other activities (While washing)	m ²	Nil	Nil									Not Required

No	Standard of Work Item Name	Work Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation	Unit											
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil									Not Required
	(b) Clear near Safety signs, kilometre posts and road side furniture	Ha	Nil	Nil									Not Required
OM402	Tree and Shrub Management	No	Nil	Nil									Not Required
	Cutting of Branches of Trees	No	Nil	Nil									Not Required
	Cutting of Shrubs from Road Way	No	Nil	Nil									Not Required
	Other activities (Trimming of Grass)	M ²	Nil	Nil									Not Required
OM500	Safety Signage and Road	Nil	Nil										Not Required
OM501	Signs Maintenance	No	Nil	Nil									Maintained
OM502	Guard Stones	Ln	N.A	N.A									Maintained
OM503	Distance Stones	No	N.A	N.A									Maintained
OM504	Road Marking	M ²	Nil	Nil									N/A
	Other activities												

15/10/2019

Executive Engineer
Rural Works Department
Works Division, Danapur

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road-	Janipur- Mohanchak Sorangpur High School Road (Chak Manjhi)
2	Batch No.-	RM/PA/DAN/20/0013
3	Project ID -	10100102062
4	Total Length of Road (in Km)	1.400
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	1.400
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	9.51299
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.47565

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.47565

Date of inspection by E/I or his agent

Date

Signature of person inspecting road

Name and Designation of person inspecting road

Certify by E/I (Signature) Date

Package No:- MR/N/20-21-Danapur/13

Block:- Fulwarisharif

Date	Time	Section	No.	Length In km	Bumps In mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$V = 0 \cdot X \cdot 2 + 0.920 \cdot X + 216.7$		
14/1/23	10:50:41	24	0.1	380	0	3800	3712	G		25.527138	85.6003	Speed Breaker	X = 3100		
14/1/23	10:51:0	24	0.1	340	10.1	3400	3460	G		25.52696	85.60908	Curve	Y = 3068		
14/1/23	10:51:16	24	0.1	390	30.3	3900	3928	G		25.527435	85.61515	Speed Breaker	(R) RURAL ROAD		
14/1/23	10:51:16	24	0.1	370	20.2	3700	3620	G		25.527235	85.62457	Normal	Good	Average	Poor
14/1/23	10:52:0	24	0.1	380	20.2	3800	3712	G		25.527035	85.6347	Normal			
14/1/23	10:52:26	24	0.1	360	20.2	3600	3648	G		25.526595	85.64157	Curve			
14/1/23	10:52:26	24	0.1	360	30.3	3600	3648	G		25.525757	85.63955	Normal			
14/1/23	10:53:1	24	0.1	380	20.2	3800	3712	G		25.524935	85.63803	Curve			
14/1/23	10:53:1	24	0.1	360	30.3	3600	3648	G		25.524607	85.64713	Speed Breaker			
14/1/23	10:53:36	24	0.1	380	20.2	3800	3712	G		25.524395	85.65707	Normal			
14/1/23	10:53:36	24	0.1	370	20.2	3700	3620	G		25.524265	85.66458	Curve			
14/1/23	10:54:0	24	0.1	320	30.3	3200	3273	G		25.524473	85.67508	Normal			
14/1/23	10:54:10	24	0.1	390	30.3	3900	3928	G		25.524447	85.68518	Normal			
14/1/23	10:54:17	24	0.1	380	20.2	3800	3712	G		25.524232	85.69528	Speed Breaker			
TOTAL			1.400	5160.000	303.000	51600	51333								
AVERAGE						3685.714286	3666.642857								

3/10/2023
14/1/23

कार्यपालक अधिकारी
श्रीमान कर्ण विष्णु
कोशी प्रदेश, बानेश्वर

Name of Customer :	FreeDagan Construction P.M.Ltd
Name of Work/ Road :	Jampur-Mohanchak Sorengpur
Lab Job number :	
Date :	14-01-2023
Section No.	24


Test Date :	14-01-2023	Road Name :	Jampur-Mohanchak Sorengpur
Machine No :	374	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval :	
Weather :		UV Range :	3273 To 5000
Start Location :		Dist Range :	0 To 15
End Location :		Equation :	Y = 0 * X - 2 + 0.936 * X + 278.4

Print Generate Report and Graph

Redraw Graph

Map View

File : G:\Offline Maintenance Requisition\Package No-1\325071612.Xls, Section No.: 24, Eqn: $Y = 0 * X - 2 + 0.936$
 Name of Customer : FreeDagan Construction P.M.Ltd, Name of Work/ Road : Jampur-Mohanchak Sorengpur High

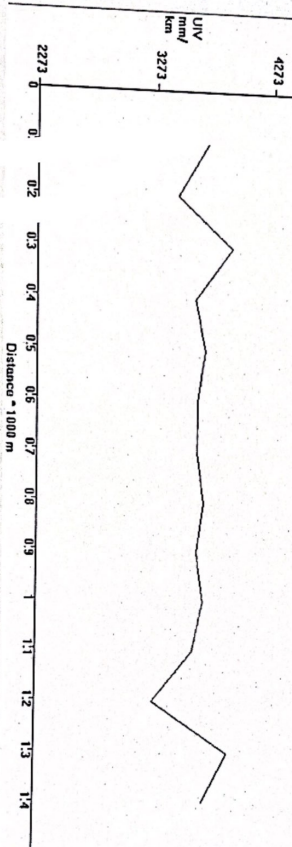

24/1/23

उपरोक्त ग्राफ को
 ध्यान से देखें
 और त्रुटि बताएं
