

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा-1।

पत्रांक.../143737/छ छपरा-1/दिनांक...11-10-22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-1

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :-

नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-1।

(Cuma)
11.10.22

Name of Works Division:- Chapra-1

Maintenance Requisition Formate for Scheme Head- MR (3054) Under

Road Details					AA Details		Agreement							
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
1	CHANAPUR - JAMANPURA	RM/SA/C HA/19/0 019	31306302024	26/04/2021	36.047	17.45255	36.047	3.49051	3.49051	3.49051	3.49051	3.49051	17.45255	1.56
2	SITALPUR - SADHPUR	RM/SA/C HA/19/0 019	31306302076	1/1/2022	31.479	14.40881	31.479	1.53406	2.10952	2.94642	2.64774	5.17107	14.40881	1.46
3	T-011 - SALIMPATTI	RM/SA/C HA/19/0 019	31306302082	8/3/2022	79.083	37.79181	79.083	3.9548	5.41655	8.44099	6.78578	13.1937	37.79181	3.7
Total _____					146.61	69.65	146.61	8.98	11.02	14.88	12.92	21.86		

Bihar Rural Road Maintenance Policy-2018

Actual Maintenance Expenditure						Current Maintenance Demand										Remarks
1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
0.00000	0.00000	0.00000	0.00000	0.00000	0.00000	1645	1.56	0.87262	0.87262	0.87262	0.87262	1	1	1	3.49048	
0.00000	0.00000	0.00000	0.00000	0.00000	0.00000	2562	1.46	0.72044	0.72044	1	1	1	1	1	1.44088	
0.00000	0.00000	0.00000	0.00000	0.00000	0.00000	2431	3.7	1.88959	1	1	1	1	1	1	1.88959	
0.00	0.00	0.00	0.00	0.00	0.00			3.48	1.59	0.87	0.87	0.00	0.00	0.00	6.82	


 Executive Engineer
 R.W.D. Works Division
 Chapra-1
 11.10.22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	CHANAPUR - JAMANPURA		
2	Batch No.	RM/SA/CHA/19/0019		
3	Project ID	31306302024		
4	Total Length of Road (in Km)	1.56		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	1.56		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	17.45255		
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.87262		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.87262

Date of inspection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

(Cumer)
11.10.22

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MIR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Chapra-1

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- CHANAPUR - JAMANPURA

Length of Road: 1.56 KM

Period : From.....

Inspector: A.E RWD Sub Division,Manjhi

To: Executive Engineer


RWD Works Division Chapra-1

Date:

Position: A.E

S No	Standard Work item Name	Work Units	Units of work required in each kilometre										Comments
			1	2	3	4	5	6	7	8	9	10	
OM101	OM100 Sealed Pavement												
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
	Surface Treatment												
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200	Shoulder												
	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
OM201	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%	Nil							Defects rectified within stipulated time.
OM 300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required

File : C:\Users\del\Downloads\27031008.Xls. Section No. : 60. Eqn : $Y = 0 \cdot X^2 + 0.816 \cdot X + 249$
 Name of Customer : Santoshi Singh. Name of Work/ Road : Chanaupur To Jamnapura. Lab Job number :

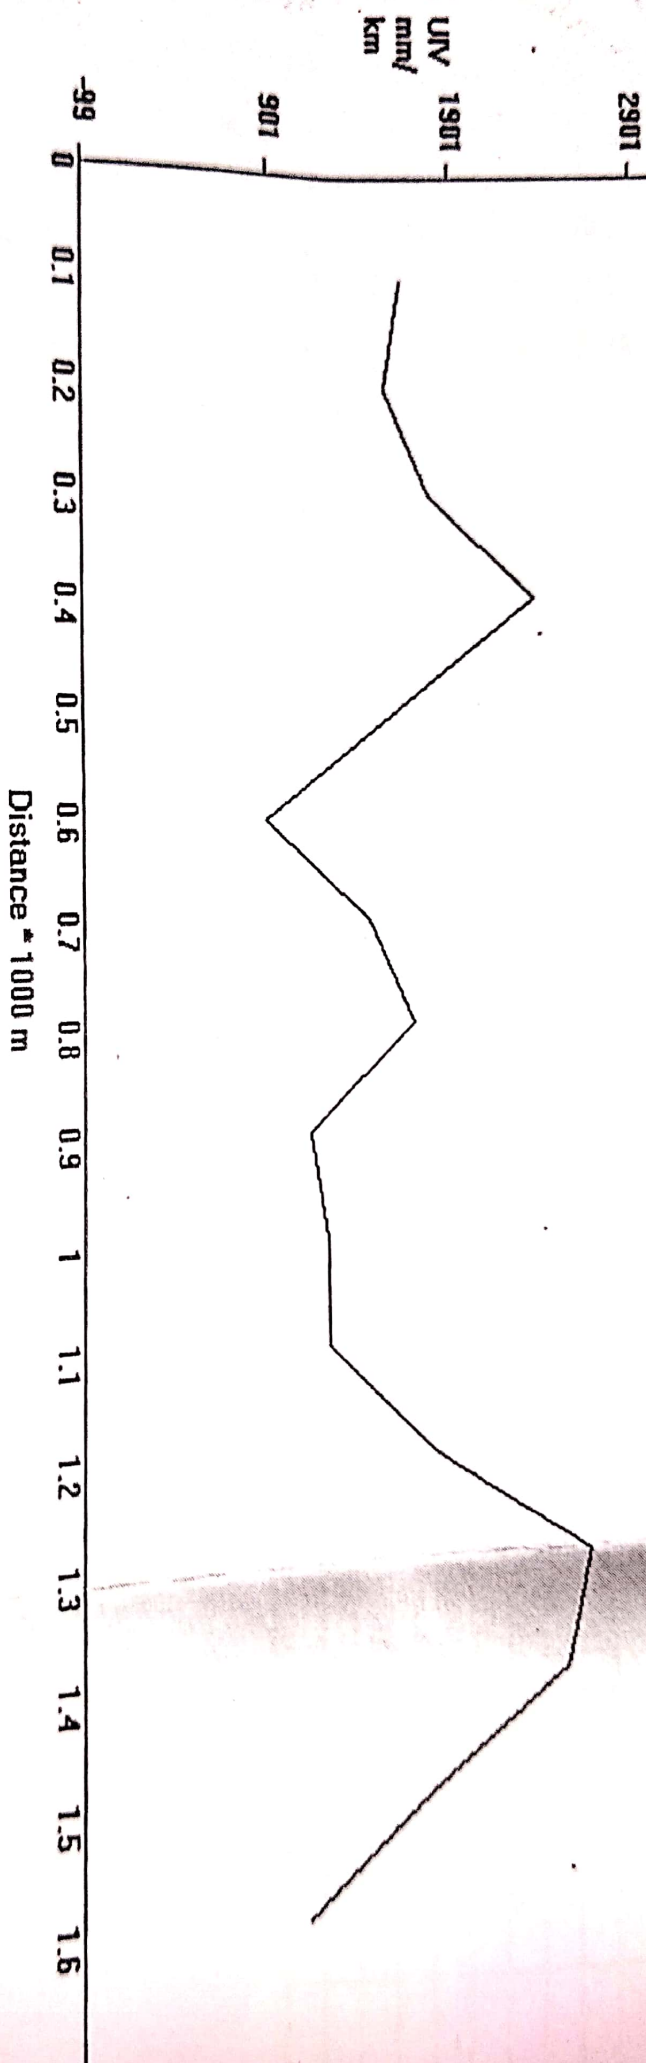

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	In mm	Rate	mm/km	mm/km	ROAD			$Y = 0 * X^2 + 0.816 * X + 249$			
27/3/21	9:53:0	60	0.1	170	0	1700	1636	G	25.92397	84.514225	Normal	X = 984		
27/3/21	9:53:0	60	0.1	160	10.1	1600	1554	G	25.924357	84.514865	Normal	Y = 1051		
27/3/21	9:53:34	60	0.1	190	10.1	1900	1799	G	25.92461	84.515605	Normal			
27/3/21	9:56:0	60	0.1	260	10.1	2600	2370	G	25.92452	84.516632	Culvert			
27/3/21	9:57:40	60	0.1	170	10.1	1700	1636	G	25.9229	84.518502	Normal	(R) RURAL ROAD		
27/3/21	9:58:0	60	0.1	80	20.2	800	901	G	25.922135	84.518803	Normal	Good	Average	Poor
27/3/21	9:58:15	60	0.1	150	10.1	1500	1472	G	25.921355	84.519225	Curve	<4000	4001-5000	>5001
27/3/21	9:58:51	60	0.1	180	10.1	1800	1717	G	25.920655	84.519427	Normal			
27/3/21	9:59:0	60	0.1	110	20.2	1100	1146	G	25.920593	84.52042	Normal			
27/3/21	9:59:0	60	0.1	120	20.2	1200	1228	G	25.920668	84.52143	Normal			
27/3/21	9:59:26	60	0.1	120	20.2	1200	1228	G	25.920927	84.522357	Normal			
27/3/21	9:59:26	60	0.1	190	20.2	1900	1799	G	25.920872	84.52338	Normal			
27/3/21	10:0:1	60	0.1	290	20.2	2900	2615	G	25.920922	84.52443	Normal			
27/3/21	10:0:1	60	0.1	270	10.1	2700	2452	G	25.921352	84.52515	Normal			
27/3/21	10:5:19	60	0.1	180	10.1	1800	1717	G	25.922015	84.52574	Normal			
27/3/21	10:7:5	60	0.1	90	10.1	984	1051	G	25.921937	84.525655	Normal			
						Total-	26321							
