

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा-1।

पत्रांक 391/8179 छपरा-1/दिनांक 14.03.2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-1

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये अनुरक्षण कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये अनुरक्षण कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-1।

14.03.2023

Road Details					AA Details		Agreement							
Sl. No.	Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15
1	FURSATPUR - HASANPURA	RM/SA/CHA/19/0001	31306202043	28/06/2021	42.601	17.61057	42.601	1.60203	2.53656	6.08622	3.00532	4.38044	17.61057	2.2
2	SAHO SARAY - SARGATTI	RM/SA/CHA/19/0001	31306202096	10/10/2021	20.205	7.29102	20.205	0.41425	0.86802	2.43907	0.94613	2.62355	7.29102	1
Total					62.81	24.90	62.81	2.02	3.40	8.53	3.95	7.00	24.90	3.20

Rural Road Maintenance Policy-2018

Actual Maintenance Expenditure						Current Maintenance Demand										Remarks
1st Year Maintenance	2nd Year Maintenance	3rd Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintenance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total	
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
0.00000	0.00000	0.00000	0.00000	0.00000	0.00000	2.2	3229	0.88052	0.88052	0.88052	0.88052	0.88052	0.88052	1	5.28312	
0.00000	0.00000	0.00000	0.00000	0.00000	0.00000	1	3135	0.36455	0.36455	0.36455	0.36455	0.36455	1	1	1.82275	
															7.10587	


Executive Engineer
R.W.D. Works Division
Chapra-I

Deer

14.03.2023

Chandra
14/03/2023

File :E:\Lalan Kumar\FURSATPUR - HASANPURA\05040852.xls. Section No. :33. Eqn : $Y = 0.0000X^2 + 1.0000X +$
Name of Customer :Lalan Kumar, Name of Work Road :FURSATPUR - HASANPURA. Lab Job number :

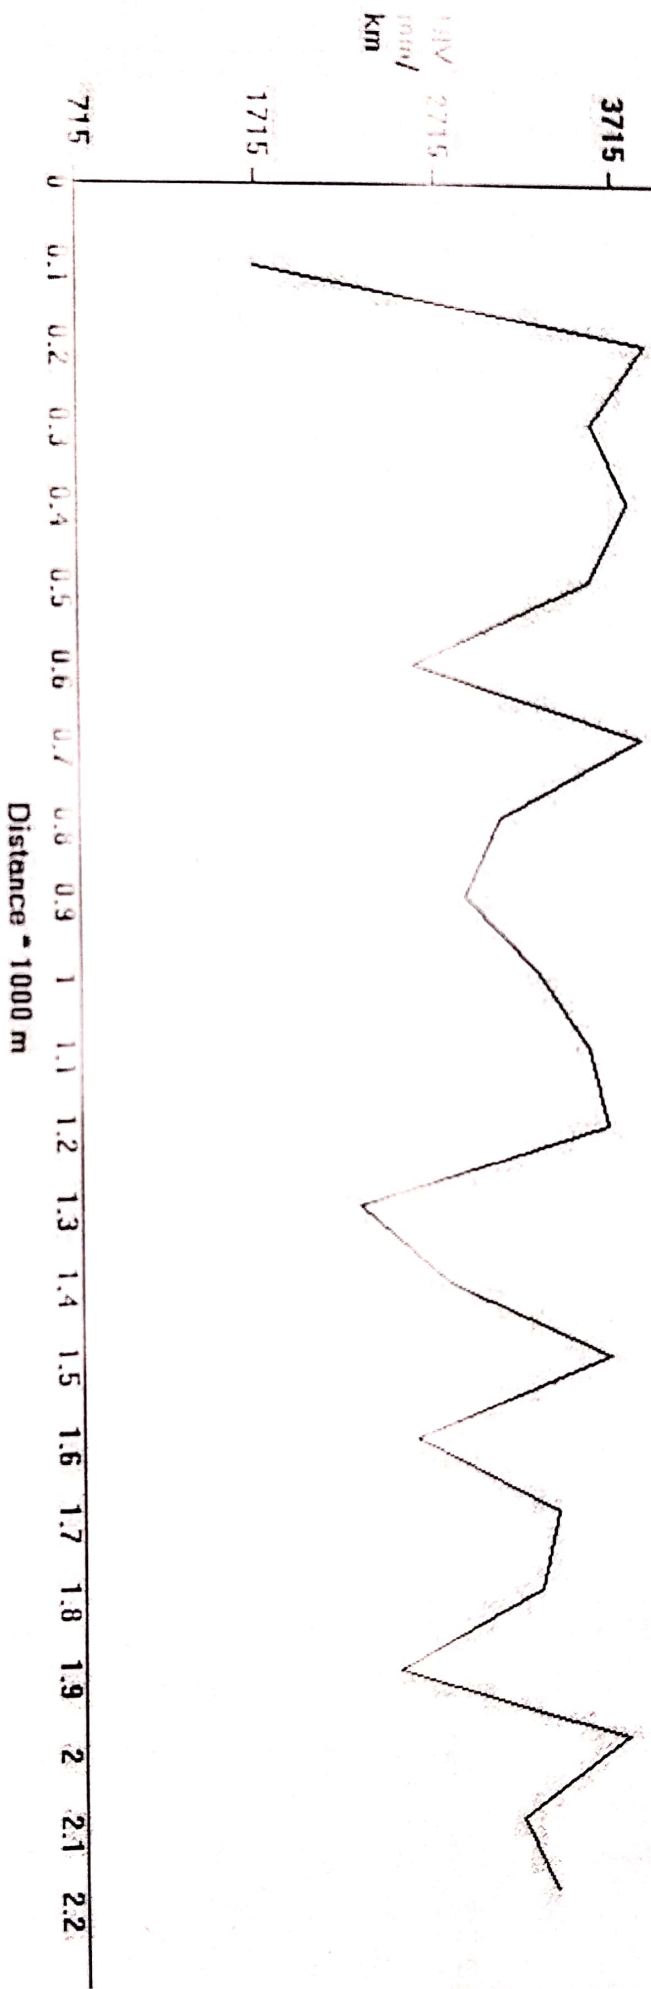

Scheme - New MR
Road Name- FURSATPUR - HASANPURA

Contractor Name - Lalan Kumar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event	Y = 0 * X ^ 2 + 1.000 * X + 415.2		
5/10/21	8:27:39	33	0.1	130	10.1	1300	1715	G	25.824394	84.851244	Normal	X = 3000		
5/10/21	8:28:15	33	0.1	350	10.1	3500	3915	G	25.823994	84.851733	Normal	Y = 3415		
5/10/21	8:29:0	33	0.1	320	10.1	3200	3615	G	25.823774	84.853143	Normal			
5/10/21	8:29:24	33	0.1	340	20.2	3400	3815	G	25.823932	84.853306	Curve			
5/10/21	8:30:0	33	0.1	320	20.2	3200	3615	G	25.82347	84.854477	Normal	(R) RURAL ROAD		
5/10/21	8:30:0	33	0.1	220	10.1	2200	2615	G	25.823315	84.854702	Curve	Good	Average	Poor
5/10/21	8:30:35	33	0.1	350	10.1	3500	3915	G	25.822593	84.855561	Normal	<4000	4001-5000	>5001
5/10/21	8:31:10	33	0.1	270	20.2	2700	3115	G	25.82173	84.856178	Speed Breaker			
5/10/21	8:31:45	33	0.1	250	20.2	2500	2915	G	25.820785	84.85627	Normal			
5/10/21	8:32:0	33	0.1	290	10.1	2900	3315	G	25.820191	84.856133	Speed Breaker			
5/10/21	8:32:21	33	0.1	320	10.1	3200	3615	G	25.819119	84.855721	Normal			
5/10/21	8:33:0	33	0.1	330	20.2	3300	3715	G	25.818846	84.855531	Normal			
5/10/21	8:33:0	33	0.1	190	30.3	1900	2315	G	25.817761	84.856221	Normal			
5/10/21	8:34:6	33	0.1	240	20.2	2400	2815	G	25.817586	84.85678	Normal			
5/10/21	8:34:6	33	0.1	330	30.3	3300	3715	G	25.816818	84.857382	Speed Breaker			
5/10/21	8:35:0	33	0.1	220	10.1	2200	2615	G	25.815783	84.857976	Normal			
5/10/21	8:35:17	33	0.1	300	40.4	3000	3415	G	25.815177	84.858593	Normal			
5/10/21	8:35:17	33	0.1	290	40.4	2900	3315	G	25.814773	84.858957	Curve			
5/10/21	8:36:0	33	0.1	210	30.3	2100	2515	G	25.816943	84.86008	Normal			
5/10/21	8:36:0	33	0.1	340	40.4	3400	3815	G	25.817074	84.859098	Normal			
5/10/21	8:36:28	33	0.1	280	40.4	2800	3215	G	25.817574	84.858055	Curve			
5/10/21	8:37:3	33	0.1	300	30.3	3000	3415	G	25.817589	84.857234	Normal			
Total									71030					
IRI Value									3229					

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	FURSATPUR - HASANPURA		
2	Batch No.	RM/SA/CHA/19/0001		
3	Project ID	31306202043		
4	Total Length of Road (in Km)	2.2		
5	Length of Road to Meet Required Service Level [Completed length] (in Km) (1)	3.2		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	17.61057		
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.88052		
Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				0.88052

Date of inpection by E/I or his agent Prepared by
Contractor's self Control unit

Date

Signature of person inspecting road

Name and Designation of person inspecting road
(Signature)

14.03.2023

Certify by E/I (signature) Date

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Chapra-1

Government of Bihar

OM01

Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- FURSATPUR - HASANPURA

Length of Road: 2.2 KM

Period : From.....

Inspector: A.E RWD Sub Division, GARKHA

To: Executive Engineer
RWD Works Division Chapra-1

Date:

Position: A.E

Standard Work item			Work		Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10			
OM100 Sealed Pavement															
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.		
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found		
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found		
Surface Treatment															
OM104	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Aggregate (Surface Ravelling) found		
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required		
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found		
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required		
OM106	Digouts	m2	N/A	N/A	N/A	N/A									
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A									
Other activities															
OM200 Shoulder		Lm													
OM201	Unsealed Shoulder	No													
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required		
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Defects rectified within stipulated time.		
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found		
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required		
	Other Activite (Raincut)		3%	1%	2%	Nil							Defects rectified within stipulated time.		
OM 300 Drainage including culverts major															
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required		

14.03.1015

