

कार्यपालक अभियन्ता का कार्यालय

Mobile No- 8986915814

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Email ID- cerwdwd2bettiah@gmail.com

पत्रांक- 1837 (अनु०) / नरकटियागंज, दिनांक- 08/10/2023

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह— सचिव नोडल पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।

विषय:-

MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maint. Policy-2018) योजना अन्तर्गत 5 (पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के लिए सूची बनाकर इस पत्र में संलग्न कर अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु०:- 1. अधियाचना पत्र।

विश्वासभाजन,



कार्यपालक अभियन्ता,

या०का०वि०, का०प्र०, नरकटियागंज।

08/10/2023

Requisition Format for Scheme Head - 5 Year Maintenance of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl No	Package No.	Name of Road	Project ID as per MIS	Administrative Section Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Current Maintenance Demand (In Lac)				Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)				1st Qtr Maint Demand	2nd Qtr Maint Demand	3rd Qtr Maint Demand	4th Qtr Maint Demand	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
1	RM/WE/NAR/19/0021	DONE CANAL - PARARIYA	31808902031	3628 27.08.2019	8.880	299.082	198.475	70.544	43/20-21 16.03.2020	15-03-2021	28-07-2021	3.52720	3.52720	0.00000	0.00000	
2	RM/WE/NAR/19/0021	NARKATIAGANJ SIKTA ROAD- BHARBHARWA	31808902124	3628 27.08.2019	2.250	96.669	89.313	17.825	43/20-21 16.03.2020	15-03-2021	26-03-2021	0.89127	0.89127	0.00000	0.00000	
3	RM/WE/NAR/19/0021	Similar to Bharrhwa	318891032205	3628 27.08.2019	1.580	76.610	56.403	12.744	43/20-21 16.03.2020	15-03-2021	12-03-2021	0.63721	0.63721	0.00000	0.00000	

[Signature]
7/10/23
HE

[Signature]
Executive Engineer
Rural Works Department
Work Division Narkatiaganj
07/10/2023

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD, Works Division, Narkatiaganj

1st Quarter

1	Name of the Road	DONE CANAL - PARARIYA		
2	Batch No.	RM/WE/NAR/19/0021		
3	Project ID	31808902031		
4	Total Lenth of Road (in KM)	8.880		
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	8.880		
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	70.54406		
8	Quarterly Payment : 4/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	3.5272030		
Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non- Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				3.5272030

Date of inspection by E/I or his agent

Prepare by Contractor's self Control unit

M/s CHANDRA MOHAN OJHA

चन्द्र मोहन ओजा

PARTNER.

Date

Signature of person inspecting road

Name and Designation of person inspecting road

(Signature)

Certify by E/I [signature] Date

Executive Engineer

Rural Works Department

Works Division, Narkatiaganj

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)													
RWD, Works Division, Narkatiaganj			1st Quarter										
Government Of Bihar QM01 Rural Works Department			SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT										
Road From:- DONE CANAL - PARARIYA Length of Road :8.88 KM Inspector :- A.E. RWD WORKS SUB DIVISION, Mainatanr			To:- Executive Engineer RWD, Works Division Narkatiaganj Position :- A.E.										
			Date:-										
No	standard Of Work Item Name	Unit	Unit Of Required in each Kilometer										Comments
			1	2	3	4	5	6	7	8	9	10	
OM100	Sealed pavement												
OM101	Pothole Patching	m ²	NIL	NIL	NIL								No pothole found
OM102	Surface Depression and Rut patching	m ²	NIL	NIL	NIL								No Surface Depression and Rut patching found
OM103	Crack Sealing	Lm	NIL	NIL	NIL								No crack
	Surface Treatment		NIL	NIL	NIL								Not required
OM104	(a) Loss of Aggregate (Surface Raveling)	m ³	NIL	NIL	NIL								No Loss of Aggregate (Surface raveling) found
	(b) Bleeding / Flushing	m ²	NIL	NIL	NIL								No bleeding / flushing found
	(c) Crocodile Cracking	m ²	NIL	NIL	NIL								No Crocodile cracking found
OM105	Edge Repair	m ²	NIL	NIL	NIL								Notified & repaired
OM106	Digouts	m ²	N.A.	N.A.	N.A.								
OM107	Concrete pavement	m ³	N.A.	N.A.	N.A.								
	Other activities												
OM200	Shoulder												
	Unsealed Shoulder												
OM201	(a) Edge Drop-off	Lm	NIL	NIL	NIL								No Edge Drop off found
	(b) Roughness, Scouring or Potholes	Lm	NIL	NIL	NIL								No Roughness, Scouring or Potholes found
	(c) Holding water	Lm	NIL	NIL	NIL								No Holding Water Found
OM202	Embankment Repair	M ³	NIL	NIL	NIL								Notified & repaired
	Other activities (Rain Cuts)		N.A.	N.A.	N.A.								
OM300	Drainage including culverts major												
OM301	Surface Drains & Verges	Lm	N.A.	N.A.	N.A.								NA
OM302	Culvert Cleaning	No	NIL	NIL	NIL								DONE
OM303	Culvert and pit Repair	M ³	NIL	NIL	NIL								DONE
	Other activities (White washing)	M ²	NIL	NIL	NIL								Not required

M/s CHANDRA MOHAN OJHA

चन्द्र मोहन ओझा

Contractor PARTNER.

Recd
मानक
J.E

Recd
07/10/23
A.E

Recd
07/10/23
E.E

No	standard Of Work Item Name	Work Unit	Unit Of Required in each Kilometers										Comments
			1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	NIL	NIL	NIL								Done
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	NIL	NIL	NIL								Done
OM402	Trees and Shrub Management	No	NIL	NIL	NIL								Done
	Cutting Of Branches Of Trees	No	NIL	NIL	NIL								Done
	Cutting Of Shrubs From Road Way	No	NIL	NIL	NIL								Done
	Other activities (Trimming of Grass)	M ²	NIL	NIL	NIL								Done
OM500	Safety Signage and Road												Done
OM501	Signs Maintenance	No	NIL	NIL	NIL								Not Required
OM502	Guard Stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								N.A.
OM504	Road Marking	M ²	NIL	NIL	NIL								N.A.
	Other activities												Not Required

M/s CHANDRA MOHAN OJHA

चन्द्र मोहन ओजा

PARTNER.
Contractor

Received
7/10/23
J.E

Received
07/10/23
A.E

Executive Engineer
Rural works Department
Works Division, Narkatiaganj

Name of Road - DONE CANAL - PARARIYA (Sec-26)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
29/7/22	17:9:2	26	0.1	280	20.2	2800	2836	G	27.199075	84.612743	Normal
29/7/22	17:9:37	26	0.1	300	20.2	3000	3041	G	27.19857	84.61342	Normal
29/7/22	17:10:17	26	0.1	300	10.1	3000	3027	G	27.197948	84.614107	Normal
29/7/22	17:10:17	26	0.1	280	20.2	2800	2776	G	27.197403	84.61483	Normal
29/7/22	17:10:17	26	0.1	310	20.2	3100	3083	G	27.19708	84.61579	Normal
29/7/22	17:10:48	26	0.1	280	30.3	2800	2755	G	27.197103	84.61677	Normal
29/7/22	17:17:0	26	0.1	290	23.5	2900	2857	G	27.19764	84.617457	Normal
29/7/22	17:17:23	26	0.1	300	20.2	3000	2981	G	27.198555	84.617542	Normal
29/7/22	17:17:23	26	0.1	330	30.3	3300	3257	G	27.19927	84.617978	Normal
29/7/22	17:17:23	26	0.1	340	20.2	3400	3358	G	27.20008	84.618	Normal
29/7/22	17:17:58	26	0.1	310	30.3	3100	3062	G	27.200947	84.618568	Normal
29/7/22	17:17:0	26	0.1	330	30.3	3300	3347	G	27.201753	84.618502	Normal
29/7/22	17:17:0	26	0.1	270	30.3	2700	2674	G	27.202622	84.618753	Normal
29/7/22	17:17:0	26	0.1	270	30.3	2700	2747	G	27.203437	84.618753	Normal
29/7/22	17:17:32	26	0.1	240	23.5	2400	2368	G	27.20432	84.618787	Curve
29/7/22	17:17:32	26	0.1	300	30.3	3000	2960	G	27.204795	84.61946	Normal
29/7/22	17:13:0	26	0.1	240	30.3	2400	2449	G	27.205707	84.61941	Normal
29/7/22	17:13:8	26	0.1	230	30.3	2300	2347	G	27.206568	84.619377	Normal
29/7/22	17:13:8	26	0.1	290	30.3	2900	2857	G	27.20749	84.61946	Normal
29/7/22	17:13:8	26	0.1	310	30.3	3100	3143	G	27.208327	84.619292	Normal
29/7/22	17:13:43	26	0.1	290	30.3	2900	2857	G	27.208915	84.618618	Normal
29/7/22	17:14:0	26	0.1	270	20.2	2700	2653	G	27.20949	84.618147	Normal
29/7/22	17:14:0	26	0.1	230	20.2	2300	2347	G	27.21031	84.618568	Normal
29/7/22	17:14:18	26	0.1	290	30.3	2900	2939	G	27.211145	84.618838	Normal
29/7/22	17:14:18	26	0.1	320	30.3	3200	3245	G	27.211995	84.619192	Normal
29/7/22	17:14:18	26	0.1	300	30.3	3000	2977	G	27.212685	84.61978	Normal
29/7/22	17:15:0	26	0.1	260	30.3	2600	2645	G	27.213437	84.6201	Normal
29/7/22	17:15:0	26	0.1	250	23.5	2500	2477	G	27.214337	84.620318	Normal
29/7/22	17:33:22	26	0.1	260	20.2	2600	2627	G	27.215203	84.620522	Normal
29/7/22	17:33:22	26	0.1	300	30.3	3000	2959	G	27.215982	84.620975	Normal
29/7/22	17:34:0	26	0.1	310	20.2	3100	3075	G	27.216587	84.621648	Normal

Road
29/7/22

Done
7/10/23

Handwritten signature

Name of Road - DONE CANAL - PARARIYA (Sec-26)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
29/7/22	17:34:0	26	0.1	260	30.3	2600	2636	G	27.217263	84.622305	Normal
29/7/22	17:34:0	26	0.1	300	30.3	3000	2976	G	27.217987	84.622793	Normal
29/7/22	17:34:33	26	0.1	300	30.3	3000	2977	G	27.21882	84.622677	Normal
29/7/22	17:34:33	26	0.1	310	30.3	3100	3066	G	27.219703	84.62244	Normal
29/7/22	17:35:0	26	0.1	310	23.5	3100	3074	G	27.220523	84.622625	Curve
29/7/22	17:35:9	26	0.1	300	23.5	3000	3046	G	27.221352	84.622357	Normal
29/7/22	17:35:9	26	0.1	330	23.5	3300	3327	G	27.222223	84.62234	Normal
29/7/22	17:35:9	26	0.1	320	23.5	3200	3227	G	27.223068	84.62244	Normal
29/7/22	17:35:9	26	0.1	330	23.5	3300	3276	G	27.224038	84.622625	Normal
29/7/22	17:36:9	26	0.1	340	23.5	3400	3366	G	27.224912	84.622793	Normal
29/7/22	17:36:9	26	0.1	310	0	3100	3053	G	27.225798	84.622793	Normal
29/7/22	17:36:9	26	0.1	300	20.2	3000	2957	G	27.226675	84.622978	Normal
29/7/22	17:37:9	26	0.1	300	20.2	3000	2958	G	27.227558	84.623265	Normal
29/7/22	17:37:9	26	0.1	330	10.1	3300	3328	G	27.22841	84.62345	Curve
29/7/22	17:37:9	26	0.1	300	10.1	3000	2974	G	27.22848	84.62436	Normal
29/7/22	17:37:9	26	0.1	300	20.2	3000	2966	G	27.228527	84.625353	Normal
29/7/22	17:38:1	26	0.1	280	20.2	2800	2766	G	27.228488	84.626363	Normal
29/7/22	17:38:1	26	0.1	290	20.2	2900	2853	G	27.228358	84.627373	Curve
29/7/22	17:38:1	26	0.1	290	20.2	2900	2924	G	27.229173	84.627608	Normal
29/7/22	17:39:3	26	0.1	300	20.2	3000	2973	G	27.229978	84.627962	Normal
29/7/22	17:39:3	26	0.1	290	20.2	2900	2925	G	27.23086	84.628232	Normal
29/7/22	17:39:3	26	0.1	300	20.2	3000	2958	G	27.23164	84.628703	Normal
29/7/22	17:39:3	26	0.1	300	20.2	3000	2966	G	27.23248	84.62909	Normal
29/7/22	17:25:29	26	0.1	340	20.2	3400	3357	G	27.233288	84.629477	Normal
29/7/22	17:26:0	26	0.1	340	20.2	3400	3430	G	27.23404	84.629848	Normal
29/7/22	17:26:4	26	0.1	320	20.2	3200	3166	G	27.234843	84.630285	Normal
29/7/22	17:26:4	26	0.1	280	20.2	2800	2838	G	27.235578	84.630892	Normal
29/7/22	17:26:39	26	0.1	290	20.3	2900	2940	G	27.236127	84.631565	Normal
29/7/22	17:26:39	26	0.1	280	21.2	2800	2819	G	27.236843	84.632305	Normal
29/7/22	17:26:39	26	0.1	300	21.3	3000	3009	G	27.237445	84.632895	Normal
29/7/22	17:34:26	26	0.1	310		3100	3064	G	27.238015	84.633652	Curve

Revised
21/10/23

Revised
21/10/23
AC

Name of Road - DONE CANAL - PARARIYA (Sec-26)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
29/7/22	17:35:2	26	0.1	290	20.2	2900	2940	G	27.238862	84.634007	Normal
29/7/22	17:35:2	26	0.1	290	20.2	2900	2940	G	27.239513	84.63345	Normal
29/7/22	17:35:2	26	0.1	310	20.2	3100	3145	G	27.240303	84.632928	Curve
29/7/22	17:35:37	26	0.1	340	30.3	3400	3430	G	27.24119	84.633097	Curve
29/7/22	17:35:37	26	0.1	280	30.3	2800	2757	G	27.2419	84.633585	Curve
29/7/22	17:36:0	26	0.1	260	30.3	2600	2553	G	27.242537	84.634343	Normal
29/7/22	17:36:17	26	0.1	250	23.5	2500	2451	G	27.243078	84.63513	Normal
29/7/22	17:36:17	26	0.1	300	23.5	3000	3043	G	27.243738	84.635823	Normal
29/7/22	17:36:17	26	0.1	250	23.5	2500	2532	G	27.24447	84.636328	Normal
29/7/22	17:36:17	26	0.1	240	30.3	2400	2430	G	27.24516	84.636952	Normal
29/7/22	17:36:47	26	0.1	290	30.3	2900	2940	G	27.245802	84.63749	Normal
29/7/22	17:37:0	26	0.1	320	30.3	3200	3226	G	27.246527	84.63808	Normal
29/7/22	17:37:0	26	0.1	290	30.3	2900	2940	G	27.247418	84.638	Normal
29/7/22	17:37:23	26	0.1	270	20.2	2700	2736	G	27.248178	84.638635	Normal
29/7/22	17:38:31	26	0.1	240	20.2	2400	2430	G	27.249012	84.639073	Normal
29/7/22	17:38:31	26	0.1	300	20.2	3000	3022	G	27.249827	84.639512	Curve
29/7/22	17:39:0	26	0.1	330	30.3	3300	3328	G	27.250232	84.638838	Normal
29/7/22	17:39:8	26	0.1	290	20.2	2900	2859	G	27.25054	84.637862	Normal
29/7/22	17:39:8	26	0.1	260	23.5	2600	2634	G	27.250922	84.636952	Normal
29/7/22	17:39:8	26	0.1	330	24.5	3300	3272	G	27.25158	84.636835	Normal
29/7/22	17:40:1	26	0.1	360	24.5	3600	3586	G	27.25223	84.637542	Normal
29/7/22	17:40:1	26	0.1	290	24.5	2900	2900	G	27.252363	84.63845	Normal
29/7/22	17:40:1	26	0.1	330	24.5	3300	3300	G	27.252713	84.639292	Normal
29/7/22	17:40:1	26	0.1	290	24.5	2900	2853	G	27.253537	84.639545	Normal
29/7/22	17:41:2	26	0.1	290	24.5	2900	2853	G	27.25443	84.639713	Curve
29/7/22	17:41:2	26	0.1	270	24.5	2700	2749	G	27.25519	84.639393	Normal
29/7/22	17:41:2	26	0.075	340	22.5	3400	3377	G	27.25602	84.639578	Normal
Average IRI Value=							2945				

Range
7/10/22
JE

Range
07/10/23
AE

[Signature]
Executive Engineer
Rural Works Department
Work Division, Narkatiyaganj

Name of Customer : M/S Chandra Mohan Ojha
 Name of Work/ Road : DONE CANAL - PARARIYA
 Lab Job number :
 Date : 29-Jul-22
 Section No. : 26


Test Date : 29-Jul-22 Road Name : DONE CANAL - PARARIYA
 Machine No : 402 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval :
 Weather : UV Range : 1347 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 9 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

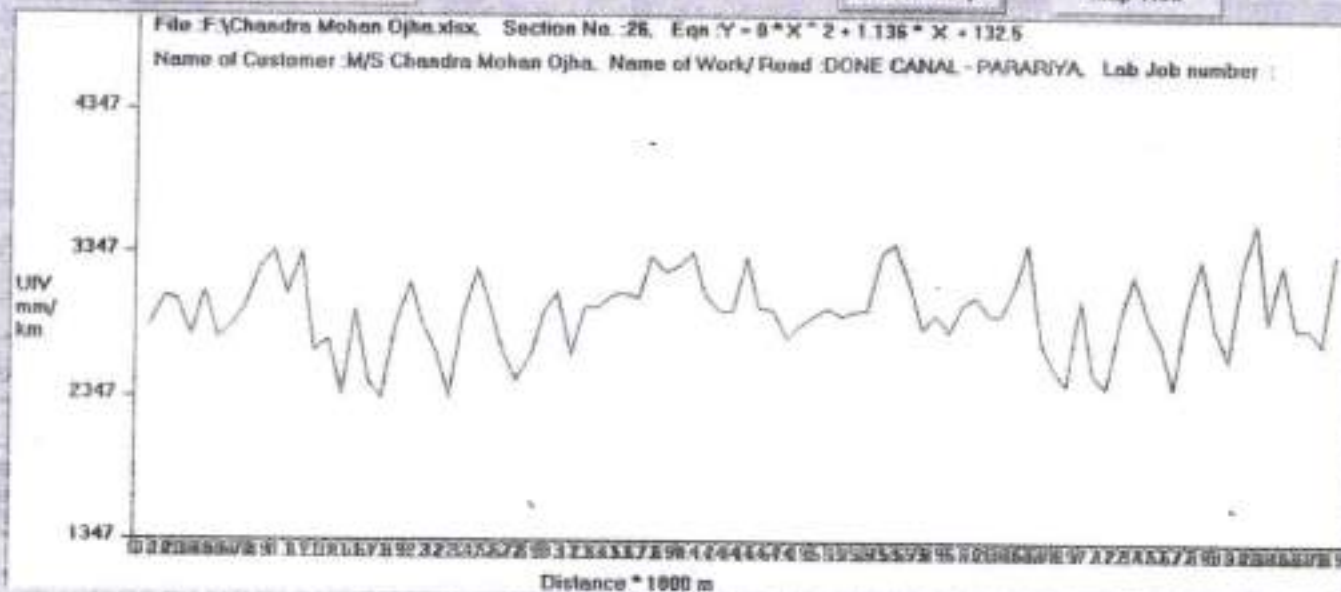

Executive Engineer
 Rural Works Department
 Work Division, Narkatiyaganj

Recd
 5/10/22
 JE

07/10/23
 AE

3/10/23
